



ANNUAL REPORT 2023-24

MONITORING & EVALUATION CELL

PLANNING & DEVELOPMENT DEPARTMENT

GOVERNMENT OF SINDH



ANNUAL REPORT 2023-24





MEC ANNUAL REPORT 2023-24 (CONTRIBUTORS)

APPROVING AUTHORITY

Chairman - P&D Board
Najam Ahmed Shah

REVIEWER

Director General - MEC
Nisar Ahmed Memon

EDITORIAL

Director (Monitoring) - MEC
Fatehdin Junejo

Director (MIS) - MEC
Sarfraz Ahmed Khan

Assistant Director
(Content Management) - MEC
Tufail Ahmed Shaikh

DISCLAIMER (MEC ANNUAL REPORT 2023-24)

We have made every effort to cross-check and verify the accuracy of the data provided. All statistics and information are accurate as of the financial year 2023-24. The status of the monitored schemes has been updated for this period and may change after defined period.

The analysis in this report focuses on the units monitored during F.Y 2023-24. Each development scheme, even if implemented in different geographical locations, are counted as separate units for monitoring purposes. Therefore, the term "scheme" is used interchangeably with "units," even when one scheme covers multiple units. Monitoring reports published during this period have been included accordingly. Some reports that were visited in previous years may be included in this year based on their publication date.

This report does not contain any references to third parties, neither does the report endorse any such third parties or their product / services nor the report sponsored, endorsed or associated with such third parties.

For any questions or feedback related to this report, please reach out through the MEC official platform.



info@mecsindh.gov.pk



www.mecsindh.gov.pk




+ 0092 (21) 99211927

+ 0092 (21) 99211418 (Ext-DG)



3rd Floor, Office of the Director
General – Monitoring &
Evaluation Cell, Tughluq
House, Sindh Secretariat,
Karachi.

MESSAGE

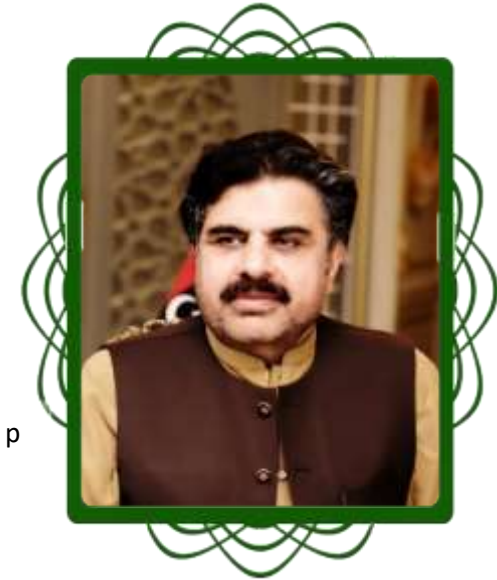

MINISTER, P&D BOARD

Over the past decade, the Province of Sindh has experienced rapid increase in urbanization and infrastructure development. In response, the Sindh Government has been dedicated to maintaining a consistent increase in the provincial development budget and ensuring its effective execution. This commitment aims to deliver the benefits of the development portfolio directly to the people of the province while fostering self-accountability through the Monitoring & Evaluation (M&E) of development projects at every stage.

The Planning & Development Department, Sindh has not only prioritized significant investments in public service delivery in areas such as education, health, food security, safe drinking water, sanitation, and resilient infrastructure for energy production, road networks, and water resources management, but has also ensured the proper implementation of these schemes through its Monitoring & Evaluation Cell (MEC).

The Monitoring and evaluation work as watch dog to essential quality management tools. It also keep a watch on progress of development schemes and raise an alert where interventions are required by the decision-making authorities. The Department serves as a key self-accountability mechanism implemented by the Sindh Government. It supports administrative departments by helping them adjust and improve their strategies, ensuring more effective, efficient, and impactful outcomes in their respective sectors through close monitoring of the provincial development portfolio.

This report highlights the importance of the Monitoring & Evaluation and it is encouraging to see the commitment of the P&D Department to ensuring that development funds are utilized efficiently and effectively to improve the living standards of the people of Sindh.

Syed Nasir Hussain Shah

MESSAGE



CHAIRMAN, P&D BOARD

The Planning & Development Board assists Administrative Departments by providing policy and procedural guidelines during the formulation of Annual Development Plans (ADP) and coordinates efforts in progress reporting and improvement of ADP schemes. The Monitoring & Evaluation Cell, established under the P&DD, is responsible for ensuring the proper execution of financial and physical progress of development schemes, offering timely interventions and adjustments for any projects that deviate from their planned objectives.

It is encouraging to observe that the MEC is evolving into an innovative and unconventional monitoring body, dedicated to maximizing the efficacy of the public sector development portfolio within the province. The primary role of the MEC is to proactively monitor the development portfolio, utilizing real-time reporting in a paperless environment to track key performance indicators and implement timely corrective measures.

This report consolidates information on the MEC's monitoring activities for the fiscal year 2023-24, showcasing the P&D Department's commitment to ensure that development funds are used effectively and efficiently to enhance the living standards of the people of the Sindh province.

The MEC officials possess the technical expertise necessary for a dynamic assessment and analysis of the financial and physical progress of a diverse range of projects. The MEC has markedly improved its monitoring and reporting processes through the ongoing integration of cutting-edge Information Communication Technology (ICT) systems. A notable advancement is the digitization of the ADP Budget Book Volume-V, which enables stakeholders, including the general public, to easily access and evaluate progress of the project and its quality.

I am confident that this vital organ of the P&D Board will continue to advance steadily by embracing modern monitoring and evaluation techniques and harnessing technological innovations. I envision the MEC evolving into a proactive and dynamic organization that substantially improves public service delivery, leading to enhanced outcomes and superior services for the public.

Najam Ahmed Shah

MESSAGE



DIRECTOR GENERAL (MEC)

Over the years, the Monitoring & Evaluation Cell (MEC) has worked diligently to evolve into a dynamic organization with robust monitoring and evaluation systems. The core mission of MEC is to oversee the progress of ongoing development schemes, ensuring the effective utilization of public sector funds and enhancing service delivery.

This report highlights unwavering commitment to excellence and showcases the collective achievements of the MEC. It underscores proactive approach to monitoring and evaluating a substantial portion of the Government of Sindh's development portfolio, including projects in remote and challenging areas.

The integration of data analytics has been pivotal in enhancing our Monitoring and Evaluation capabilities. These advancements have allowed for more accurate tracking of project progress and efficient management of resources.

These technological innovations collectively contribute to a more effective and transparent monitoring system, reinforcing our commitment to maximizing the impact of development initiatives.

During the F.Y. 2023-24, MEC addressed the special assignments to monitor the District ADP portfolio of various Districts comprising of 834 schemes assigned by the Interim Provincial Government along with its regular monitoring visit plans.

I extend my heartfelt appreciation and recognition to all regional field monitoring offices, the MIS Directorate, and all associated officers. Their steadfast dedication and renewed efforts have been instrumental in achieving the organization's goals and targets. Their contributions are vital to the successful execution of our monitoring and evaluation activities.

Lastly, the experience and knowledge of our Minister (Planning & Development Board) and Chairman (Planning & Development Board) Government of Sindh have been instrumental in guiding us through the challenges we faced in this Annual Report finalization.

I anticipate the output and outcome of MEC activities to become a model of excellence in service delivery.

Nisar Ahmed Memon

CREDITS

MEC ANNUAL REPORT 2023-2024

Director General (MEC)
Nisar Ahmed Memon

Director (Monitoring) - MEC
Fatehdin Junejo

Director (MIS) - MEC
Sarfraz Ahmed Khan

Assistant Director
(Content Management) - MEC
Tufail Ahmed Shaikh



Planning &
Development
Department



Monitoring &
Evaluation Cell

ACRONYM

ACS	Additional Chief Secretary
AD	Administrative Department
ADB	Asian Development Bank
ADP	Annual Development Plan
CD/CDA	Coastal Development Authority
CDWP	Central Development Working Party
CM	Chief Minister
CMS	Content Management System
DC	Deputy Commissioner
DDWP	District Development Working Party
DEV	Development
DG	Director General
DS	Deputy Secretary
EA	Executing Agency
FD	Finance Department
FiLMS	File Management System
FY	Fiscal Year
GIS	Geographic Information System
GoS	Government of Sindh
GPS	Global Positioning System
HR	Human Resource
IMP	Implementation
KMC	Karachi Metropolitan Corporation
M&E	Monitoring and Evaluation
MEC	Monitoring and Evaluation Cell
MEO/MO	Monitoring and Evaluation Officer
MIS	Management Information System
P&D	Planning and Development
PD	Project Director
PDWP	Provincial Development Working Party
PHED	Public Health Engineering Department
PM	Prime Minister
PMESI	Project Monitoring and Evaluation System Improved
PS	Personal Secretary
QR	Quick Response
RMEO/RMO	Regional Monitoring and Evaluation Officer
SBI	Sindh Board of Investment
SGACD	Services General Administration and Coordination
SGRRP	Sindh Growth and Rural Rehabilitation Program
SMEO/SMO	Sector Monitoring and Evaluation Officer
SMES	Schemes Management & Evaluation System
SMS	Short Messaging Service
TPM	Third Party Monitoring
XEN	Executive Engineer

EXECUTIVE SUMMARY

This report provides a comprehensive review and analysis of the activities and accomplishments of the Monitoring & Evaluation Cell (MEC), Planning & Development Department, Government of Sindh for the Fiscal Year 2023-24. The primary focus of this report is not only to gather and convey the field monitoring observations and status of the development schemes but also make recommendations for quality improvement.

The MEC has continuously improved and strengthened its Monitoring & Evaluation systems by procurement of the latest monitoring equipment. The MEC team ensures, an active feedback loop with the Administrative Departments and Executing Agencies, aiming to communicate, address and rectify issues identified during monitoring for enhanced performance in their respective development works. Ultimately, these course-correction measures contribute to amplifying the positive impact of the development schemes and projects. The results from monitoring and evaluation are also compared with the financial data provided by the Finance Department.

For the fiscal year 2023-24, the Provincial ADP of Sindh was comprised of total 5,256 development schemes, with 3,311 being ongoing and 1,945 new schemes. During the year, the total monitoring reports published by the MEC are 548 for total 486 provincial ADP schemes/units, out of which 321 (i.e. 66%) schemes/units were found satisfactory, while 165 (i.e. 34%) schemes/units were marked as unsatisfactory. The Administrative Departments responded to 81 (i.e. 37%) with compliance reports to address the issues identified in the unsatisfactory monitoring reports. Additionally, the MEC addressed the special assignments during F.Y 2023-24, MEC was specially assigned to monitor the District ADP portfolio of 05 Districts comprising of 834 schemes and Foreign Funded projects i.e. Competitive & livable City of Karachi (CLICK) & Sindh Flood Emergency Rehabilitation Project (SFERP) by the Interim Provincial Government.

In general, the majority of the schemes declared as satisfactory are executed as per the planning and projected scope, whereas, major reasons for the unsatisfactory reports are deviation from the scope due to premature planning, in-appropriate execution, unnecessary delays in completion of the scheme, compromised quality, change of scheme location, poor workmanship and supervision.

In way forward, keeping in view the overall assessment of the MEC, it is highly recommended that in order to maintain proper quality and achieve results of the schemes, parameters of proper quality management as per PMI (Project Management Institute) may be adopted especially proper scope analysis, survey and detailed planning are pre-requisites before execution & monitoring to achieve the desired results and decline in the number of unsatisfactory schemes.

SALIENT FEATURES




Table of Contents

01 Organizational Overview

Vision, Mission, Values and Functions

Monitoring Dashboard (Work Flow)

Mobilization of Drones

MEC Monitoring Plan

15 Development Overview

Prioritized Department-Wise Release Position

Key Monitoring Indicators for Prioritized Departments

09 ADP Portfolio

5-Year Trend Analysis of Provincial ADP Allocations

Department-Wise ADP Allocations

27 Key Performance Indicators

Overall Status of Monitoring Visits and Schemes

Department-Wise Monitoring Visits

Department-Wise Status of Schemes Monitored

Regional Monitoring Visits

5-Year Trend Analysis of Monitoring Visits

Key Result Indicators **37**

Department-Wise Compliance Status of Monitored Schemes

5-Year Trend Analysis of the Status of Monitored Schemes

Monitoring Revisits Outcomes

Unsatisfactory Schemes Visits

Summary of Completed Schemes

Special Assignment

Establishment of District ADP Cell

Third Party Monitoring

Way Forward **69**

MEC's Monitoring Plan for FY 2023-24

53 Findings & Recommendations

Auqaf Department

Education Department

Forest & Wild Life Department

Irrigation & Lining of Main Canals Department

Health Department

Livestock & Fisheries Department

Local Government & Mega Schemes of Karachi

Public Health Engineering Department

Sports & Youth Affair Department

Works & Services Department

73 Annexures

Annexure (A)

Department Wise Schemes Monitored in FY 2023-24

Annexure (B)

List of Re-Visited Schemes in FY 2023-24

Annexure (C)

List of Completed Schemes in FY 2023-24

Annexure (D)

Assets Distribution Ceremony

Annexure (E)

MEC Offices & Team Members



OVERVIEW



ORGANIZATIONAL




Improve Public Sector Development Service Delivery Outcomes for Amplified Societal Impact




Ensuring rigorous monitoring and evaluation of public sector development schemes for improved service delivery with the following objectives

1. *To ensure that the Standards of Quality are maintained in development projects*
2. *To keep a regular track of the progress of schemes*
3. *To enable timely & informed decisions through efficient reporting*
4. *To promote and enhance institutional learning and knowledge through the instant availability of chronological indicators*
5. *To coordinate with various authorities for smooth and unhindered implementation*
6. *To Review and Evaluate the output & outcome of schemes*


CORE VALUES



FUNCTIONS

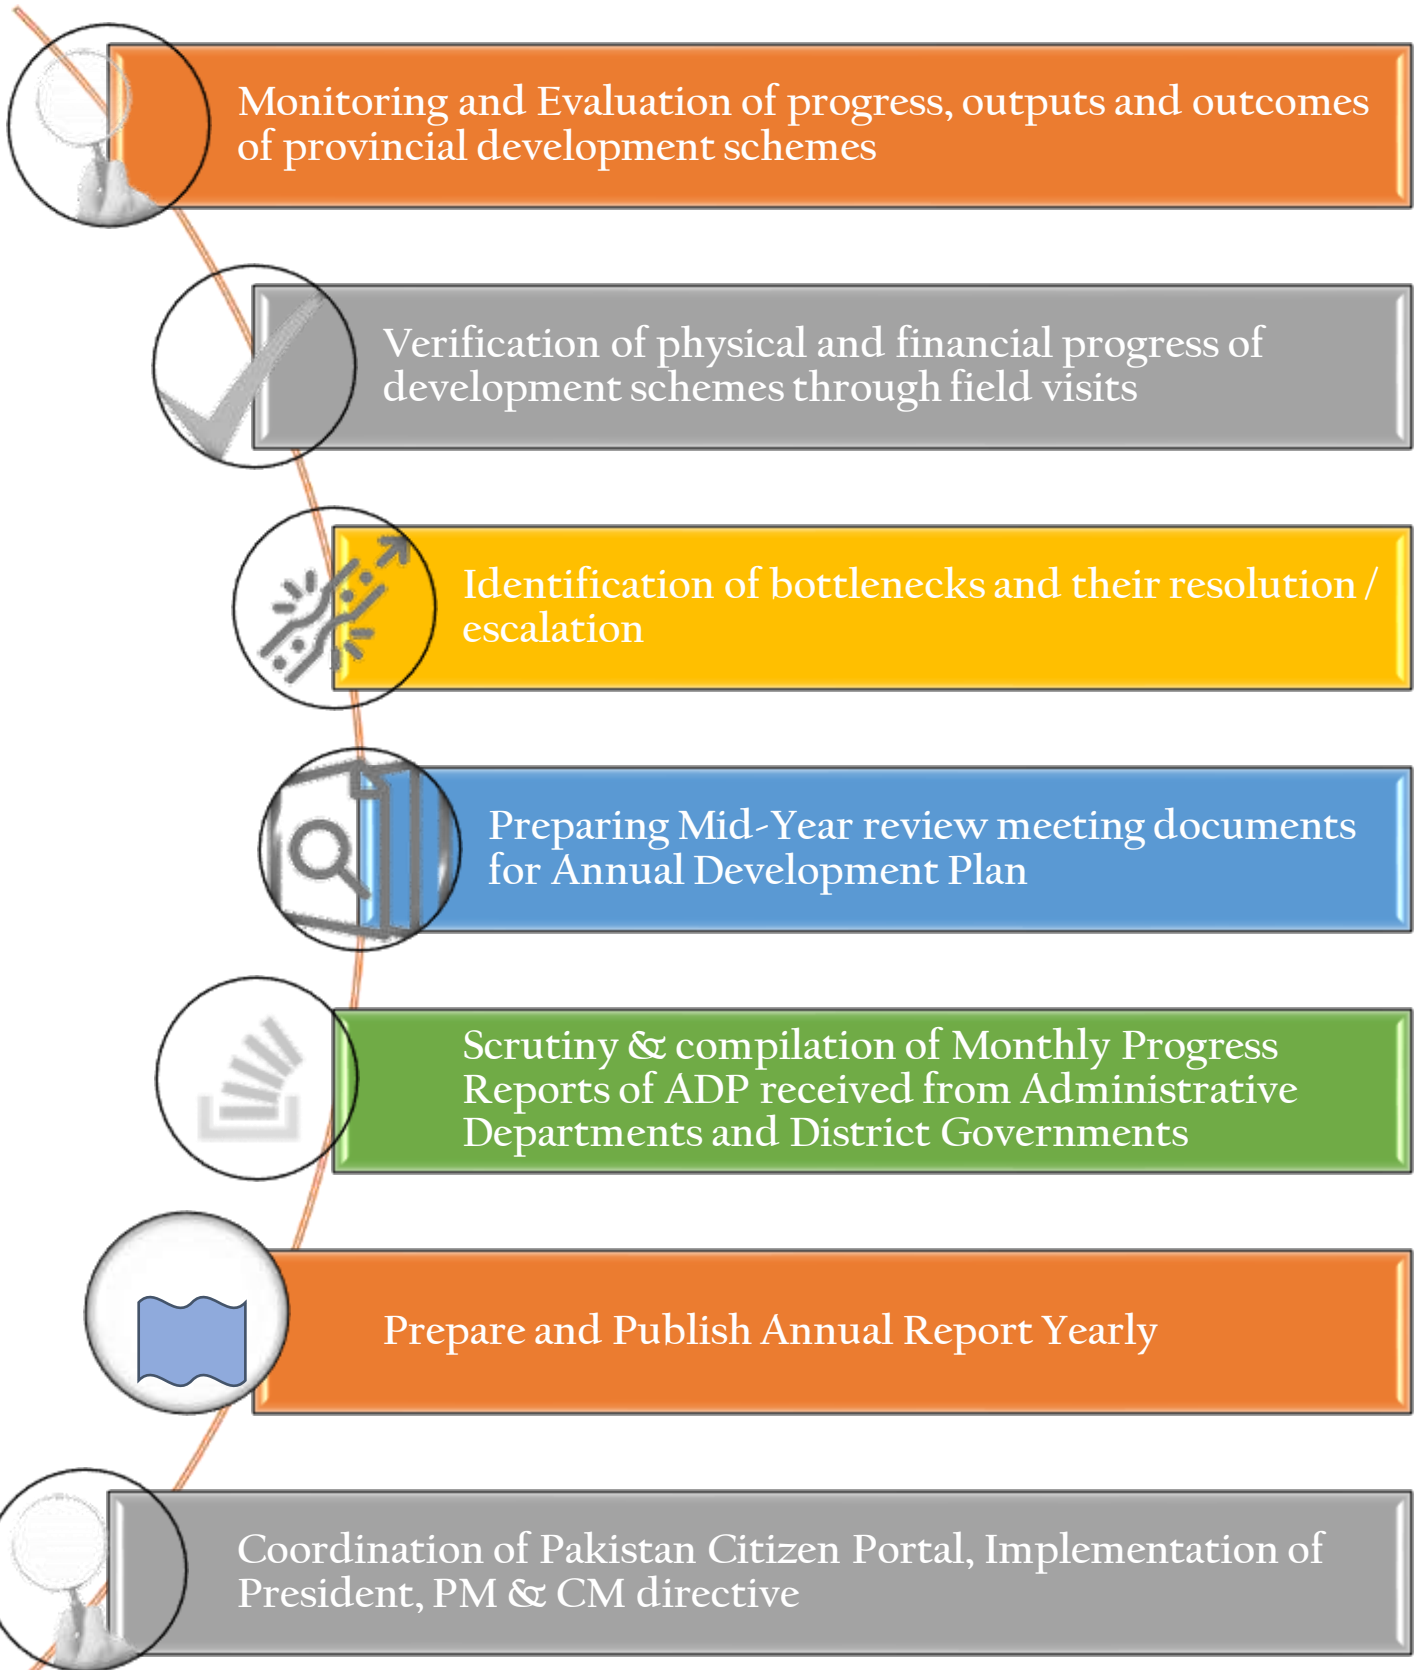

MONITORING DASHBOARD (WORKFLOW)

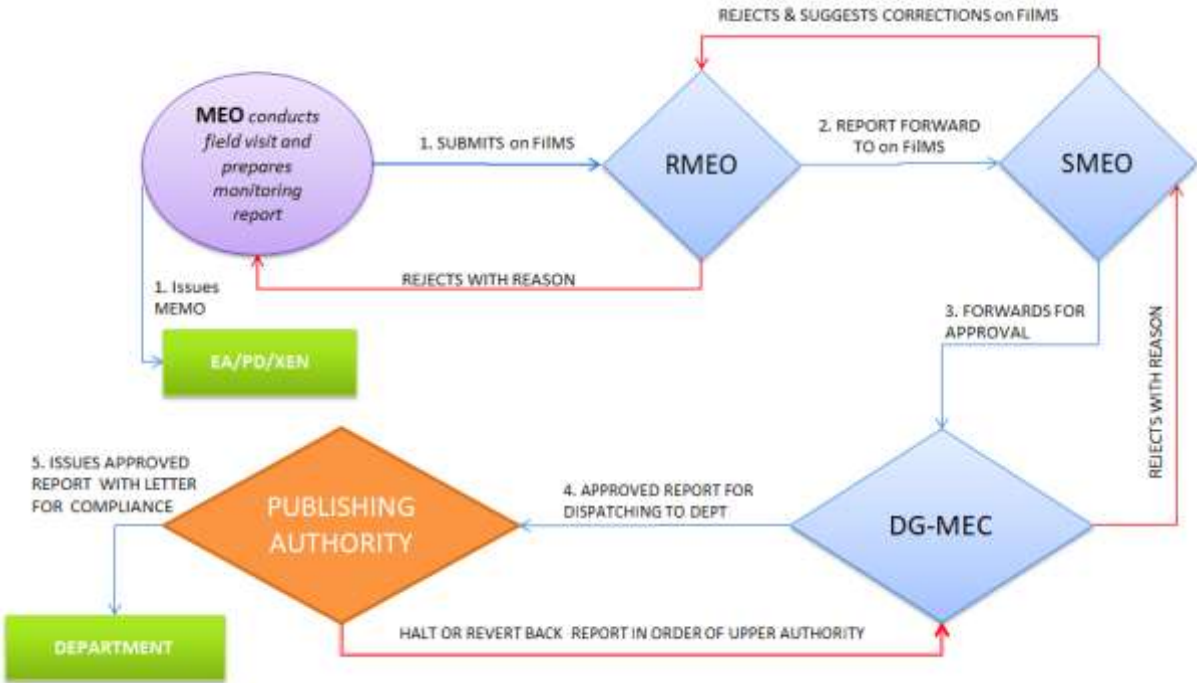

MEC has several quality filters to ensure that the automated and paperless monitoring system is transparent. File Management System (FilMS) is an indigenously-built bespoke system that ensures efficient monitoring, reporting, and evaluation of the development schemes.

The monitoring & Evaluation Officer (MEO) submits the report after the monitoring visit to the Regional Monitoring & Evaluation Officer (RMEO) who ensures that all the technical requirements pertaining to the monitoring visit are addressed. RMEO intimates the relevant Sector Monitoring & Evaluation Officer (SMEO) for validation of the report for the requisite compliance standards. SMEO then submits the validated reports to the Director-General for approval and issuance of a letter to the relevant Line Department for compliance vis-à-vis the monitoring report findings.

MOBILIZATION OF DRONES

Introduction of BIM and Drone Technology in M&E Cell Reporting

The M&E Cell has initiated a transformative approach by integrating cutting-edge technologies into its reporting and evaluation processes. Among the most notable developments is the adoption of **Building Information Modeling (BIM)**, an intelligent, 3D model-based tool that provides users with a comprehensive, digital representation of a facility's physical and functional characteristics. BIM's advanced capabilities will enhance the accuracy, efficiency, and transparency of monitoring, offering a clearer view of project progress and outcomes.

In parallel with BIM integration, M&E is also considering the introduction of **drone technology** to provide high-quality aerial imagery and videos. These drone videos would be uploaded to a dedicated cluster on **FilMS (File Management System)**, enabling seamless access to visual data for project stakeholders. This initiative will not only improve the monitoring of construction and infrastructure projects but also provide real-time, on-the-ground insights that traditional methods may not capture effectively.

By leveraging both BIM and drones, the M&E Cell aims to streamline data collection, improve reporting accuracy, and enhance the overall quality of project management.

The use of drones in construction offers numerous benefits, enhancing both the efficiency and safety of construction projects. Here are some of the key advantages accrued through their use:

- Improved Surveying and Mapping
- Enhanced Site Monitoring
- Improved Safety
- Cost Efficiency
- Increased Efficiency and Productivity
- Better Data Collection for Planning
- Environmental Monitoring
- Better Communication and Reporting
- Post-Construction Inspections
- Accessibility in Difficult Environments




MEC MONITORING PLAN



Routine Visits



LTBC/SI Visits



Compliance Visits

MEC is responsible for active monitoring and rigorous evaluation of ADP schemes executed by various departments working for the Government of Sindh. MEC's robust monitoring mechanism is manifested through its overall visit plan that comprises 25% routine visits, 25% visits to ADP schemes that are Likely to be Completed (LTBC)/Special Initiatives in the corresponding financial year, and 50% compliance visits to the schemes with previously unsatisfactory status.

The three main categories of monitoring visits include First Visits, Revisits, and Visits for Compliance. In simple terms, the MEC team visits a cohort of schemes every financial year out of which a subset of schemes is revisited.

It is worth mentioning that revisits are also done for schemes that are termed 'satisfactory' to ascertain if the satisfactory status of those schemes is maintained over time. For schemes that are termed 'unsatisfactory', the MEC team issues compliance notices to make sure that the issues are promptly rectified.

Once the Department submits para-wise replies to indicate compliance with the issues raised by the MEC team, the 'compliance' monitoring visit is conducted to ensure that the submitted replies have been implemented on the ground too. These quality filters ensure that the Departments guarantee timely compliance to improve the financial and physical progress of the ongoing ADP schemes.



ADPO

PORTFOLIO




FINANCIAL TREND ANALYSIS OF PROVINCIAL ADP

In the post-devolution context, Government of Sindh has been progressively increasing the size of its development portfolio to undertake a series of initiatives for the province. The focus of these initiatives has been to achieve a balanced growth of infrastructure, production and social sectors for equitable development.

ADP YEAR	ON-GOING SCHEMES	NEW SCHEMES	TOTAL SCHEMES	THROW-FORWARD	ALLOCATION	RELEASES	EXPENDITURE	UTILIZATION %
2019-20	1,853	852	2,705	606,227	208,000	117,350	81,516	69
2020-21	2,069	177	2,246	607,570	155,000	96,214	82,877	86
2021-22	1,645	1,670	3,315	740,771	222,500	171,208	152,824	89
2022-23	2,506	1652	4,158	893,054	332,165	219,912	208,135	95
2023-24	3,311	1945	5,256	1,095,784	385,500	264,253	248,747	94

The last 5-year period of Provincial ADP shows that quantum of total development schemes has increased from 2,705 in FY 2019-20 to 5,256 schemes in FY 2023-24. The size of Provincial ADP Portfolio has increased in terms of allocations from Rs. 208 billion in FY 2019-20 to about Rs. 385.5 billion in FY 2023-24. Throw-Forward as of June, 2019 was Rs. 606 billion, making the ratio of throw-forward to total allocation in FY 2019-20 equal to 2.9:1. Throw-Forward as of June, 2023 was Rs. 1,095.78 billion, making the ratio of throw-forward to total allocation in FY 2023-24 equal to 2.8:1.

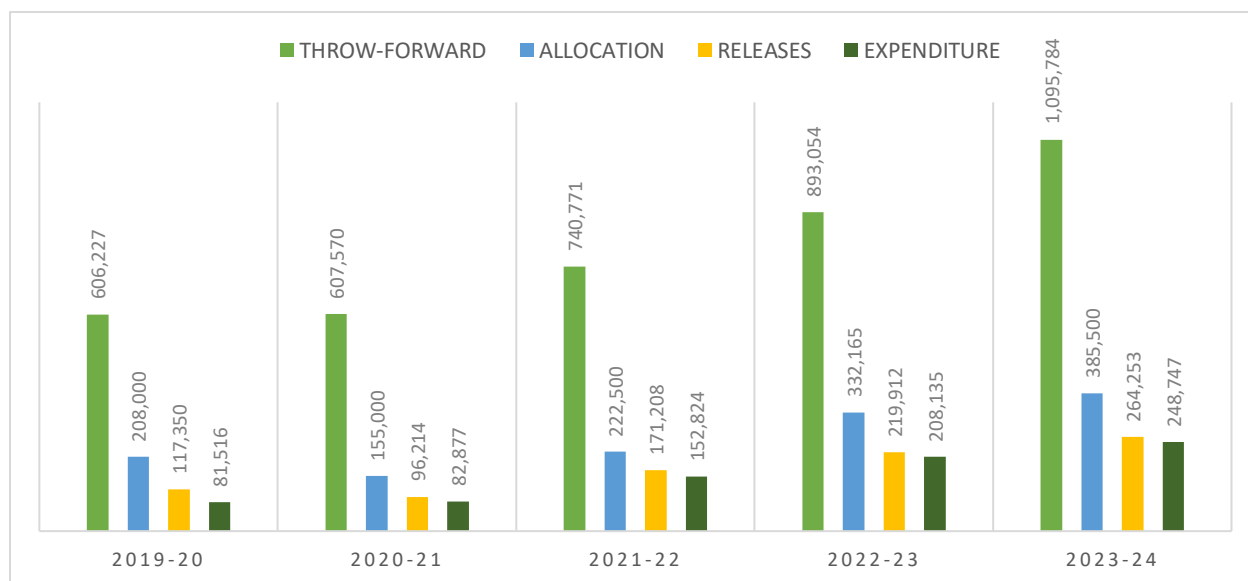

DEPARTMENT WISE ADP BUDGET ALLOCATION IN FY 2023-24


S.No	Department	Allocation (RS. Million)
1	AGRICULTURE	6,977
2	AUQAF, ZAKAT, USHR & R.A.	460
3	BOARD OF REVENUE	259
4	COOPERATIVE	20
5	CULTURE, TOUR., ANTIQ: & ARCH	2,867
6	EDUCATION SECTOR	34,690
7	ENERGY	2,128
8	ENVIRONMENT, C. C. & C.D.	1,002
9	EXCISE & TAXATION	140
10	FINANCE	1,175
11	FOOD	293
12	FOREST & WILDLIFE	2,049
13	GOVERNOR'S SECRETARIAT	83
14	HEALTH	19,739
15	HOME	11,517
16	HUMAN RIGHTS	138
17	HUMAN SETTLEMENT, SD&SH	69
18	INDUSTRIES & COMMERCE	1,503
19	INFORMATION	231
20	INFORMATION, SCI. & TECH	742
21	INVESTMENT	344
22	IRRIGATION	24,950
23	LABOUR & HUMAN RES:	138
24	LAW P.A. & PROSECUTION	1,280
25	LINING OF MAIN CANALS	10,000
26	LIVESTOCK & FISHERIES	2,435
27	LOCAL GOVERNMENT & HTP	62,631
28	MATCHING ALLOCATION	6,369
29	MEGA PROJECTS FOR KARACHI CITY	12,362
30	MINES & MINERAL DEV:	102
31	MINORITIES AFFAIRS	1,050
32	NEW DEVELOPMENT INITIATIVES	10,000
33	PLANNING & DEVELOPMENT	8,765
34	POPULATION WELFARE	350
35	PROVINCIAL ASSEMBLY	1,180
36	PROVINCIAL OMBUDSMAN	69
37	PUBLIC HEALTH ENGG: & RD	24,374
38	REHABILITATION (PDMA)	708
39	SGA&C	26,981
40	SINDH PUBLIC SERVICE COMM:	793
41	SINDH REVENUE BOARD	5
42	SOCIAL PROTECTION	892
43	SOCIAL WELFARE	762
44	SPORTS & YOUTH AFFAIRS	2,973
45	THAR COAL INFRASTR. DEV:	1,405
46	TRAINING MANAGEMENT & RES:	200
47	TRANSPORT & MASS TRANSIT	8,500
48	WOMEN DEVELOPMENT	300
49	WORKS & SERVICES	89,501

The size of Provincial ADP for FY 2023-24 was about Rs. 385 billion. The ADP portfolio comprised of 5,256 Schemes (3,311 Ongoing and 1,945 New Schemes). The overall development portfolio also included allocations of Rs. 30 billion for District ADP, Federal Grants of Rs. 53 billion and Foreign Project Assistance (FPA) of Rs. 267 billion. The total development outlay for FY 2023-24 amounted up to the tune of Rs. Rs. 735 billion.

In terms of ADP allocations, the priority departments are Works & Services, Local Government, Education, Public Health Engineering, Health, and Irrigation.

The Works & Services department has received the highest allocation in FY 2023-24 and was recorded at Rs. 89.5 billion out of the total ADP portfolio of Rs. 385.5 billion. This accounts for about 23% of the Total Provincial ADP outlay.

The prioritization of Local Government & HTP sector is also reflected in the Provincial ADP of FY 2023-24 with allocations of about Rs. 62.6 billion. This adds up to Rs. 152.1 billion which is almost 40% of the Provincial ADP portfolio. Earmarking significant allocations for priority sectors reflects the resolve and commitment of the provincial government towards balanced growth and equitable development of the province.

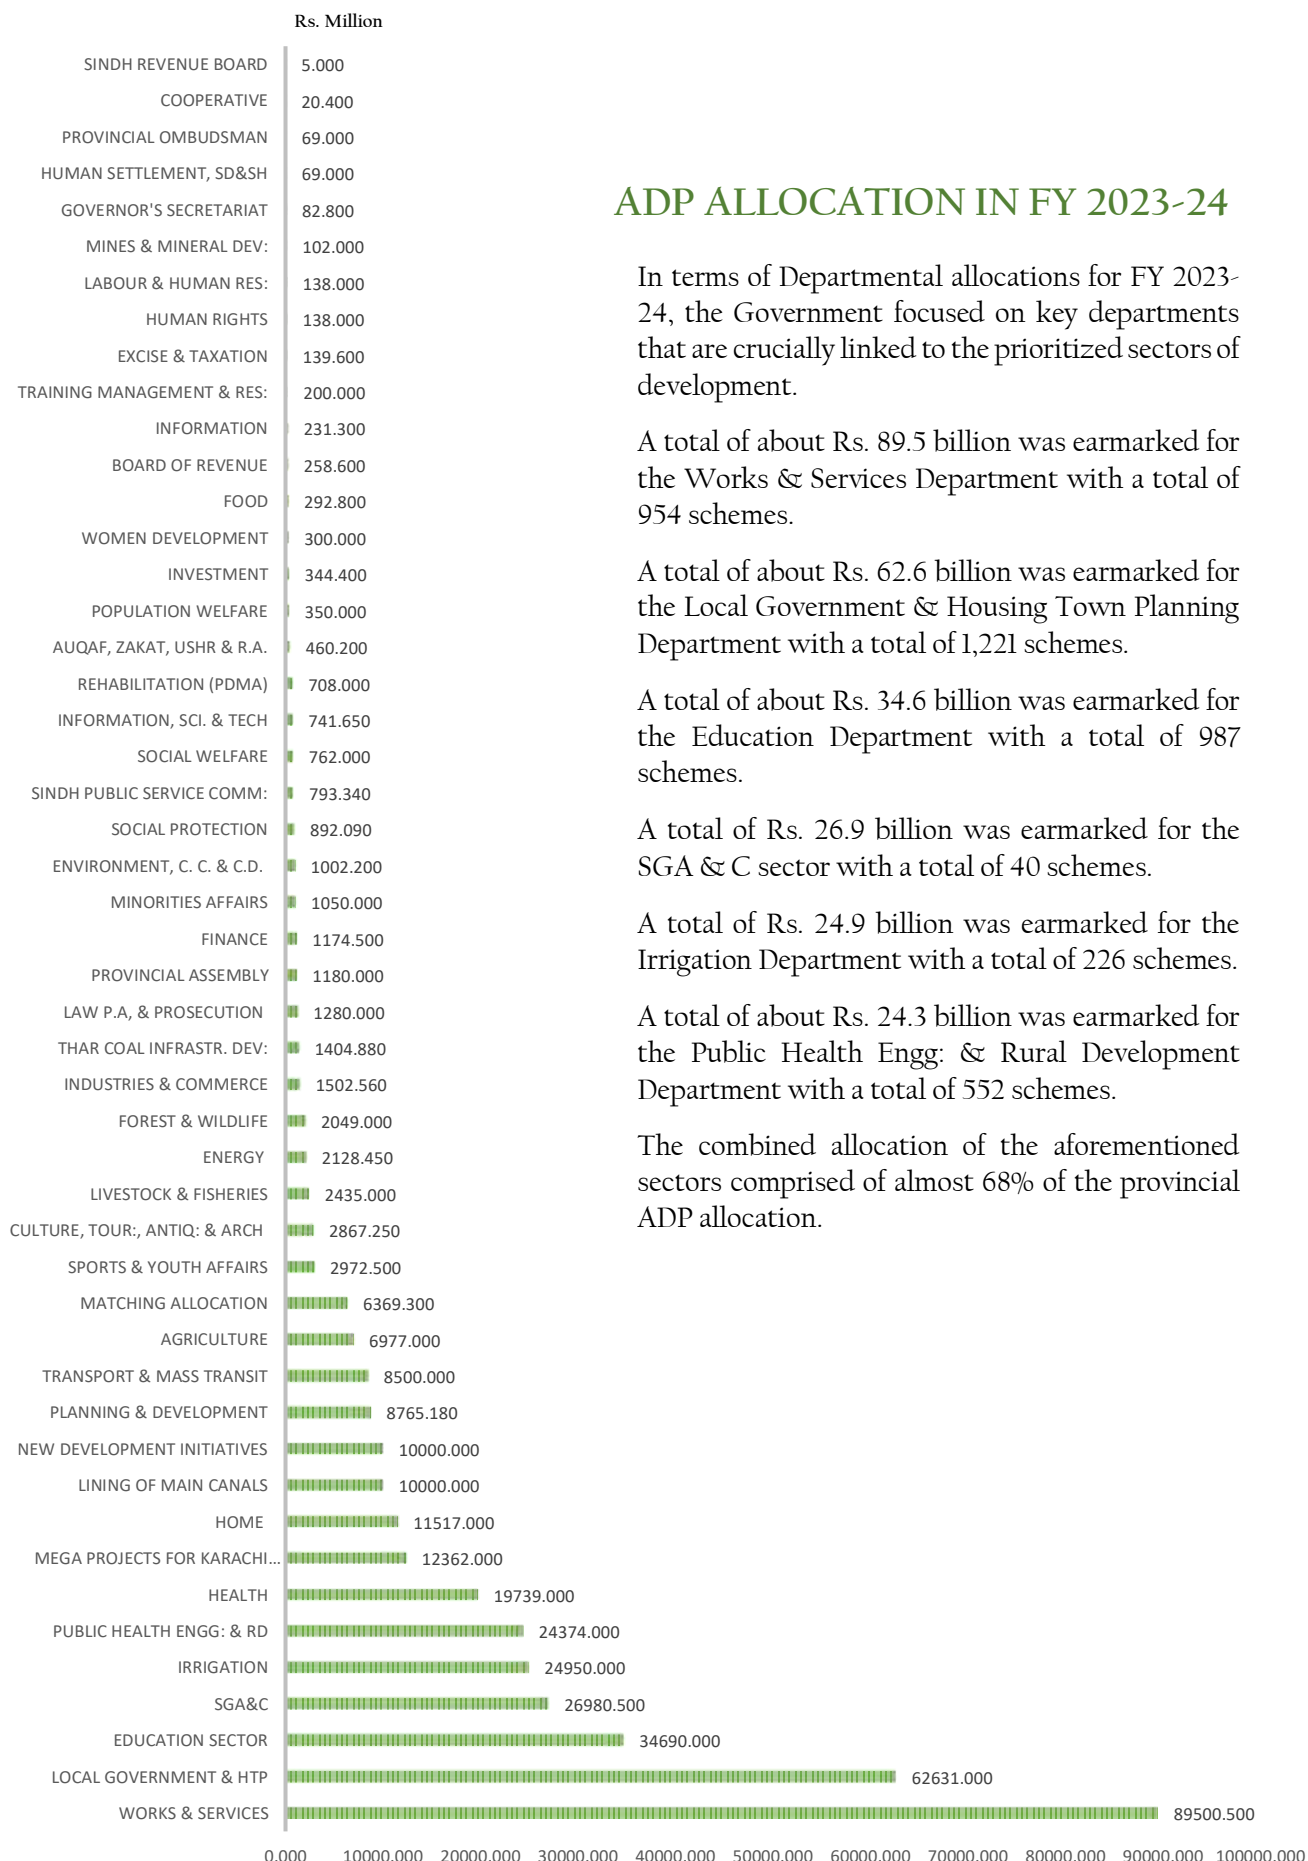

ADP ALLOCATION IN FY 2023-24

In terms of Departmental allocations for FY 2023-24, the Government focused on key departments that are crucially linked to the prioritized sectors of development.

A total of about Rs. 89.5 billion was earmarked for the Works & Services Department with a total of 954 schemes.

A total of about Rs. 62.6 billion was earmarked for the Local Government & Housing Town Planning Department with a total of 1,221 schemes.

A total of about Rs. 34.6 billion was earmarked for the Education Department with a total of 987 schemes.

A total of Rs. 26.9 billion was earmarked for the SGA & C sector with a total of 40 schemes.

A total of Rs. 24.9 billion was earmarked for the Irrigation Department with a total of 226 schemes.

A total of about Rs. 24.3 billion was earmarked for the Public Health Engg: & Rural Development Department with a total of 552 schemes.

The combined allocation of the aforementioned sectors comprised of almost 68% of the provincial ADP allocation.




OVERVIEW



DEVELOPMENT

AGRICULTURE

Agriculture is the backbone of the economy of Pakistan and Sindh contributes due share in agriculture sector of the country. The primary domain of the Agriculture, Supply & Prices Department of GoS is to transform Sindh's agriculture sector into a competitive, productive and sustainable segment of the economy with modern agricultural practices and technology. Throw-Forward for the department as of June, 2023 was Rs. 27,841 million with Rs. 6,977 million allocated FY 2023-24. This translates into a throw-forward to allocation ratio of 4.0:1. The Financial releases were Rs. 6,689 million of which Rs.6,604 million were utilized to complete the developmental schemes for the year. 05 schemes were monitored for the Agriculture Department with 05 monitoring visits.

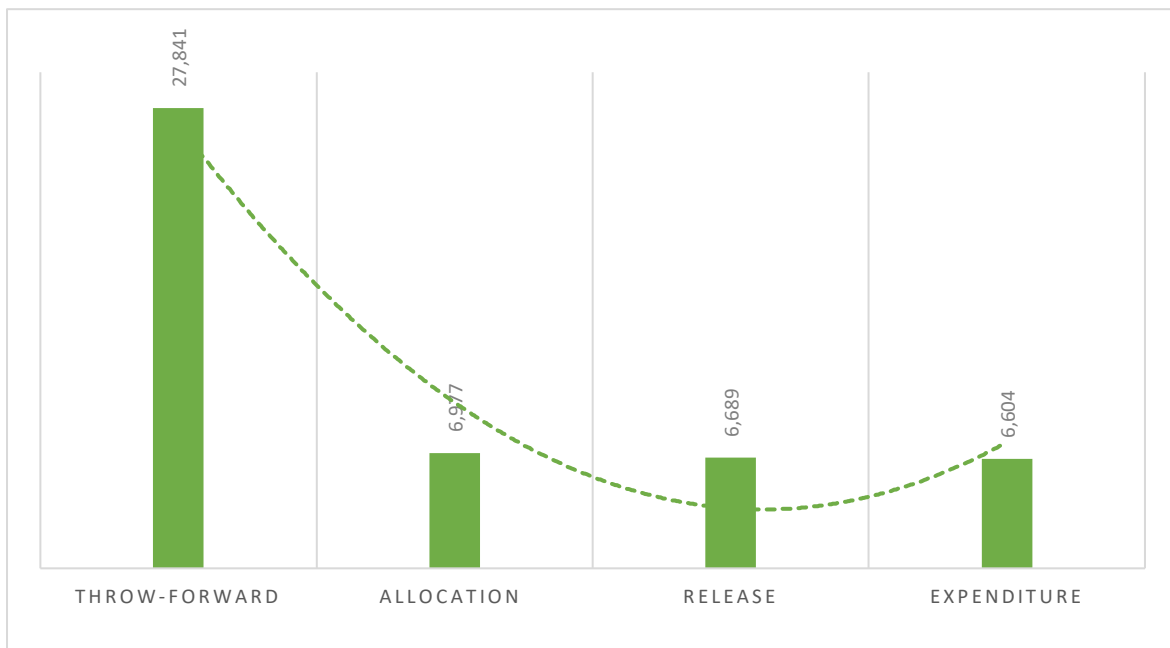

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

EDUCATION

Education is one of the priority sectors of the Government of Sindh comprising of 5 Administrative Departments i.e., School Education & literacy Department, College Education Department, Universities and Boards Department, Department of Empowerment of Persons with Disabilities (DEPD), and Sindh Technical Education & Vocational Training Authority (STEVTA). Throw-Forward for the department as of June, 2023 was Rs. 121,010 million with Rs. 34,690 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.5:1. The releases amounted to Rs. 16,440 million out of which an expenditure of Rs.14,977 million was incurred. 54 schemes of the Education Sector were monitored with 62 monitoring visits.

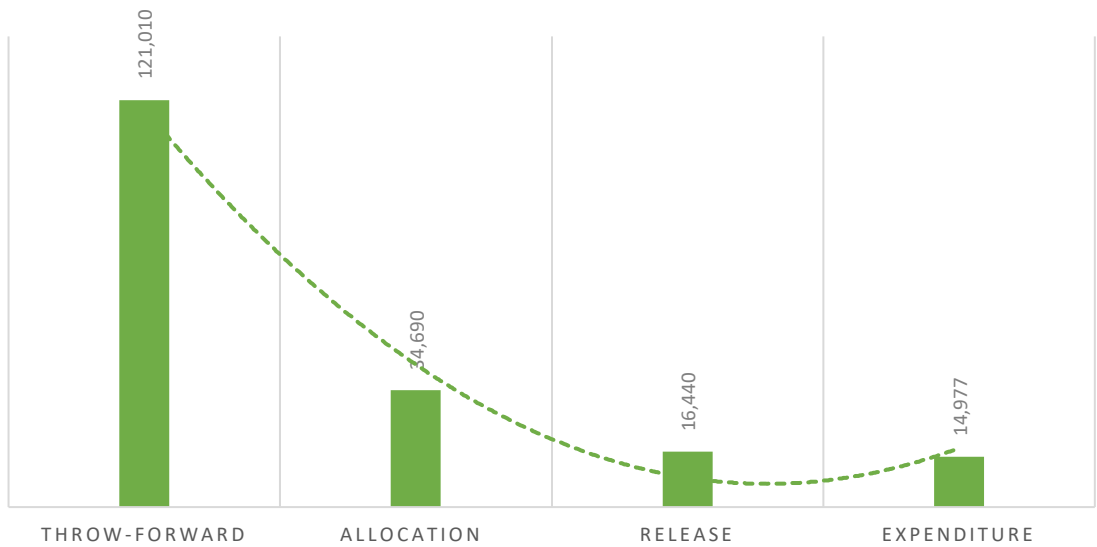

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

HEALTH

The Provincial Health department of GoS is responsible for ensuring quality healthcare services for the province with functions including administration, execution, legislation and regulation of the healthcare institutions. Throw-Forward for the department as of June, 2023 was Rs. 60,475 million with Rs. 19,739 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.1:1. The releases were Rs. 5,059 million of which the department was able to utilize Rs. 2,778 million in FY 2023-24. 32 schemes of the Health Department were monitored with 38 visits.

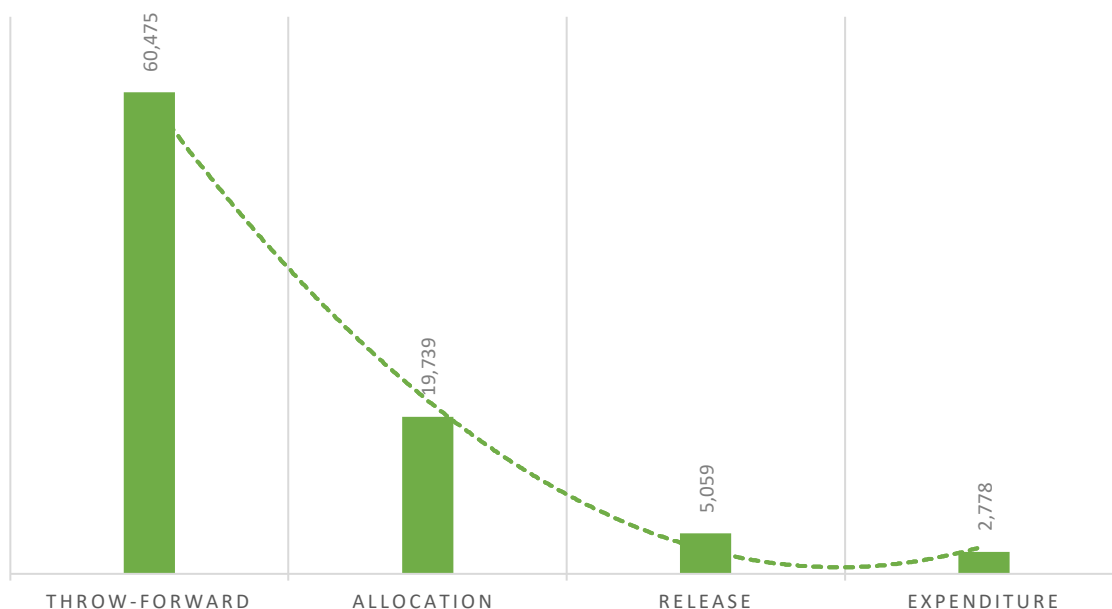

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

HOME

Home Department plays a pivotal role in maintenance of law & order and internal security. In addition, there is long list of traditional functions performed by the Department. The aforementioned role requires constant support from various attached departments which include Police Department, Inspectorate General of Prisons and Directorate of Civil Defense and Directorate of Reclamation & Probation. Throw-Forward for the department as of June, 2023 was Rs. 33,988 million with Rs. 11,517 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.0:1. The releases amounted to Rs. 8,128 million. The expenditures incurred were Rs. 7,681 million. 13 schemes of Home Department were monitored with 13 monitoring visits.

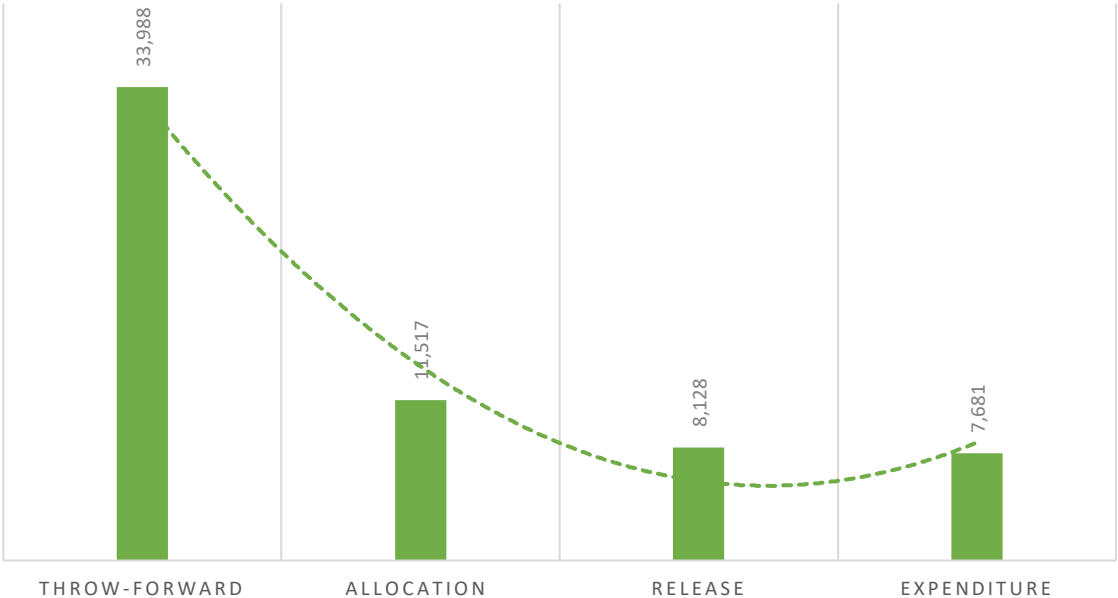

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

IRRIGATION

Irrigation Department is responsible for operations, maintenance, development & management of irrigation network, surface drainage system and tube-wells in addition to flood control and rain water harvesting. Throw-Forward for the department as of June, 2023 was Rs. 90,402 million with Rs. 24,950 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.6:1. The releases against which were Rs. 18,052 million. The department was able to utilize Rs.17,528 million during the year. 12 schemes of the Irrigation Department were monitored with 16 monitoring visits.

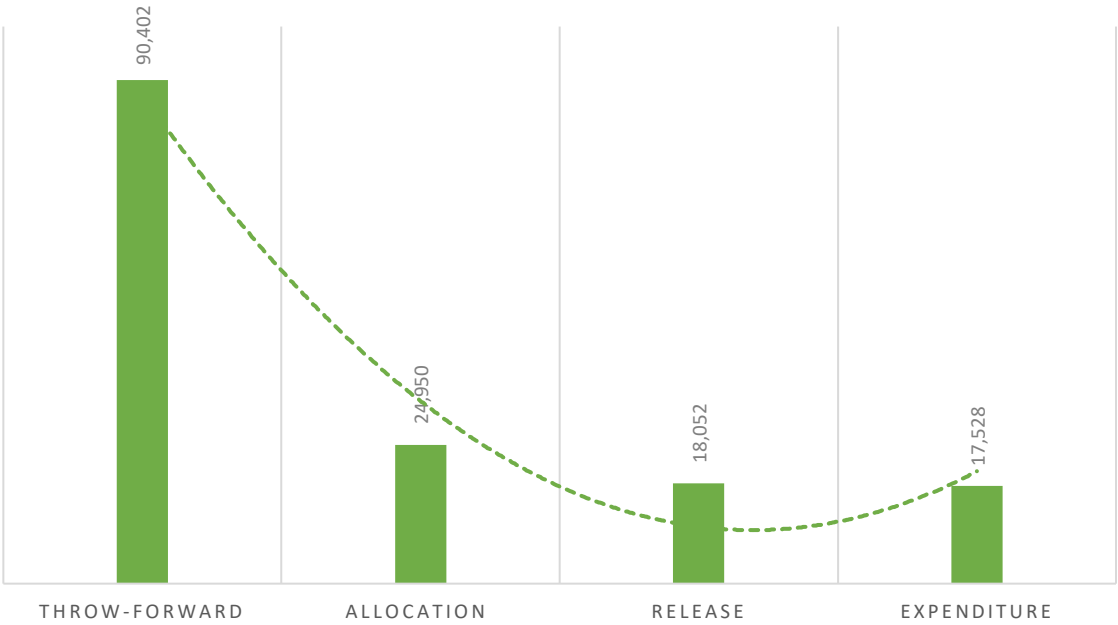

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

LAW, P.A. & PROSECUTION

The Law, Parliamentary Affairs & Criminal Prosecution department deals with legal matters pertaining to government business. Throw-Forward for the department as of June, 2023 was Rs. 5,497 million with Rs. 1,280 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 4.3:1. The releases amounted to Rs. 939 million out of which around Rs. 933 million were utilized. 02 schemes of Law, P.A. & Prosecution Department were monitored with 02 monitoring visits.

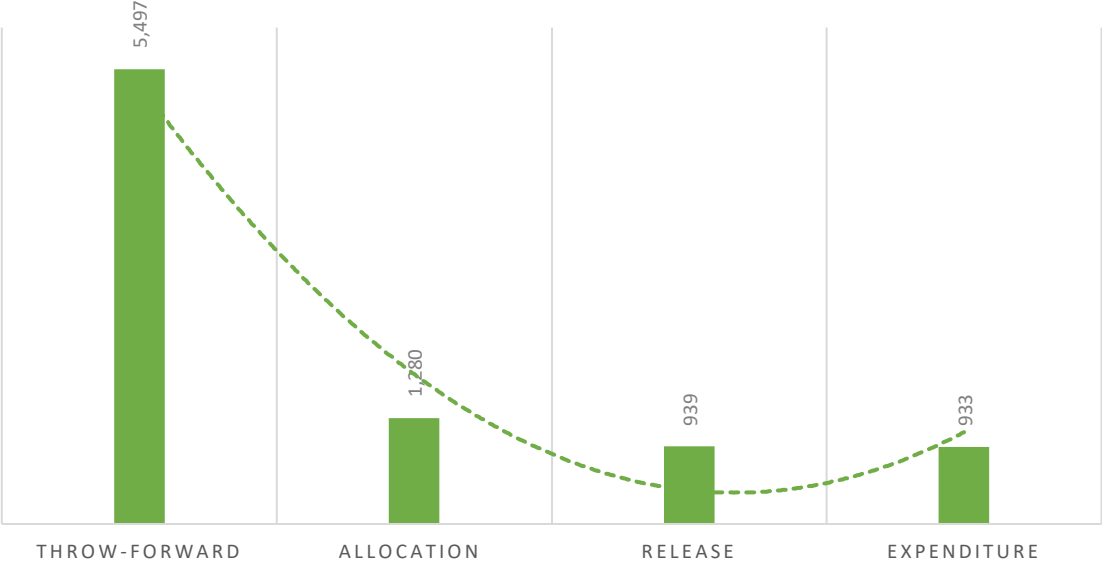


Monitoring Status



LIVESTOCK AND FISHERIES

Livestock & Fisheries Department caters to the requirements of livestock sector in the province. Livestock is increasingly becoming a very important sector of national economy, contributing even more than all the other agricultural crops combined. Throw-Forward for the department as of June, 2023 was Rs. 8,058 million with Rs. 2,435 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.3:1. The releases were Rs. 1,056 million. The expenditures incurred were Rs. 819 million. 11 schemes of Livestock & Fisheries Department were monitored with 13 monitoring visits.

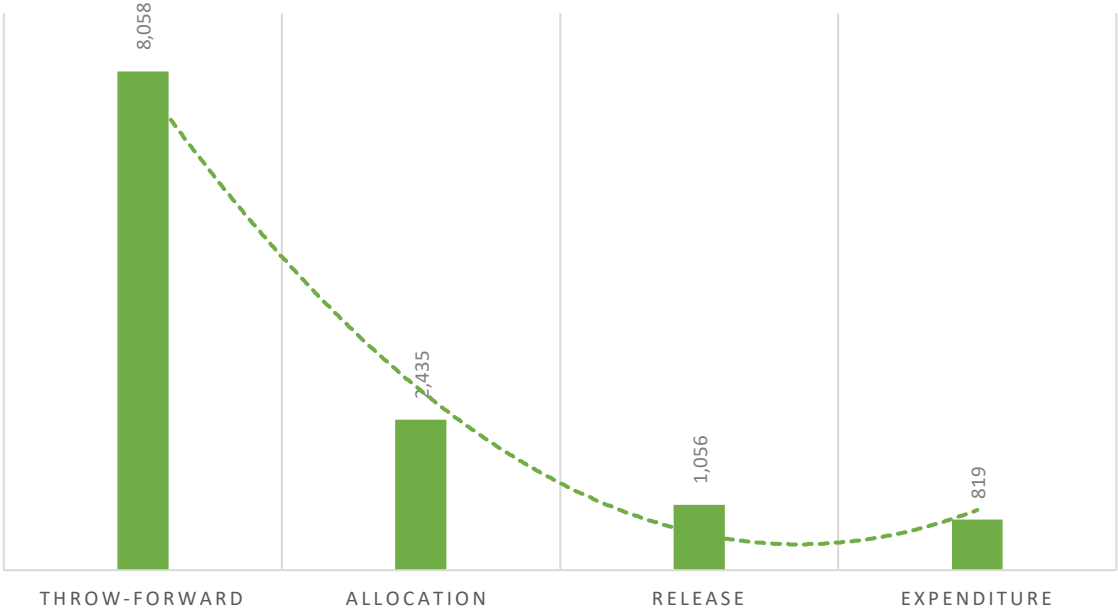


Monitoring Status



LOCAL GOVERNMENT

The Local Government department of GoS is responsible to promote good governance, effective delivery of services and transparent decision-making through institutionalized participation of the people at local level. Throw-Forward for the department as of June, 2023 was Rs. 192,595 million with Rs. 62,631 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 3.1:1. The releases were recorded at Rs.38,846 million out of which Rs. 35,729 million were utilized. 90 schemes of the Local Government Department were monitored with 103 monitoring visits.

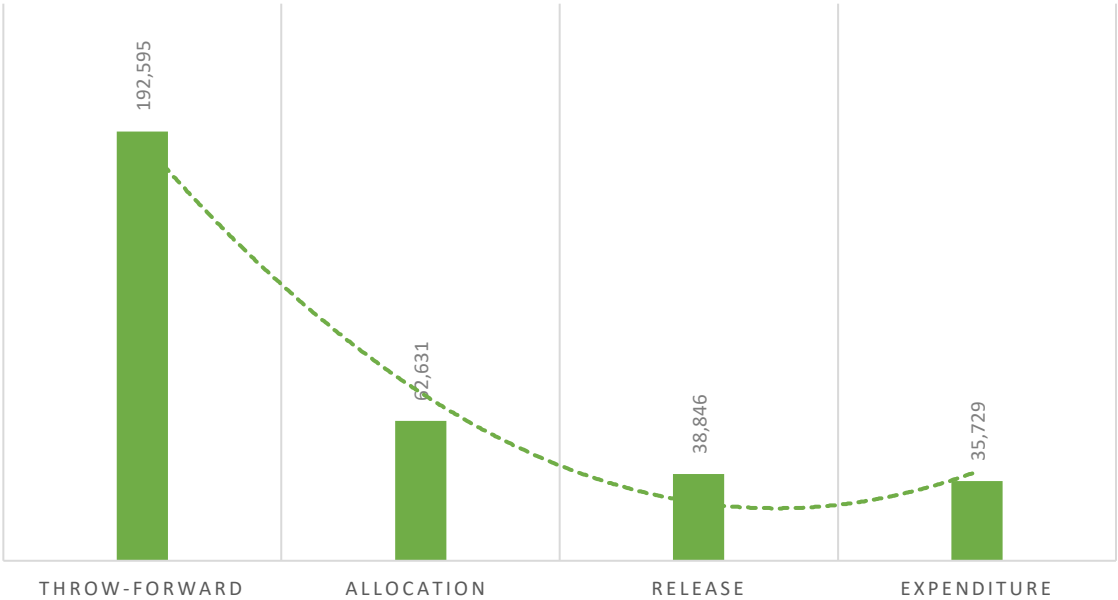

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

PUBLIC HEALTH ENGINEERING & RURAL DEVELOPMENT

The Public Health Engineering & Rural Development Department works on designing, planning and executing water supply and drainage schemes in urban and rural areas of Sindh. Throw-Forward for the department as of June, 2023 was Rs. 66,874 million with Rs. 24,374 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 2.7:1. The releases were recorded at Rs.16,955 million out of which Rs. 15,212 million were utilized. 69 schemes of PHE & RD Department were monitored with 72 monitoring visits.

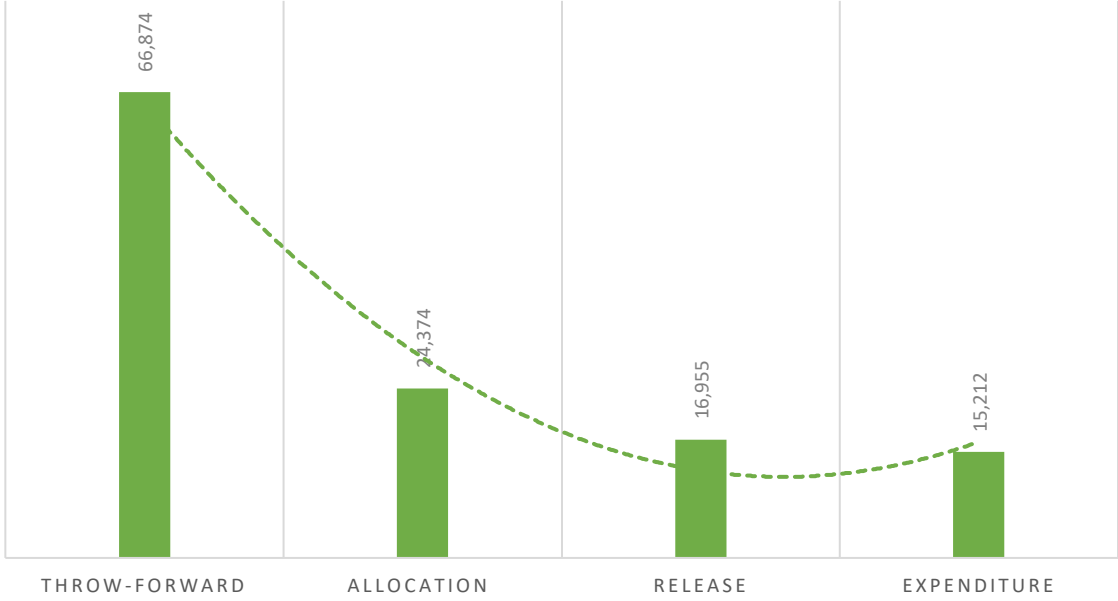

Monitoring Status



ADP Allocations
in billion Rupees




Schemes Monitored



Monitoring Visits

WORKS & SERVICES


Works & Services department is directly responsible for development initiatives that are concerned with development works such as roads, bridges and other related infrastructural initiatives of the province. Throw-Forward for the department as of June, 2023 was Rs. 180,723 million with Rs. 89,501 million allocated for FY 2023-24. This translates into a throw-forward to allocation ratio of 2.0:1. The financial releases were Rs. 82,655 million out of which the expenditures incurred were 79,773 million. 89 schemes of Works & Services Department were monitored with 92 monitoring visits.

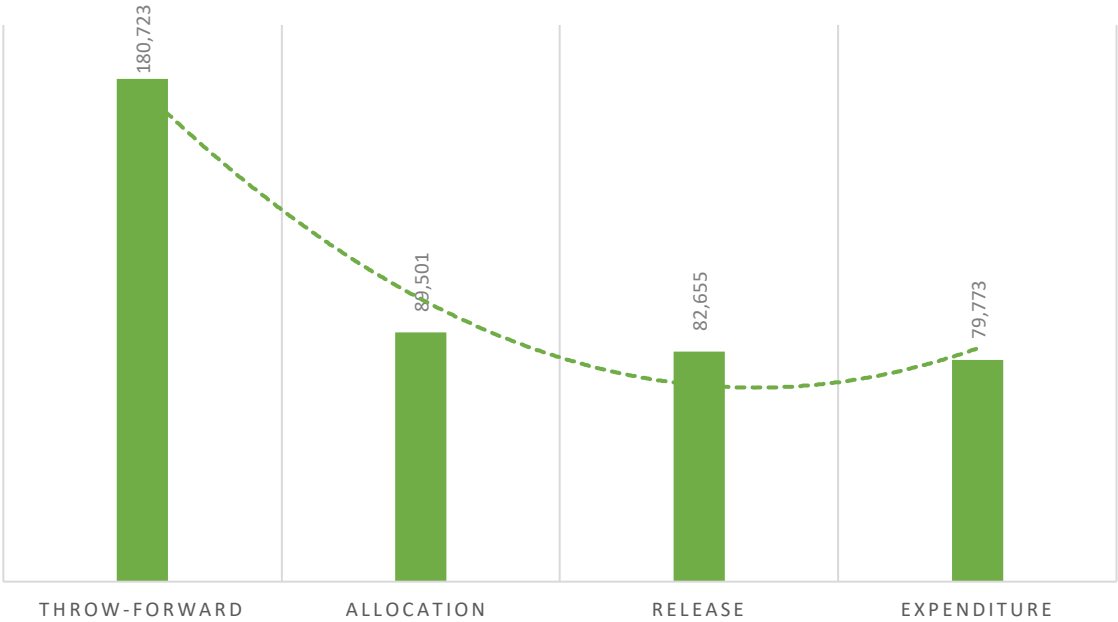

Monitoring Status



ADP Allocations
in billion Rupees



Schemes Monitored



Monitoring Visits



KEY



PERFORMANCE INDICATOR

MONITORING PROGRESS

MEC made a total of 548 field monitoring visits to the 486 schemes during FY 2023-24. This essentially meant revisiting several schemes to track monitoring during the execution phase, ensure compliance of unsatisfactory observations and improvement in the progress indicators. Out of the 548 visits, 327 visits were found satisfactory (60%) and 221 visits were found unsatisfactory (40%). Number of compliances received was 81 (37% of unsatisfactory visits).


Monitoring Visits Status



STATUS OF SCHEMES MONITORED

FY 2023-24

MEC Team monitored 486 schemes during FY 2023-24, out of which 321 schemes (66%) were found satisfactory and 165 schemes (34%) were found unsatisfactory.

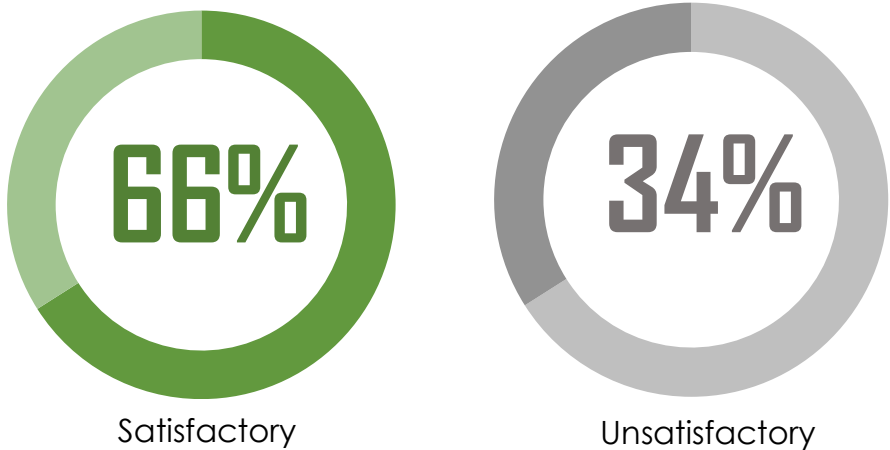

DEPARTMENT-WISE MONITORING VISITS IN FY 2023-24

S.#.	Departments / Sectors	Number of Visit	Satisfactory	Percentage	Un-Satisfactory	Percentage	Compliance Received	Percentage
1	Agriculture, GOS	5	1	20	4	80	1	25
2	Antiquities, GOS	1	0	0	1	100	0	0
3	Auqaf, GOS	11	5	45	6	55	1	17
4	Culture, GOS	7	4	57	3	43	0	0
5	Education and Literacy, GOS	62	34	55	28	45	12	43
6	Energy, GOS	6	3	50	3	50	3	100
7	Excise & Taxation, GOS	3	3	100	0	0	0	0
8	Food, GOS	1	0	0	1	100	0	0
9	Forest, Wildlife & CDA, GOS	11	7	64	4	36	0	0
10	Health, GOS	38	11	29	27	71	8	30
11	Home, GOS	13	12	92	1	8	0	0
12	Human Rights, GOS	2	0	0	2	100	2	100
13	Human Settlement, Spatial Development & Social Housing	1	0	0	1	100	0	0
14	Industrial & Commerce, GOS	3	1	33	2	67	1	50
15	Information & Archives, GOS	2	2	100	0	0	0	0
16	Irrigation (Water & Drainage), GOS	16	7	44	9	56	4	44
17	Labour Dept, GOS	1	1	100	0	0	0	0
18	Law P.A, & Prosecution	2	2	100	0	0	0	0
19	Lining of Main Canals	13	10	77	3	23	2	67
20	Livestock and Fisheries, GOS	13	8	62	5	38	4	80
21	Local Government, GOS	103	57	55	46	45	18	39
22	Mega Schemes for Karachi City	8	5	63	3	38	2	67
23	Minorities & Affairs, GOS	8	8	100	0	0	0	0
24	Planning & Development, GoS	4	1	25	3	75	2	67
25	Population Welfare, GOS	3	2	67	1	33	1	100
26	Provincial Ombudsman, GOS	2	1	50	1	50	1	100
27	Public Health Engineering, GOS	72	40	56	32	44	4	13
28	Rehabilitation (PDMA), GOS	3	3	100	0	0	0	0

S.#.	Departments / Sectors	Number of Visit	Satisfactory	Percentage	Un-Satisfactory	Percentage	Compliance Received	Percentage
29	S.G.A.and Coordination, GOS	3	0	0	3	100	2	67
30	Social Welfare, GOS	4	2	50	2	50	2	100
31	Special Education	1	1	100	0	0	0	0
32	Sports & Youth Affairs, GOS	23	19	83	4	17	3	75
33	STEVTA, GOS	1	1	100	0	0	0	0
34	Thar Coal Infrastructure Development	3	0	0	3	100	0	0
35	Transport & Comm. (Roads), GOS	1	0	0	1	100	1	100
36	Universities and Boards	2	1	50	1	50	1	100
37	Women Development, GOS	4	1	25	3	75	0	0
38	Work and Service, GOS	92	74	80	18	20	6	33
Total		548	327	60	221	40	81	37

In terms of the Line Departments with respect to monitoring, MEC focused on ten prioritized Departments which accounted for 82.5% (401 out of 486 schemes) of total schemes monitored and 81.2% (445 out of 548 visits) of the total monitoring visits (including fresh visits, re-visits and compliance visits)

The prioritized departments included Education and Literacy Department which is comprised of 54 schemes of Education during FY 2023-24 with 62 total monitoring visits. Out of 54 schemes, 33 (61%) were found to be satisfactory while 21 schemes (39%) were found unsatisfactory. Out of the 62 monitoring visits, 34 visits were satisfactory (55%) and 28 were unsatisfactory (45%).

MEC team monitored the schemes of Health Department comprised of 32 schemes monitored during FY 2023-24 with 38 total monitoring visits. Out of 32 schemes, 11 (34%) were found to be satisfactory and 21 schemes (66%) were found to be unsatisfactory. Out of the 38 monitoring visits, 11 visits were satisfactory (29%) and 27 were unsatisfactory (71%).

MEC monitored 13 schemes of Home Department during FY 2023-24 with 13 total monitoring visits. Out of 13 schemes, 12 (92%) were found to be satisfactory and 01 schemes (8%) found to be unsatisfactory. Out of the 13 monitoring visits, 12 visit were satisfactory (92%) and 01 were unsatisfactory (8%).

MEC visited 12 development schemes of Irrigation Department during FY 2023-24 with 16 total monitoring visits. Out of 12 schemes, 06 (50%) were found to be satisfactory and 06 schemes (50%) were found to be unsatisfactory. Out of the 16 monitoring visits, 07 visits were satisfactory (44%) and 09 were unsatisfactory (56%).

Visits to Lining of Main Canal Department comprised of 11 monitored schemes during FY 2023-24 with 13 total monitoring visits. Out of 11 schemes, 10 (91%) were found to be satisfactory and 01 schemes (9%) were found to be unsatisfactory. Out of the 13 monitoring visits, 10 visits were satisfactory (77%) and 03 were unsatisfactory (23%).

In case of Livestock & Fisheries Department visits comprised of 11 schemes monitored during FY 2023-24 with 13 total monitoring visits. Out of 11 schemes, 08 (73%) were found to be satisfactory and 03 schemes (27%) were found to be unsatisfactory. Out of the 13 monitoring visits, 08 visits were satisfactory (62%) and 05 were unsatisfactory (38%).

Monitoring of schemes of Local Government Department comprised of 90 monitored schemes during FY 2023-24 with 103 total monitoring visits. Out of 90 schemes, 56 (62%) were found to be satisfactory and 34 schemes (38%) were found to be unsatisfactory. Out of the 103 monitoring visits, 57 visits were satisfactory (55%) and 46 were unsatisfactory (45%).

MEC team's visit to the schemes of Public Health Engineering Department comprised of 69 schemes during FY 2023-24 with 72 total monitoring visits. Out of 69 schemes, 40 (58%) were found to be satisfactory and 29 schemes (42%) were found to be unsatisfactory. Out of the 72 monitoring visits, 40 visits were satisfactory (56%) and 32 were unsatisfactory (44%).

Monitoring visits to Sports & Youth Affairs Department comprised of 20 monitored schemes during FY 2023-24 with 23 total monitoring visits. Out of 20 schemes, 19 (95%) were found to be satisfactory and 01 schemes (5%) were found to be unsatisfactory. Out of the 23 monitoring visits, 19 visits were satisfactory (83%) and 04 were unsatisfactory (17%).

Visits to Works & Services Department comprised of 89 monitored schemes during FY 2023-24 with 92 total monitoring visits. Out of 89 schemes, 74 (83%) were found to be satisfactory and 15 schemes (17%) were found to be unsatisfactory. Out of the 92 monitoring visits, 74 visits were satisfactory (80%) and 18 were unsatisfactory (20%).

NUMBER OF SCHEMES MONITORED IN FY 2023-24

S.#.	Departments / Sectors	Number of Schemes Visited	Satisfactory	Percentage	Un-Satisfactory	Percentage
1	Agriculture, GOS	5	1	20.0	4	80.0
2	Auqaf, GOS	9	4	44.4	5	55.6
3	Antiquities, GOS	1	0	0.0	1	100.0
4	Culture, GOS	7	4	57.1	3	42.9
5	Education and Literacy, GOS	54	33	61.1	21	38.9
6	Energy, GOS	3	3	100.0	0	0.0
7	Excise & Taxation, GOS	3	3	100.0	0	0.0
8	Food, GOS	1	0	0.0	1	100.0
9	Forest, Wildlife & CDA, GOS	11	7	63.6	4	36.4
10	Health, GOS	32	11	34.4	21	65.6
11	Home, GOS	13	12	92.3	1	7.7
12	Human Rights, GOS	1	0	0.0	1	100.0
13	Human Settlement, GOS	1	0	0.0	1	100.0
14	Industrial & Commerce, GOS	2	1	50.0	1	50.0
15	Information, Science & Technology, GOS	2	2	100.0	0	0.0
16	Irrigation (Water & Drainage), GOS	12	6	50.0	6	50.0
17	Labour Dept, GOS	1	1	100.0	0	0.0
18	Law P.A. & Prosecution	2	2	100.0	0	0.0
19	Lining of Main Canals	11	10	90.9	1	9.1

S.#.	Departments / Sectors	Number of Schemes Visited	Satisfactory	Percentage	Un-Satisfactory	Percentage
20	Livestock and Fisheries, GOS	11	8	72.7	3	27.3
21	Local Government, GOS	90	56	62.2	34	37.8
22	Mega Schemes for Karachi City	5	3	60.0	2	40.0
23	Minorities & Affairs, GOS	8	8	100.0	0	0.0
24	Planning & Development, GoS	3	1	33.3	2	66.7
25	Population Welfare, GOS	2	2	100.0	0	0.0
26	Provincial Ombudsman, GOS	1	1	100.0	0	0.0
27	Public Health Engineering, GOS	69	40	58.0	29	42.0
28	Rehabilitation (PDMA), GOS	3	3	100.0	0	0.0
29	S.G.A.and Coordination, GOS	2	0	0.0	2	100.0
30	Social Welfare, GOS	2	2	100.0	0	0.0
31	Special Education	1	1	100.0	0	0.0
32	Sports & Youth Affairs, GOS	20	19	95.0	1	5.0
33	STEVA, GOS	1	1	100.0	0	0.0
34	Thar Coal Infrastructure Development	3	0	0.0	3	100.0
35	Universities and Boards	1	1	100.0	0	0.0
36	Women Development, GOS	4	1	25.0	3	75.0
37	Work and Service, GOS	89	74	83.1	15	16.9
Total		486	321	66.0	165	34.0

DEPARTMENTAL PERFORMANCE

MEC team made 548 monitoring visits to 486 ongoing schemes in FY 2023-24 to determine whether the scheme has been satisfactory or unsatisfactory in terms of financial and physical progress. Overall, 321 schemes (66%) were termed satisfactory and 165 schemes (34%) were found unsatisfactory. The M&E Cell working under P&DD schedule the visit plan on monthly basis which is approved a week before the following month. MEC team starts collecting data from the executing agencies and prepare the plan accordingly, liaison with the concerned engineers and project directors. With the use of experienced team and modern equipment, MEC strive hard to achieve their objective to provide factual position of development schemes helping heads of administrative departments and other government agencies to take corrective measures to improve the public sector delivery.

MONITORING BY REGIONAL OFFICES

Disaggregating the monitoring visits and schemes monitored by region illustrates interesting findings about the regional progress of development schemes.

In Karachi Region, MEC Team monitored 133 schemes with 174 monitoring visits. Out of the 133 schemes monitored, 83 were found to be satisfactory (62%) and 50 schemes were found unsatisfactory (38%). Out of the 174 monitoring visits, 87 visits were found satisfactory (50%) and 87 visits were unsatisfactory (50%).


Monitoring Summary of Region-Wise Schemes in FY 2023-24			
Region	Schemes	Satisfactory	Unsatisfactory
Hyderabad	114	88	26
Sukkur	155	107	48
Karachi	133	83	50
Larkana	84	43	41
Total	486	321	165

In Hyderabad Region, MEC Team monitored 114 schemes with 122 monitoring visits. Out of the 114 schemes monitored, 88 were found to be satisfactory (77%) and 26 schemes were found unsatisfactory (23%). Out of the 122 monitoring visits, 88 visits were found satisfactory (72%) and 34 visits were unsatisfactory (28%).

In Larkana Region, MEC Team monitored 84 schemes with 86 monitoring visits. Out of the 84 schemes monitored, 43 were found to be satisfactory (51%) and 41 schemes were found unsatisfactory (49%). Out of the 86 monitoring visits, 44 visits were found satisfactory (51%) and 42 visits were unsatisfactory (49%).


In Sukkur Region, MEC Team monitored 155 schemes with 166 monitoring visits. Out of the 155 schemes monitored, 107 were found to be satisfactory (69%) and 48 schemes were found unsatisfactory (31%). Out of the 166 monitoring visits, 108 visits were found satisfactory (65%) and 58 visits were unsatisfactory (35%).

Regional Monitoring Visits in FY 2023-24			
Region	Satisfactory	Unsatisfactory	Total
Hyderabad	88	34	122
Sukkur	108	58	166
Karachi	87	87	174
Larkana	44	42	86
Total	327	221	548

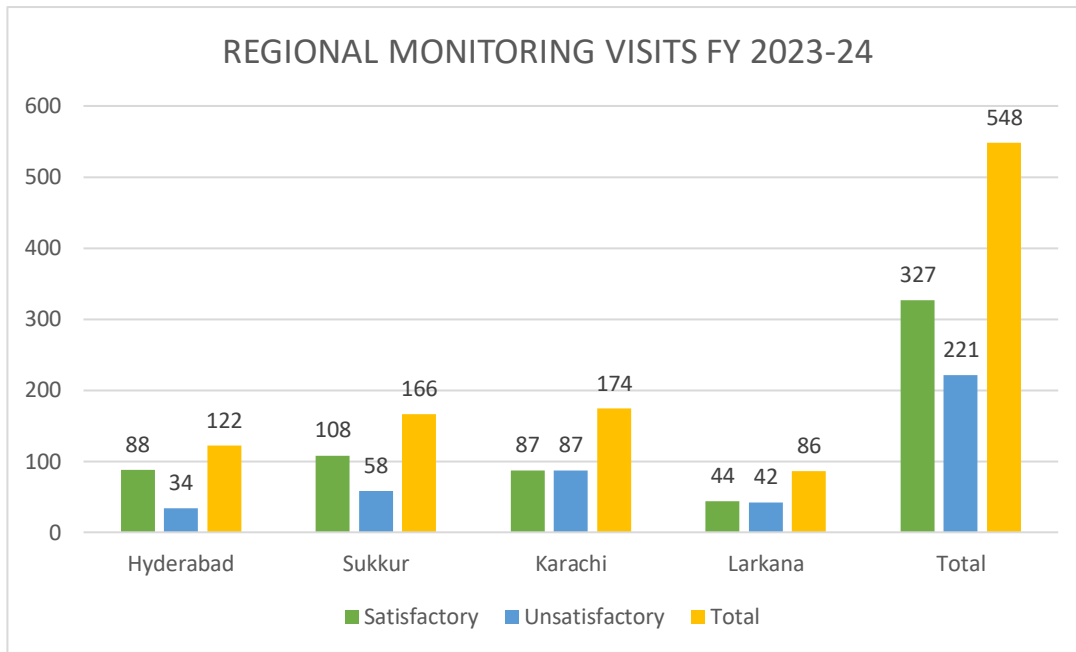

FIELD MONITORING OVER THE YEARS

MEC Team visited a total of 486 schemes during FY 2023-24 with several re-visits for a number of schemes. The total number of monitoring visits accumulated to 548. The total ADP portfolio for FY 2023-24 comprised of 5,256 schemes with 3,311 ongoing and 1,945 new schemes. The graph below illustrates the field monitoring trend over the years in relation to the total ADP portfolio for the corresponding year.

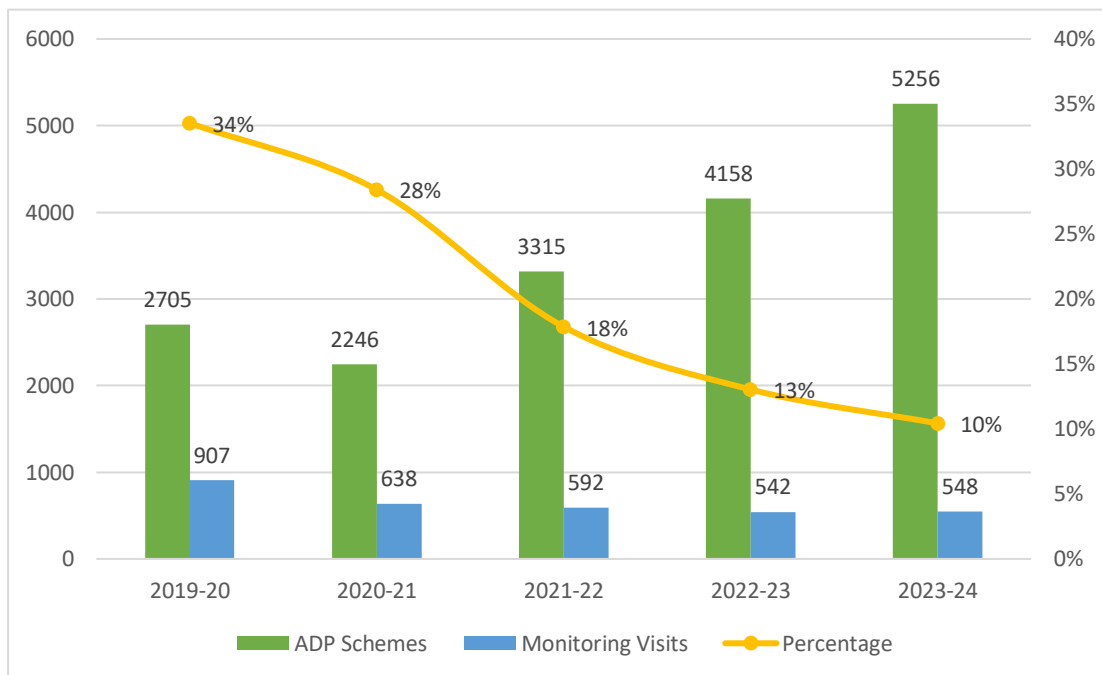





KEY RESULT INDICATORS

RESPONSES RECEIVED FROM LINE DEPARTMENTS

MEC Team proactively pursued monitoring of 486 schemes along various Line Departments with a total of 548 monitoring visits. This reflected the commitment to ensure quality control for development schemes, especially those termed unsatisfactory.

Top 10 Departmental Response Against Compliance:

Departments / Sectors	Percentage
Human Rights, GOS	100
Energy, GOS	100
Provincial Ombudsman, GOS	100
Social Welfare, GOS	100
Transport & Comm. (Roads), GOS	100
Human Rights, GOS	100
Universities and Boards	100
Livestock and Fisheries, GOS	80
Sports & Youth Affairs, GOS	75
Lining of Main Canals	67


In terms of response received from the corresponding department against the compliance sent for unsatisfactory status, almost 22 of total 30 departments complied and rectified the issues in the time prescribed.

However, 08 departments failed to comply against the feedbacks generated by MEC for unsatisfactory performance.

TREND ANALYSIS OF OBSERVATION TYPE

With a total of 548 monitoring visits for 486 development schemes for FY 2023-24, MEC has ensured that repeated monitoring visits translate into improved financial and physical progress indicators over time. It is evident that repeated visits over the same schemes have considerably improved their quality. This is reflected in the fact that out of 548 monitoring visits, 327 visits were found to be satisfactory (60%) and 221 visits were found to be unsatisfactory (40%). However, the ultimate status of the 486 monitored schemes demonstrate that 321 schemes were termed satisfactory (66%) and 165 schemes remained unsatisfactory (34%). This essentially means that continuous monitoring and repeated visits helped improve the quality of schemes considerably.

Status	2019-20	2020-21	2021-22	2022-23	2023-24
Satisfactory	69%	57%	65%	63%	60%
Unsatisfactory	31%	43%	35%	37%	40%

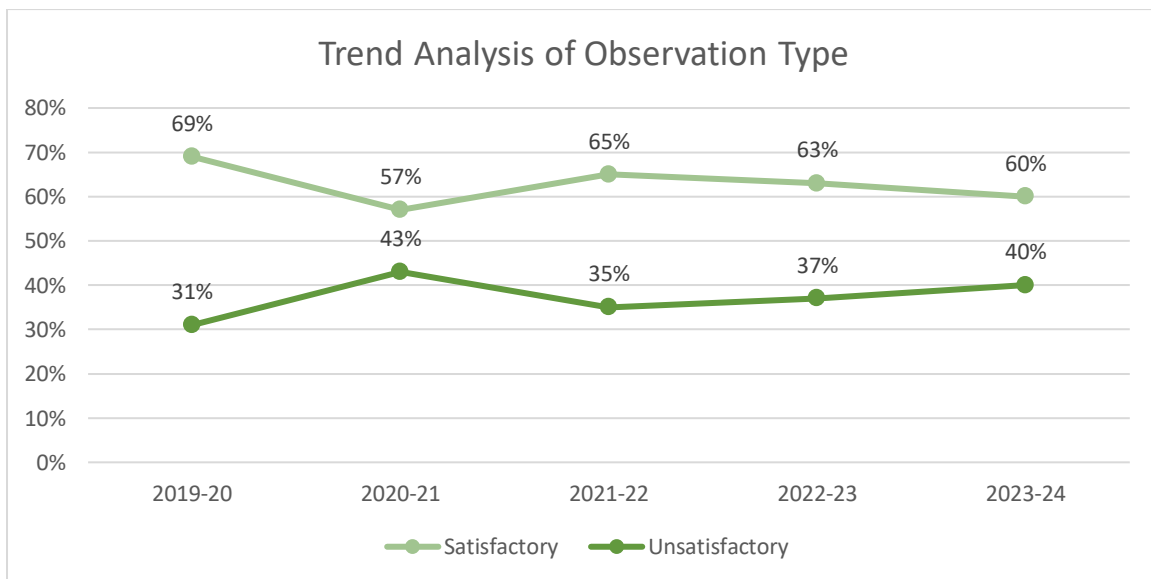

Note: Before FY 2018-19, the categories of observation type included Average, Satisfactory and Unsatisfactory status. However, FY 2018-19 onwards, the "average" observation type is now considered unsatisfactory. Hence, now the observation type only includes two broad categories of satisfactory and unsatisfactory status.

UNSATISFACTORY SCHEMES 4 YEAR ANALYSIS


Departments	Percent % Of Unsatisfactory Schemes						
	2020-21	2021-22	2022-23	3-Year Average	2023-24	Increase / Decrease	Index
Agriculture, Supply & Prices	36.0	20.0	30.0	28.7	30.0	1.3	↑
Auqaf, Zakat, Ushr & R.A.	36.4	57.0	38.0	43.8	55.0	11.2	↑
Board of Revenue	88.9	0.0	0.0	29.6	0.0	-29.6	↓
Culture, Tour & Antique	27.3	53.0	36.0	38.8	43.0	4.2	↑
Education Sector	37.5	31.0	29.0	32.5	45.0	12.5	↑
Environment & Coastal Development	0.0	0.0	0.0	0.0	0.0	0.0	↓
Forest & Wildlife	45.5	8.0	21.0	24.8	36.0	11.2	↑
Health	34.1	51.0	53.0	46.0	71.0	25.0	↑
Home	50.0	38.0	80.0	56.0	8.0	-48.0	↓
Industries & Commerce	50.0	75.0	50.0	58.3	67.0	8.7	↑
Irrigation	40.0	35.0	22.0	32.3	56.0	23.7	↑
Livestock & Fisheries	51.7	50.0	40.0	47.2	38.0	-9.2	↓
Local Government & HTP	37.7	28.0	42.0	35.9	45.0	9.1	↑
Minorities Affairs	50.0	38.0	25.0	37.7	0.0	-37.7	↓
Planning & Development	33.3	0.0	50.0	27.8	75.0	47.2	↑
Public Health Engineering	49.2	27.0	29.0	35.1	44.0	8.9	↑
Rural Development	95.8	100.0	18.0	71.3	0.0	-71.3	↓
SGA & C	36.4	40.0	33.0	36.5	100.0	63.5	↑
Sports & Youth Affairs	20.0	16.0	33.0	23.0	17.0	-6.0	↓
Thar Coal Infrastructure Development	100.0	67.0	0.0	55.7	100.0	44.3	↑
Women Development	75.0	0.0	50.0	41.7	75.0	33.3	↑
Works & Services	34.9	35.0	32.0	34.0	20.0	-14.0	↓
Average	46.8	35.0	32.3	38.0	42.0		
<i>No. of Departments where the % of Unsatisfactory Schemes Decreased</i>					↓		8
<i>No. of Departments where the % of Unsatisfactory Schemes Increased</i>					↑		14

MONITORING OUTCOMES

Compliance Outcomes in FY 2023-24

S. No.	Department	1st Visit Compliances Received	Revisit(s) Compliances Received	Total Compliances Received	% Contribution of Revisits in Compliance
1	Agriculture, GOS	1	0	1	0
2	Antiquities, GOS	0	0	0	n/a
3	Auqaf, GOS	1	0	1	0
4	Culture, GOS	0	0	0	n/a
5	Education and Literacy, GOS	11	1	12	8.33
6	Energy, GOS	3	0	3	0
7	Excise & Taxation, GOS	0	0	0	n/a
8	Food, GOS	0	0	0	n/a
9	Forest, Wildlife & CDA, GOS	0	0	0	n/a
10	Health, GOS	3	5	8	62.50
11	Home, GOS	0	0	0	n/a
12	Human Rights, GOS	1	1	2	50.00
13	Human Settlement, Spatial Development & Social Housing	0	0	0	n/a
14	Industrial & Commerce, GOS	0	1	1	100
15	Information & Archives, GOS	0	0	0	n/a
16	Irrigation (Water & Drainage), GOS	4	0	4	0
17	Labour Dept, GOS	0	0	0	n/a
18	Law P.A, & Prosecution	0	0	0	n/a
19	Lining of Main Canals	2	0	2	0
20	Livestock and Fisheries, GOS	2	2	4	50.00
21	Local Government, GOS	16	2	18	11.11
22	Mega Schemes for Karachi City	2	0	2	0
23	Minorities & Affairs, GOS	0	0	0	n/a
24	Planning & Development, GoS	2	0	2	0


S. No.	Department	1st Visit Compliances Received	Revisit(s) Compliances Received	Total Compliances Received	% Contribution of Revisits in Compliance
25	Population Welfare, GOS	1	0	1	0
26	Provincial Ombudsman, GOS	1	0	1	0
27	Public Health Engineering, GOS	4	0	4	0
28	Rehabilitation (PDMA), GOS	0	0	0	n/a
29	S.G.A.and Coordination, GOS	0	2	2	100
30	Social Welfare, GOS	1	1	2	50
31	Special Education	0	0	0	n/a
32	Sports & Youth Affairs, GOS	3	0	3	0
33	STEVTA, GOS	0	0	0	n/a
34	Thar Coal Infrastructure Development	0	0	0	n/a
35	Transport & Comm. (Roads), GOS	1	0	1	0
36	Universities and Boards	1	0	1	0
37	Women Development, GOS	0	0	0	n/a
38	Work and Service, GOS	5	1	6	16.67
TOTAL:		65	16	81	19.75

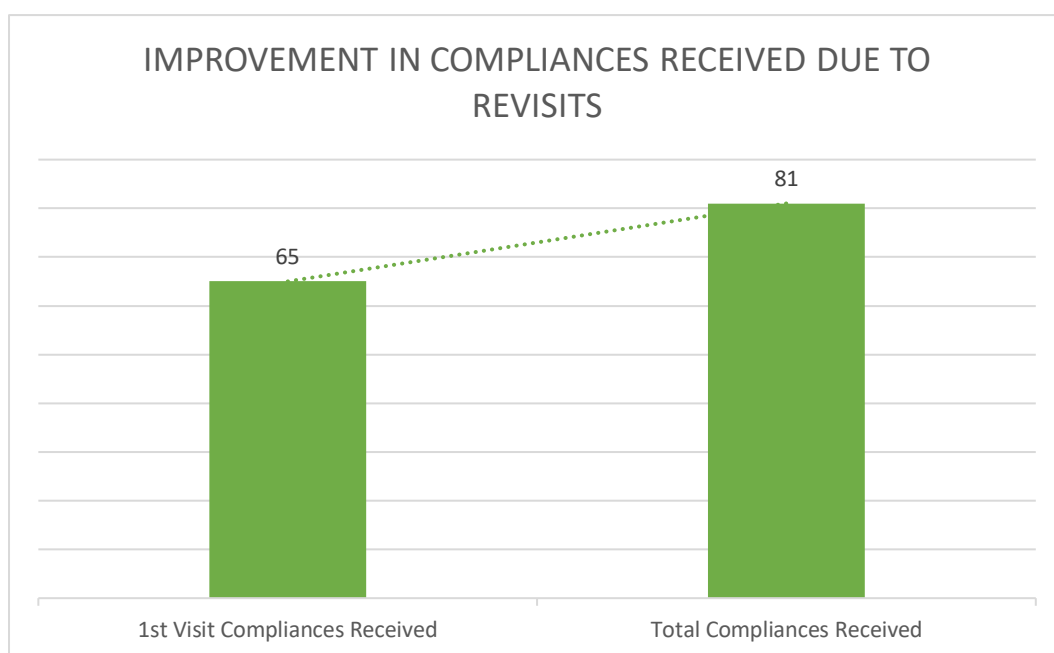

UNSATISFACTORY SCHEMES STATUS

S. No.	Department	Unsatisfactory Status (FY 2022-23)	Unsatisfactory Status (FY 2023-24)
1	Agriculture, GOS	1	4
2	Auqaf, GOS	1	5
3	Antiquities, GOS	0	1
4	Cooperative, GOS	1	0
5	Culture, GOS	2	3
6	Education and Literacy, GOS	10	21
7	Energy, GOS	1	0
8	Excise & Taxation, GOS	2	0
9	Food, GOS	10	1
10	Forest, Wildlife & CDA, GOS	0	4
11	Health, GOS	13	21
12	Home, GOS	5	1
13	Human Rights, GOS	0	1
14	Human Settlement, GOS	1	1
15	Industrial & Commerce, GOS	1	1
16	Information & Archives, GOS	2	0
17	Irrigation (Water & Drainage), GOS	4	6
18	Karachi Metropolitan Corporation, KWSB	1	0
19	Lining of Main Canals, GOS	0	1
20	Livestock and Fisheries, GOS	0	3
21	Local Government, GOS	19	34
22	Mega Schemes for Karachi City	0	2

S. No.	Department	Unsatisfactory Status (FY 2022-23)	Unsatisfactory Status (FY 2023-24)
23	Minorities & Affairs, GOS	3	0
24	Physical Planning & Housing (Buildings), GOS	1	0
25	Planning & Development, GoS	1	2
26	Public Health Engineering, GOS	12	29
27	Rehabilitation (PDMA), GOS	1	0
28	Rural Development, GOS	2	0
29	S.G.A.and Coordination, GOS	1	2
30	Sports & Youth Affairs, GOS	1	1
31	Thar Coal Infrastructure Development, GOS	0	3
32	Women Development, GOS	1	3
33	Work and Service, GOS	26	15
Total		123	165

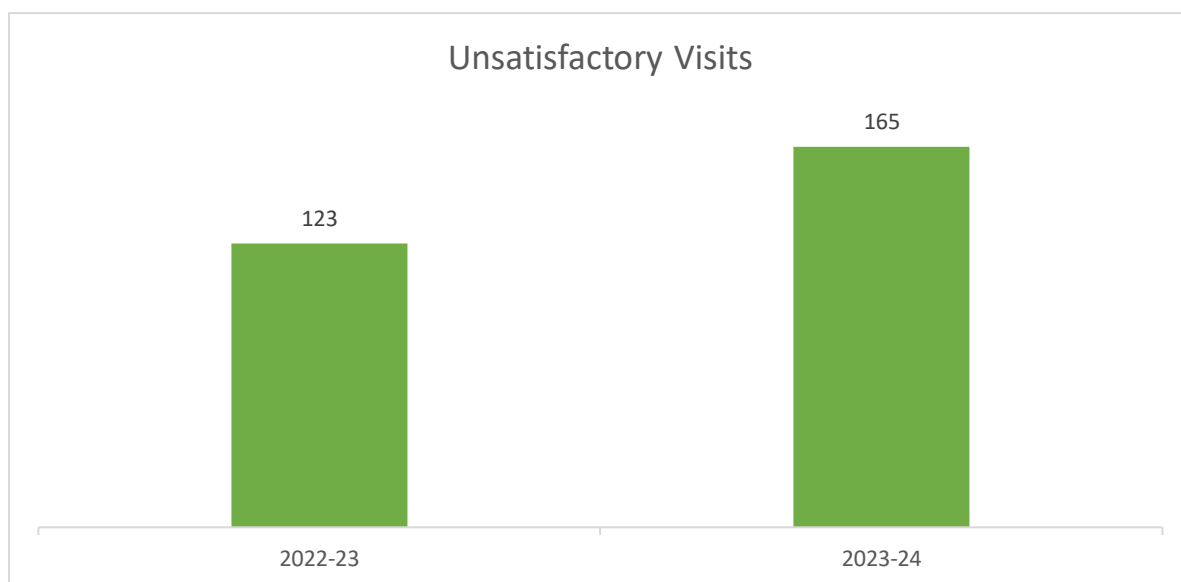

SUMMARY OF COMPLETED SCHEMES IN FY 2023-24

S.NO	Department	No of Schemes	Estimated Cost
1	Agriculture, Supply & Prices	4	8557.960
2	Auqaf, Zakat, Ushr & R.A.	5	93.000
3	Board of Revenue	1	2128.101
4	Culture, Tourism, Antiquities & Archives	7	1333.486
5	Education (School)	64	5988.690
6	Education (College)	41	2243.549
7	Education (Emp)	1	14.924
8	Education (STEVTA)	1	42.232
9	Education (U&B)	3	246.962
10	Finance	1	30.000
11	Forest & Wildlife	3	3936.294
12	Health	8	3223.212
13	Home	2	219.684
14	Human Settlement	2	56.694
15	Industries & Commerce	5	606.171
16	Information S&T	3	621.598
17	Irrigation	38	14263.804
18	Law, P.A & Prosecution	4	497.082
19	Livestock & Fisheries	3	403.974
20	LG (Water Supply)	49	14169.815
21	LG (Bldgs)	3	437.021
22	LG (Roads)	32	8772.468
23	LG (Community Services)	11	1367.951
24	LG (HTP)	1	230.720
25	LG (Livestock)	2	538.911

S.NO	Department	No of Schemes	Estimated Cost
26	Lining of Main Canals	7	1550.284
27	Mega Projects for Karachi	9	15318.321
28	Minorities Affairs	24	478.825
29	Planning & Development	5	486.246
30	Population Welfare	5	34.819
31	Public Health Engineering	71	9785.909
32	Rural Development	4	70.700
33	Sindh Public Service Commission	1	120.000
34	Social Protection	1	339.920
35	Social Welfare	1	75.200
36	Sports & Youth Affairs	16	940.438
37	Thar Coal Infrastructure	1	1936.266
38	Transport & Mass Transit	3	377.225
39	Women Development	2	102.918
40	Works & Services	159	44014.316
Total		603	145655.69

SPECIAL ASSIGNMENTS DURING F.Y 2023-24

MEC addressed the special assignments during F.Y 2023-24, MEC was specially assigned to monitor the District ADP portfolio of 05 Districts comprising of 833 schemes by the Interim Provincial Government, the details are given in the table below;

S#	District	First Visit			Compliance Visit (Current Status)		
		No. of Schemes Visited	Satisfactory	Un-Satisfactory	No. of Schemes Visited	Satisfactory	Un-Satisfactory
1	Jacobabad	132	29	103	74	72	02
2	Kashmore & Knadhkot	204	83	121	37	31	6
3	Karachi – KMC	201	45	156	156	136	20
4	Matiari	221	111	110	13	05	08
5	Shikarpur	75	25	50	09	09	00
	Total	833	293	540	289	253	36

Scan the following QR Code for detail list of the above table



During F.Y 2023-24, MEC was also assigned the special visits to monitor the Foreign funded portfolio, the details are given in the table below;

S#	Projects	No. of Schemes Visited	Satisfactory	Un-Satisfactory
1	CLICK (1 st Visit)	141	93	48
2	CLICK (2 nd Visit)	50	19	31
3	CLICK (3 rd Visit)	31	31	00
3	SFERP (First-Visit)	57	N/A	
4	SFERP (Re-Visit)	106		
5	CLICK (Compliance-Visit)	31	31	00
6	PHED 100 Schemes	100	Functional / Non-Function RO Plant status	
	Total	516	174	79

ESTABLISHMENT OF DISTRICT ADP CELL

In pursuance of Chief Minister, Sindh and his Cabinet's interaction sessions held at Divisional level dated 07th and 8th May 2024, the Planning and Development Board, Government of Sindh established a dedicated special cell viz "District ADP Cell" in Planning and Development Board, Government of Sindh to gather and compile data gathered on prescribed proformas distributed during the above-mentioned sessions. The Cell gathered the proposals for 28,838 numbers of schemes directly from the MPAs, MNAs, notables and other representatives of general public. District wise details for number of proposals received are given in the table below;

DISTRICT-WISE PROPOSALS RECEIVED			
S.#.	DISTRICT	# OF PROPOSAL RECV.	# OF SCHEMES
1	Badin	1	1,445
2	Dadu	2	1,543
3	Ghotki	9	1,113
4	Hyderabad	7	1,193
5	Jacobabad	2	58
6	Jamshoro	2	355
7	Kamber Shahdadkot	5	5,823
8	Karachi Central	5	279
9	Karachi East	5	310
10	Karachi Kemari	1	195
11	Karachi Korangi	2	18
12	Karachi Malir	1	198
13	Karachi South	2	573
14	Karachi West	3	401
15	Kashmore	2	62
16	Khairpur	2	239
17	Larkana	3	113
18	Matiali	4	119
19	Mirpurkhas	1	2,407
20	Nausharo Feroze	2	3,311
21	Sanghar	3	725
22	Shaheed Benazirabad	2	1,637
23	Shikarpur	2	548
24	Sujawal	2	465
25	Sukkur	6	1,446
26	Tando Allahyar	2	468
27	Tando Muhammad Khan	2	1,268
28	Tharparkar	4	2,413
29	Thatta	1	54
30	Umerkot	3	59
	Total	88	28,838

Sector wise details for number of proposals received for new schemes are given in table below;

SECTOR-WISE PROPOSALS RECEIVED		
S.#.	SECTOR	# OF SCHEMES
1	Auqaf	10
2	College Education	7
3	Culture & Tourism	115
4	Development Work	124
5	Education	1,657
6	Energy	640
7	Food Department	1
8	Forest & Wildlife	6
9	Health	513
10	Home	2
11	Human Settlement	6
12	Industries & Commerce	3
13	Information, Science & Technology	1
14	Irrigation	239
15	Labour Department	3
16	Livestock & Fisheries	33
17	Local Govt.	2,586
18	Buildings	433
19	Roads	2,934
20	Minority Affairs	63
21	Public Health & Engineering	6,376
22	Rural Development	327
23	School Education	226
24	Social Welfare	29
25	Sports & Youth Affairs	34
26	STEVTA	16
27	Transport	11
28	Universities & Board	22
29	Water & Drainage	9
30	Water & Sewerage	53
31	Water Sanitation	251
32	KW&SB	48
33	Water Supply	26
34	Works & Services	3,679
35	Gas (Federal)	41
36	ADP Scheme	22
37	Any Concerned Department	8,292
	Total	28,838

THIRD PARTY MONITORING

During the year 2022-23, the M&E Cell explored the idea of hiring consultants for conducting, preparing, and submitting reports under the Third-Party Monitoring (TPM) mechanism. Keeping the cost factor under consideration, the following three schemes were randomly selected to undergo TPM. As a result, all three were placed under a rigorous Inspection and Testing Plan, which, in regular visits, is not usually undertaken by the M&E Cell during its routine assessments.

1. ADP# 978 'INFRASTRUCTURE DEVELOPMENT OF INDUSTRIAL ESTATE LARKANO'
2. ADP# 842 'MEHRAN UNIVERSITY COLLEGE OF ENGINEERING & TECHNOLOGY AT KHAIRPUR'
3. ADP#2782 'W/R OF MITHI TO DIPLO ROAD (39.20 KMS)'

The rigorous Inspection and Testing Plan adopted by consultants included below tests:

a. Road Construction

- i. Sieve Analysis
- ii. CBR Test
- iii. Crushing Test
- iv. LOS ANGELES (Abrasion Test)
- v. Impact Test
- vi. Soundness Test
- vii. Flakiness & Elongation Index Test
- viii. Sp Gravity and Water Absorption Test
- ix. Liquid and Plastic Limit Test
- x. Bitumen Adhesion Test
- xi. Bitumen (Flash and Fire Point) Test
- xii. Field Density Test (FDT)
- xiii. Concrete Compressive Strength of Toe Wall
- xiv. 3-Edge Load Bearing Test for RCC Pipes
- xv. Testing for Riding Quality

b. For Buildings

- i. Schmidt Hammer Test for compressive strength of structural elements
- ii. Cement Tests
- iii. Sieve Analysis
- iv. Compressive Strength of Pavers, Kerb Stones and Bricks
- v. Rebar Scanning in structural members.
- vi. Tensile strength and Bending Test
- vii. Pressure Testing of Pipes and Joints
- viii. Concrete Slump Test



FINDINGS

&

RECOMMENDATIONS



AUQAF DEPARTMENT

GENERAL FINDINGS

During FY 2023-24 Development schemes of Auqaf department have been visited by Monitoring & Evaluation Cell, Planning Development Department Govt of Sindh. A total of 11 schemes were visited by MEC in FY 2023-24. Out of 11 Schemes the quality of work on 05 Schemes i.e., 45.5% were declared satisfactory, whereas on 06 Schemes i.e., 54.5% quality of work was declared unsatisfactory.



RECOMMENDATIONS

E/A should avoid advance payment, and work may be executed as per scope of PC-I.

In all restoration and conservation work, it must be ensured that any material used must be free from impurities and the water must be potable.

Regular maintenance must be carried out of the completed schemes by the administrative departments to preserve the sites.

Restoration and conservation work will be done with special care to avoid any sort of damage to the old structure and without disturbing the originality of the religious sites.

In the light of study / survey, priority should be given to those areas/components, which are vulnerable, and need immediate attention.

Keeping in view the social & cultural importance of the religious schemes, department Should have to expedite his vigilance to monitor the scheme on regular basis so that the designed objects would be achieved within the required time frame.



EDUCATION

GENERAL FINDINGS

Education sector is a crucial component of the provincial government's efforts to improve and reform education. The Sindh Govt. ADP allocates substantial funds each year to various schemes aimed at addressing long-standing challenges in Sindh's educational infrastructure, access, and quality.

One of the primary focuses of these schemes is the rehabilitation and construction of school buildings. Many schools, especially in rural and underdeveloped areas, lack basic facilities such as classrooms, clean drinking water, electricity, and sanitation. The ADP plan provides for the construction of new school buildings, the repair of dilapidated structures, and the provision of essential utilities to make schools more conducive to learning.

In this regard, other key components e.g., College Education and Universities & Boards are also playing pivotal role in overall betterment and welfare of the society and there has been extra focus on development schemes pertaining to colleges and universities in order to have state of the art infrastructure facilities in these sub sectors.

MEC conducted 62 visits of Education Department and found 34 schemes satisfactory i.e. 55% while 28 schemes were unsatisfactory i.e. 45

Undue delay in submission of project related data by executing agency still continues to be a big issue regarding which serious action needs to be taken.

The communication gap between executing agency and contractors lead to certain on-site issues and physical progress of projects is adversely affected.

Improper releases against the allocations cause manifold increase in project cost which has colossal burden on budget planning and cost escalation factor becomes imminent.

On site workmanship can be improved by adopting best engineering practice through constant surveillance by the executing agency and the consultants.

Lack of drinking water, separate lavatories for girls and boys as well inadequate raising of compound walls is another key issue which needs to be resolved on priority basis.

The revenue component of education development schemes suffers a lot especially due to tricky hierarchy. Thus, its real time benefits are hardly transferred to its actual beneficiaries who keep asking and demanding for class room furniture, books and other government funded items for which funds are already allocated and released. Timely availability of new revenue items to schools, colleges and universities as per given PC-I listings can make a huge difference in the functionality of our education system.



EDUCATION

RECOMMENDATIONS

Ensure that funds are released as per given schedule and according to the allocated budget. Delays in funding disrupt project timelines and often lead to suboptimal outcomes.

Enforce strict quality control measures during the construction of new schools and renovation of existing infrastructure. Regular site inspections by qualified engineers should be mandated, and poor-quality work should be corrected immediately to avoid future complications.

Improve coordination between the Education Department, the Planning and Development Department, and other relevant agencies to ensure that development plans align with local needs and priorities.

Introduction of technology specially in-classroom education delivery. It is imperative to introduce digital learning tools, computer labs, and smart classrooms, especially in underserved areas.

Allocate special funds to enhance access to education for girls and marginalized communities. Ensure that gender equity is a priority in all new schools and projects by providing gender-sensitive infrastructure such as separate restrooms, boundary walls for safety, and transportation facilities.

The Education Department should allocate specific funds for maintenance and ensure that regular inspections are conducted to prevent deterioration.

Executing agencies should submit timely and accurate Monthly Progress Reports (MPRs) and Project Completion Reports (PC-IV) to monitor the status of schemes and identify areas that need immediate attention.

Fostering the partnerships with private sector organizations, NGOs, and international donors to pool resources, expertise, and technology. Such collaborations can enhance the effectiveness of education schemes and introduce innovative approach.



FOREST & WILD LIFE

GENERAL FINDINGS

The forest & wildlife Department of Sindh is graded in four different categories viz. Riverine Forests, Irrigated Plantations, Protected Forests and Mangrove Forests. Monitoring & Evaluation Cell, Planning Development Department Govt of Sindh has paid visit to 11 schemes of Forest & Wildlife Department during FY 2023-24. Out of 11 Schemes, the quality of work on 07 Schemes i.e., 64% were declared satisfactory, whereas on 04 Schemes i.e., 36% quality of work was declared unsatisfactory.

RECOMMENDATIONS

Forest department should engage in capacity development of locals for better protection of the planted areas, and to motivate the masses for tree plantation by providing free plants.

Targets may be increased as the newly vacated area has potential for deep forest.

The E/A should provide the detail/data of capital component to MEC, P&D department, which is important to physical verification at site.

E/A should submit GIS survey report and should share coordinates with MEC.

Number of plants of Parker sonia, Nerium Indicum commonly known as Kaner, and Pongamia pinnata commonly known as Sukh chain, should be increased on the median of road as these plants grow thicker and they can save the eyesight of drivers from the headlights of vehicles coming from the opposite sides.


Watering to young plants should be ensured particularly for Urban plantation.

Regular supervision and maintenance of new plantation must be carried out because any negligence in maintenance could damage the plantation.

Raised micro and macro plantation should be supplied for plantation in coming spring season to local farmers, landlords, NGOs and other stakeholders on subsidized rates. It will facilitate in increasing tree cover in the province.

If any area of soil is not suitable for plants, then it should be replaced with fertile/clay soil.

Proper maintenance of young plants should be done even after the completion of the scheme.

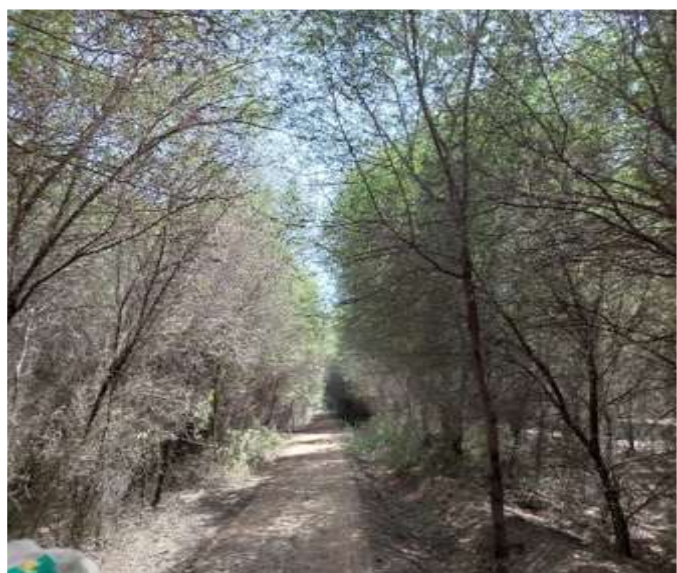

IRRIGATION & LINING OF MAIN CANALS

GENERAL FINDINGS

Irrigation Department is categorized into three parts i.e., Water management, Drainage and Lining of main canal. MEC has visited 16 schemes of Irrigation and 13 schemes of Lining of Main Canals department during FY 2023-24. Out of 16 Schemes of irrigation, 7 Schemes were found satisfactory, whereas 9 Schemes were declared unsatisfactory and out of 13 schemes of Lining of Man Canal, 10 schemes were found satisfactory, whereas 3 schemes found unsatisfactory.

MEC team identified poor quality of work, which was attributed to inadequate workmanship, insufficient supervision by the (E/A) staff, deviations from the approved PC-1 scope, and the failure to provide the necessary records in a timely manner for verifying payments against quantities.

Canal Bank Strengthening:

In most of the canal bank strengthening schemes, the earthwork found to be improperly dressed, leveled, and compacted, with no use of a sheep foot roller, potentially leading to inadequate compaction. Additionally, most of the earthen material excavated from the toe of the bank, which could compromise the bank's stability and contribute to erosion.

Drainage Schemes:

In several drainage schemes, the pumping machinery was found to be non-functional due to the lack of electricity and backup generators, which severely impacted the drainage capacity and causes water logging and soil salinity

Stone Pitching Issues:

In many locations, the stone pitching was disturbed due to improper interlocking, affecting its overall stability and causes water seepage

Furthermore, filler materials were not used in the stone pitching, resulting in visible gaps and voids. These gaps could cause seepage and settlement issues.

The profile, alignment, and slope of the stone pitching were also improperly maintained at some locations.



IRRIGATION & LINING OF MAIN CANALS

Canal Lining Schemes:

Cracks were observed in the concrete panels of lined canals at multiple locations, which could lead to seepage, water losses, and even theft.

In certain areas, the thickness of the concrete in the lined canals was found to be lesser than design specifications.

RECOMMENDATIONS

Earthwork Execution:

Earthwork should be carried out in accordance with established standard procedures and specifications to ensure proper quality and structural integrity.

Quality Testing:

Quality tests must be conducted on-site during execution to ensure that the work is performed according to the required standards and specifications.

Stone Pitching Work:

Proper profiling, alignment, and slopes should be maintained during stone pitching to ensure the work meets the required specifications. Additionally, filler materials should be used effectively at the sides to prevent seepage.

Concrete Lining Thickness:

The thickness of the concrete used in canal lining should be executed as per the approved drawings and design specifications to ensure durability and proper functionality.

Pumping Machinery and Backup Generators:

The pumping machinery at pumping stations and tube well sites should be provided in line with the site-specific requirements. Additionally, backup generators must be installed to ensure continuous operation in case of power failures.



HEALTH

GENERAL FINDINGS

The overall vision of Health Department is based on “Health for all “. The new Health Policy aims to implement this strategy of protecting peoples against Hazardous Diseases, promoting public health, upgrading curative health facilities, enhancing equity, efficiency and effectiveness in health sector.

In the financial year 2023-24, in total 38 schemes were visited by MEC, P&D Department. Out of these 38 Schemes the work on 11 Schemes i.e., 29% were declared satisfactory, while the work on the remaining 27 schemes i.e., 71% were declared unsatisfactory. Out of 27 Un-Satisfactory schemes, compliance of 8 schemes were received from concerned executing department after rectification while compliance of 19 schemes were pending.

Poor planning & supervision has been observed in execution work by the concerned XEN/AEN/Sub Engineer.

Lack of Provision of External Drainage of Building & Epoxy Flooring & Anti-Bacterial Paint in OT/ICU of hospitals in construction design was observed.

Besides other issues the key problems observed pertained to:

- i. Honey combing in many structures which showed improper mixing and placement of concrete.
- ii. Improper budget allocation & release have been observed in most of the schemes which delay the process of implementation and cost of projects/schemes being implemented and lead them towards a lengthy process of revision & re-revision.
- iii. Sindh Government ‘Not-for-Sale’ Stamp was found missing on various Medicines/consumable items procured through various schemes.

RECOMMENDATIONS

Proper planning, supervision & accountability should be ensured by the E/A i.e. concerned XEN/AEN/Sub-engineer.

Timely provision of all relevant documents regarding the Scheme should be ensured by the E/A & A.D, so that the Monitoring and Evaluation Functions are conducted smoothly.

Proper tagging & Timely procurement of revenue component should be done by E/A to ensure smooth & timely healthcare service delivery to the people of Sindh.

Transparency must be ensured by Administrative Department especially in the procurement of revenue component.

Administrative Department should avoid frequent switching of executing officials for smooth execution & timely completion of development works with proper record keeping and tagging of procured items under various ADP schemes.



LIVE STOCK & FISHERIES

GENERAL FINDINGS

MEC conducted 13 visits of Livestock & Fisheries Department F.Y 2023-24 and found 08 schemes satisfactory while 05 schemes were unsatisfactory.

It was generally observed that the department could not get funds released in time resultantly it failed to provide planned machinery, equipment, medicines, vaccines, awareness sessions and implement to the Livestock Farmers & Fishermen during period of project / scheme at project Districts.

On some schemes the pace of work was found lagging behind the financial progress

In some old on-going schemes, the execution remained unnecessarily slow which otherwise should have been priority of the department to conclude.

Lack of planning in execution of various schemes which causes unnecessary delays in completion of scheme

Mostly all schemes are executed by the DG & Directors offices which are located in Hyderabad & Karachi, so the people face many difficulties due to poor coordination b/w higher authority & field staff.

Some Schemes (Action Accelerated Programme (AAP) Livestock & Fisheries Component, Sindh Agriculture Growth Project (SAGP) Livestock Component etc..) are nearly completed which are executed by the DG / PD and avoided for providing Data & conducting visits to MEC for monitoring in the field in which the livestock farmers have facing many difficulties, no benefits & huge loss of money.

RECOMMENDATIONS

The Administrative Department should have execution plan to expedite the release utilization of funds in time to reach out to the growers in need.

Procurement of required machinery, medicines, vaccines and other revenue items should be made according to SPPRA rules and within stipulated time frame.

The Administrative Department (Livestock & Fisheries Department) should avoid procurement of local / poor quality of medicines & other revenue items etc & not mentioned in the PC-I.

E/A should pay attention to the specific observations and recommendations raised by the visiting team to achieve the project objectives timely.

The devolution of the authority should be made at divisional level so as to facilitate the farmers to seek required help and guidance accordingly

Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results

Monthly Progress Report (MPR) of schemes must be submitted by Administrative Department before 10th of every month.



LOCAL GOVERNMENT & MEGA SCHEMES OF KARACHI

GENERAL FINDINGS

The schemes executed by the Local Government Department include mainly the rehabilitation and up-gradation of basic infrastructure facilities for public use. Facilities include construction/rehabilitation/ up-gradation of Roads, Building, Infrastructure i.e., Water Supply & Sewerage, Communal & Health Facilities.

In the financial year 2023-24, a total of 103 schemes were visited by MEC Department. Out of 103 Schemes the work on 57 Schemes i.e., 55% were declared satisfactory, while the work on the remaining 46 schemes i.e., 45% were declared unsatisfactory. Out of 46 Un-Satisfactory schemes, compliance of 16 schemes were received from department after rectification while compliance of 30 schemes were pending.

Similarly, Mega Schemes of Karachi were executed by Local Government Department, in FY 2023-24, total of 08 schemes were visited out of which 05 Schemes i.e., 62.5% were declared satisfactory, while 03 schemes i.e. 37.5%, were marked as Un-satisfactory. Out of 03 un-satisfactory schemes, compliance of 02 schemes were received from department after rectification while compliance of 01 scheme was pending.

One of the major issues is adaptation of thumb rule method in formation phase of PC-I completely neglecting the consideration of actual site conditions. As of result of this practice, schemes were revised due to unrealistic/approximate estimate by department at the time of preparation of PC-I. Moreover, Lack of supervision by field staff during the execution phase, frequent transfer and posting of project managers i.e., Project Director or Executive Engineer are also some core issues.

The major issues encountered during the monitoring of schemes were that there is lack of planning in design and execution of roads and drainage schemes that proper infrastructure was not provided to accommodate the sewerage and storm water separately, most of the time sewerage and storm water flows either in sewerage or drainage network resulting in choking or overflow of system during peak discharge or rainy reason.

Furthermore, inappropriate slope is also a core issue to be addressed as appropriate slope was not maintained in execution of road to smoothly drain the water. Due to improper drainage water remains stagnant which results in deterioration and complete failure of roads (from topmost Asphalt Layer to Embankment).

Due to multiple execution agencies, it has been observed that overlapping of development works is frequent in this department which cause difficulty in monitoring and retrieving record of schemes. MEC team found hard to identify and trace the exact executing agency for fixing the responsibility of deficiency in development work.



LOCAL GOVERNMENT & MEGA SCHEMES OF KARACHI

The other main issues are inadequate allocation and releases of funds by the department which take years to complete the scheme and by the time scheme gets to completion, initial work gets deteriorated and there is no proper SOPs for the repair and maintenance, majority of the schemes were revised due to unrealistic/approximate estimate by department at the time of preparation of PC-I, Lack of supervision by field staff during the execution phase, frequent transfer and posting of project managers i.e. Project Director or Executive Engineer, NHA/PWD/SHERE/WHO specifications not being followed properly in execution and testing of material (i.e. soil classification & gradation, bitumen quality test, field density test, compaction test, Pressure testing of pipe, strength test of concrete & steel).

The KW&SB within Local Government Department does not cooperate with the MEC Team neither they provide any scheme related documents nor accompany/facilitate the MEC Team for the field visit.

On various ADP schemes the Executing Agency (Local Government Department) had not provided complete documentation to M&E Cell. In a few schemes, it was observed while reviewing the measurement book that Overpayments and Advance Payments were made to the contractor.

RECOMMENDATIONS

EA should ensure proper sewerage and drainage network flow alongside the road. Sewerage and drainage networks must be separately planned, designed and executed.

The concerned Executive Engineer & Assistant Engineer should closely monitor the execution of construction work in order to improve quality of work.

To ensure quality execution, material testing of various materials may be carried out frequently.

The EA should improve the quality of work, workmanship to meet the prescribed specification and standard and ensure that material should be procured from vendor and quarry.

The overpayments/advance payments to contractors may be discouraged & payments be made as per quantity executed at site.

The department shall ensure the timely flow of funds so that the work does not suffer and ensure that procurement of required items shall be made according to SPPRA rules and within the stipulated timeframe.

The department should ensure that an experienced workforce is deputed, and good quality material should be procured to ensure quality as per mentioned standards.

On many schemes the pace of work found to lag financial progress. E/A ensured that the physical progress shall be at par with Financial Progress.

It is therefore recommended that documentation should be made available to Monitors well before the time of the visit so as to thoroughly check the project parameters.



PUBLIC HEALTH ENG. & RURAL DEV.

GENERAL FINDINGS

In fiscal year 2023-24, a total of 72 schemes of Public Health Engineering department were visited by MEC. Out of 72 Schemes, the work on 40 Schemes i.e. 56% were found satisfactory, while on 30 schemes i.e. 44% found unsatisfactory.

The major issues observed during the monitoring of the schemes were:

Executing agency mainly focuses on minor works like PE pipes, UPVC, CC block, paver blocks & CC drains, but the outcomes/achievements remain inadequate since most of schemes became nonfunctional at early life after completion either due to design survey mistake or O&M reasons.

The sewerage almost directly disposed of in natural streams without proper treatment in oxidation ponds. In many drains scheme land acquisition for oxidation ponds were not prioritized. In urban areas the direct disposal of drainage schemes has been resolved to a greater extent while in towns & rural areas' schemes the issue is constant.

Operation and Maintenance mostly found a weakest point by both PHED & local government department i.e., Concerned Municipal Committee/ Town Committee. The Committees do not carry out the O&M work specially in pumping machinery, Diesel engine sets, suction & delivery pipes etc. after transferring of schemes from PHED to Local govt department the later very rare owns the formers scheme.

Insufficient deployment of staff at disposal works & Treatment works

It is necessary to mention that Rural Development Department is short of qualified and experience human resource to conceive and execute better schemes so as to improve the overall foot-print of the department especially Solar Light Schemes, Asphalt Metaled Roads and etc.

RECOMMENDATIONS

The department may be directed to reset the priorities and try to execute the items which benefit the community and local people in place of utilization of funds on less prioritized items like Paver & CC block. They should always prioritize the construction of drainage scheme with all components then paver block and CC blocks. A preliminary survey of every project is need of the hour.

Land acquisition matters for construction of treatment works & disposal works should be finalized before start of civil works as in 90% treatment works land was not acquired due to land disputes & slow processing by revenue department.

The department may be directed to stop direct disposal of sewerage into natural streams/water bodies

PE pipes should be used in all water supply & drainage schemes with prior testing regime to be induced before burial of pipes.

Administrative Department must submit the PC-IV of the completed schemes so as maintain the infrastructure and get the desired results. Also, PC-V post evaluation of PHED schemes may correct its fault of earlier abandon//nonfunctional of schemes.



SPORTS & YOUTH AFFAIRS

GENERAL FINDINGS

Sports & Youth Affairs Department involved various schemes in FY 2023-24 generally aimed at improving sports activities and to prepare much needed infrastructure. It is the need of the time that the general public of the province must be given the opportunity to participate in the healthy activities in their cities / areas.

During the field visit of sports scheme usually minor issues are accounted for i.e., inferior quality of plaster work, poor workmanship due to unskilled labor and delay in handing over of the completed schemes to the local sports organizations.

A total of No of schemes 23 were visited by MEC in FY 2023-24. Out of 23 Schemes the quality of work on 19 Schemes i.e., 83% were declared satisfactory, whereas 04 Schemes i.e., 17% were declared unsatisfactory.

RECOMMENDATIONS

Keeping in view the social & cultural importance of the schemes, department Should have to expedite his vigilance to monitor the scheme on regular basis so that the designed objects would be achieved within the required time frame.

Sports Department should make sure that a framework must be developed for the proper utilization of Revenue Component.

EA should improve the quality of workmanship and concrete work at site to avoid honeycombing. Moreover, quality of formwork should be enhanced with the use of plywood.

In the light of study / survey, priority should be given to those areas/components, which are vulnerable, and needs immediate attention.

Payments may be done as per work done at site after due verification of quantities by the concerned XEN.

Smooth funding as per the allocation from the source is necessary and should be released as per the allocation.

E/A should provide all the necessary documents as indicated in the official visit letter by the MEC team.

E/A should ensure proper maintenance of completed projects.



68094804_Landhi
27/06/2024 14:20
36 22522 38 31579

WORKS & SERVICES

GENERAL FINDINGS

In the financial year 2023-24, a total of 92 schemes were visited by the MEC Department. Out of 92 Schemes the work on 74 Schemes i.e., 80% were declared satisfactory, while the work on the remaining 18 schemes i.e., 19% were declared unsatisfactory. Out of 18 Un-Satisfactory schemes, compliance of 05 schemes were received from department after rectification while compliance of 13 schemes were pending.

BUILDINGS

one of the major issues is Deviation in scope of PC-I without prior approval of the Competent Authority.

Secondly, the most common issues witnessed at sites are unevenness in plaster work i.e., proper finishing surface was not maintained.

In addition to this, Visibility of steel reinforcement due to non-provision of proper concrete cover.

Moreover, Unevenness in tile / marble flooring work is also common.

The shuttering work at most of the works was observed to be of inferior quality & needs to be improved, if possible, the steel/ply shuttering may be used.

Improper grouting in tile work

Alignment issues in beams, columns & slabs


Inferior quality of electric wiring fitting and fixtures, water supply and sanitary fixtures

Honeycombing and bleeding in structure work at specific locations due to non-availability of vibrator or poor compaction of concrete work.

ROADS

Firstly, the major issues witnessed during the monitoring phase that there is a lack of planning in design and execution of roads and drainage schemes that proper infrastructures were not provided to accommodate the sewerage and storm water separately, most of the time sewerage and storm water flows either in sewerage or drainage network resulting in choking or overflow of system during peak discharge or rainy reason.

Secondly, one of the major issues is adaptation of thumb rule method in formation phase of PC-1 completely neglecting the consideration of actual site conditions. As of result of this practice, schemes were revised due to unrealistic/approximate estimate by department at the time of preparation of PC-1. Moreover, Lack of supervision by field staff during the execution phase, frequent transfer and posting of project managers i.e., Project Director or Executive Engineer are also some core issues.

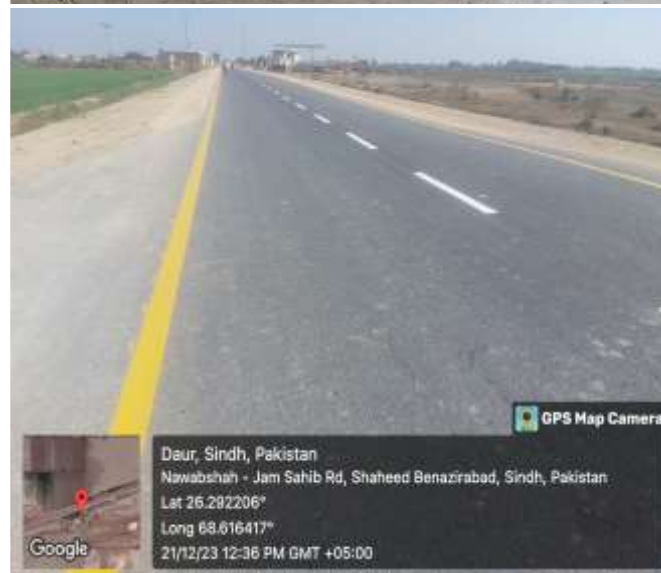

WORKS & SERVICES

Thirdly, the other main issues are inadequate allocation and releases of meager funds by the department which take years to complete the scheme and by the time scheme gets to completion, initial work gets deteriorated and there is no proper SOPs for the repair and maintenance.

Fourthly, inappropriate slope is also a core issue to be addressed as appropriate slope was not maintained in execution of road to smoothly drain the water. Due to improper drainage water remains stagnant which results in deterioration and complete failure of roads (from topmost Asphalt Layer to Embankment).

NHA/PWD/SHERE/WHO specifications not being followed properly in execution and testing of material (i.e., soil classification & gradation, bitumen quality test, field density test, compaction test, Pressure testing of pipe, strength test of concrete & steel).

RECOMMENDATIONS

The concerned Executive Engineer & Assistant Engineer should closely monitor the execution of construction work in order to improve quality of work.

There is a dire need to improve the workmanship of the contractor to meet the prescribed specification and standards.

To ensure quality execution, material testing of various materials may be carried out frequently.

To improve quality of work at construction sites, it is imperative to use of quality materials & due consideration may be given on this aspect. The contractors may be directed to obtain quality material from reputed suppliers.

The Executing Agency must ensure that work executed at sites be as per specification & approved technical sanction.

The overpayments/advance payments to contractors may be discouraged & payments be made as per quantity executed at site.

The SPPRA rules must be followed in the tendering & procurement process.

The shuttering work needs to be improved at most of the places. The use of vibrator may be used in Concreting work to avoid honey combing & attain desired strength.

The quality of D. Bs, switches, buttons & cables used in electric work may be ensured as per specification & T.S. Under-gauge steel reinforcement bars may be avoided in execution of works.

Under-gauge steel reinforcement bars may be avoided in execution of works





WAY

FORWARD



WAY FORWARD

- Overall MEC with the existing human resource was able to monitor 15% to 17% of the ADP scheme every year, which need to be enhanced and improved for quality assurance therefore it is envisaged to establish regional offices of the MEC at Divisional level
- Hiring additional Human Resource i.e. Monitoring & Evaluation Officers and procure cutting edge technology equipment and software to enhance monitoring capacity of MEC
- Third Party Monitoring mechanism is also planned and processed not only to monitor the mega projects but also to compare and introspect the work ethics and processes of the MEC monitoring team
- To develop & implement a Digitized Monthly Progress Report (MPR) System with Quick Response (QR) Code integration with Administrative Departments to enhance the timely submission of scheme progress updates
- Provide comprehensive training and development programs to all employees and equip them with cutting-edge technology which enables them to adopt modern techniques and monitoring methodologies that adhere to international standards.
- Construction of Regional Offices of M&E Cell at Karachi, Sukkur & Larkana regions through new ADP schemes
- Design an embrace an Evaluation mechanism for Completed Development Schemes



ANNEXURES



Annexure (A)

DEPARTMENT WISE SCHEMES MONITORED IN FY 2023-24

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 34	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted) (Total:30139.75 including IDA Share:18686.64, GoS Share:6120.00 & Farmers Share: 5333.11)	Un-Satisfactory	12/5/2023	Agriculture, GOS	6/28/2024	Karachi	6120
2023-24 34	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted) (Total:30139.75 including IDA Share:18686.64, GoS Share:6120.00 & Farmers Share:5333.11)	Satisfactory	11/9/2023	Agriculture, GOS	5/3/2024	Tando Muhammad Khan, Jamshoro, Hyderabad	6120
2023-24 35	Construction of Office Building for On-Farm Water Managementstaff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore & Jamshoro)	Un-Satisfactory	9/11/2023	Agriculture, GOS	5/23/2024	Dadu	96.389
2022-23 11	Construction of Additional Building Components of ATI, Jacobabad (U/R)	Un-Satisfactory	7/31/2023	Agriculture, GOS	2/14/2024	Jacobabad	99.939
2022-23 37	Construction of Office Building for On-Farm Water Managementstaff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore & Jamshoro).	Un-Satisfactory	4/17/2023	Agriculture, GOS	1/9/2024	Shaheed Benazirabad	96.389
2018-19 69	Construction of Office of the Department of Antiquities at Karachi and Sub-Offices at Jamshoro and Sukkur (Revised) (C:330.794+R:17.206) (SDG # 4,11)	Un-Satisfactory	12/11/2023	Antiquities, GOS	5/17/2024	Karachi	348
2023-24 50	Construction & Provision of Allied Facilities at Dargah Sare-Faqeer Hadi Gham Kusar Taluka Kingri District Khairpur (Revised on 17-09-2021)	Un-Satisfactory	10/30/2023	Auqaf, GOS	5/29/2024	Khairpur	95.569
2023-24 59	Construction / Repair / Renovation of Janaza Gha Bakara PeeriSingo Lane.	Satisfactory	11/20/2023	Auqaf, GOS	1/3/2024	Karachi	25
2022-23 50	Construction of Compound Wall and other Allied Facilities at Dargah & Graveyard Shaikh Tayyab Nangal District Khairpur .	Un-Satisfactory	9/12/2023	Auqaf, GOS	1/3/2024	Khairpur	8.093
2022-23 52	Rehabilitation & Reconstruction of Dargah Adham Sultan (AbuBin Abdullah) Taluka Kot Diji District Khairpur Mirs	Un-Satisfactory	9/13/2023	Auqaf, GOS	2/27/2024	Khairpur	11.95
2022-23 61	Construction / Rehabilitation of Dargah Syed Sachal Shah Bukhari village Naoabad Taluka Bakrani.	Un-Satisfactory	9/25/2023	Auqaf, GOS	5/22/2024	Larkana	15
2022-23 69	Construction of Boundary wall & Allied Facilities at Dargah Sakhi Sarwar Model Colony Airport Raod.	Satisfactory	7/11/2023	Auqaf, GOS	10/13/2023	Karachi	20
2022-23 72	Construction / Repair / Renovation of Dargah Miran PeerBaghdadi	Satisfactory	1/16/2024	Auqaf, GOS	3/28/2024	Karachi	30
2022-23 72	Construction / Repair / Renovation of Dargah Miran PeerBaghdadi.	Un-Satisfactory	5/8/2023	Auqaf, GOS	11/8/2023	Karachi	30
2022-23 77	Construction & Provision of Allied Facilities at Dargah Mian Mangho village Mian Ilyas Muhammad UC Fareedabad.	Un-Satisfactory	9/27/2023	Auqaf, GOS	5/22/2024	Larkana	15
2022-23 79	Construction & Provision of Allied Facilities at Dargah Sain Yousuf Shah Jilani UC Ratokot...	Satisfactory	9/28/2023	Auqaf, GOS	4/29/2024	Larkana	15
2022-23 79	Construction & Provision of Allied Facilities at Dargah Sain Yousuf Shah Jilani UC Ratokot.	Satisfactory	4/6/2023	Auqaf, GOS	9/12/2023	Larkana	15
2023-24 103	Missing Allied facilities of Cultural Complex at Sukkur. (Revised) 18.02.21) (C:124.650+R:53.850)	Un-Satisfactory	12/13/2023	Culture, GOS	5/29/2024	Sukkur	178.5
2023-24 111	Establishment of Auditorium at Badin. (Revised on 23.05.23) (C:160.87+R:29.130)	Satisfactory	2/12/2024	Culture, GOS	6/3/2024	Badin	190
2023-24 114	Provision of Allied Facilities at Cultural Complex Thatta. (C:64.564+R:14.941)	Satisfactory	12/5/2023	Culture, GOS	3/26/2024	Thatta	79.505
2023-24 136	Establishment & Improvement of Sambara Inn Larkano (Revised on 29.05.20) (C:127.516+R:20.308)	Satisfactory	10/25/2023	Culture, GOS	5/3/2024	Larkana	452.014
2023-24 153	Conservation & Restoration of Khudabad Masjid at District Dadu. (Revised on 15.02.23) (C:539.407)	Un-Satisfactory	11/7/2023	Culture, GOS	5/23/2024	Dadu	539.407
2018-19 69	Construction of Office of the Department of Antiquities at Karachi and Sub-Offices at Jamshoro and Sukkur (Revised) (C:330.794+R:17.206) (SDG # 4,11)	Un-Satisfactory	12/8/2023	Culture, GOS	5/31/2024	Sukkur	348
2017-18 115	Construction of Guest house for writers and artists in Hyderabad	Satisfactory	12/7/2023	Culture, GOS	6/28/2024	Hyderabad	40
2023-24 1105	Establishment of Quaid-e-Awam University of Engineering Science & Technology, Constituent College / Campus at Larkano (C:1131.925 + R:1504.983) (SDG#4)	Un-Satisfactory	11/14/2023	Education and Literacy, GOS	5/23/2024	Larkana	2636.908
2023-24 1106	Construction of Shaheed Benazir Bhutto Hostel Blocks, Security Arrangements (Electronic Equipment), Sewerage Treatment Facilities, Beautification & Improvement of QUEST at Shaheed Benazirabad	Un-Satisfactory	10/30/2023	Education and Literacy, GOS	2/26/2024	Shaheed Benazirabad	153.464
2023-24 1128	Establishment of Sufism & Modern Sciences University at Bhit Shah	Un-Satisfactory	11/15/2023	Education and Literacy, GOS	5/29/2024	Matiari	1042.776

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1133	Construction of Girls Hostel at NED University of Engineering and Technology, Karachi (C:81.750 + R:10.250) (SDG#4)	Un-Satisfactory	1/23/2024	Education and Literacy, GOS	6/28/2024	Karachi	92
2023-24 181	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	10/17/2023	Education and Literacy, GOS	5/31/2024	Sujawal	24.923
2023-24 183	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (04 Units) (SDG#4)	Satisfactory	10/18/2023	Education and Literacy, GOS	2/21/2024	Tando Allahyar	24.879
2023-24 184	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	10/19/2023	Education and Literacy, GOS	2/20/2024	Jamshoro	24.017
2023-24 186	Construction of Building for Shelterless Primary School (01 Unit) (Revised on 19.05.2023) (C: 22.392, R: 2.012) (SDG#4)	Satisfactory	10/20/2023	Education and Literacy, GOS	6/28/2024	Hyderabad	24.404
2023-24 188	Construction of Building for Shelterless Primary School (01 Unit)(C: 18.492, R: 1.379) (Revised on 19.05.2023) (SDG#4)	Satisfactory	10/23/2023	Education and Literacy, GOS	6/12/2024	Tando Allahyar	19.871
2023-24 193	Construction of Buildings for Shelterless Primary Schools 02Units) (C:35.838 + R:2.758) (Revised on 20.05.2023)(SDG#4)	Satisfactory	9/25/2023	Education and Literacy, GOS	11/10/2023	Thatta	38.596
2023-24 238	Up-gradation of Primary Schools to Elementary Schools (06 Units) (C:74.483 + R:15.192) (SDG#4)	Un-Satisfactory	1/17/2024	Education and Literacy, GOS	6/28/2024	Karachi East	89.675
2023-24 244	Construction of Building of Government Boys Lower Secondary School at Muhammad Bux Narejo Taluka Hussain Bux Mari (Revised on 23.05.2023)(SDG#4)	Satisfactory	11/8/2023	Education and Literacy, GOS	4/30/2024	Mirpurkhas	20.345
2023-24 248	Up-gradation of Girls Primary Schools to Elementary Schools at Saeed Khan Laghari & Construction of Additional Class Rooms at GBPS Saeed Khan Laghari Taluka Hala (02 Units) (SDG#4)	Satisfactory	11/30/2023	Education and Literacy, GOS	4/30/2024	Matiari	51.811
2023-24 412	Establishment of Public Schools in Sindh (05 Units) (C: 1243.851 + R: 88.760) (Revised on 20.08.09) (Re-revised on 15.07.21) (SDG#4)	Un-Satisfactory	1/2/2024	Education and Literacy, GOS	4/30/2024	Tando Muhammad Khan	2169.038
2023-24 417	Establishment of Public School at Kamber-Shahdadkot(C:544.779 + R:52.245) (Revised on 18.05.16) (SDG#4)	Un-Satisfactory	10/2/2023	Education and Literacy, GOS	4/29/2024	Qambar Shahdadkot	597.024
2023-24 420	Immediate Needs for Public School Gadap Town, Karachi (C:231.328 + R: 59.364) (SDG#4)	Un-Satisfactory	9/19/2023	Education and Literacy, GOS	1/3/2024	Karachi	290.692
2023-24 427	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.782 + R: 3.134)(SDG#4)	Un-Satisfactory	1/12/2024	Education and Literacy, GOS	5/22/2024	Matiari	42.916
2023-24 436	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (Revised on 22.05.2023)(C: Rs. 105.431 + R: 3.310) (SDG#4)	Satisfactory	3/4/2024	Education and Literacy, GOS	5/13/2024	Sukkur	108.741
2023-24 441	Construction of Girls Hostel in Public School Gadap, Karachi (C:150.227 + 10.509) (SDG#4)	Un-Satisfactory	2/22/2024	Education and Literacy, GOS	5/17/2024	Karachi Malir	160.736
2023-24 486	Re- construction of Compound Wall and other missing facilities atBahria Public School Naushahro Feroze (01 Unit) (Revised on 23.05.2023) (SDG#4)	Satisfactory	1/25/2024	Education and Literacy, GOS	6/28/2024	Naushero Feroz	52.171
2023-24 496	Provision of Missing Facilities at Government School, PAF BaseKorangi Creek(01 Unit) (SDG#4)	Un-Satisfactory	12/26/2023	Education and Literacy, GOS	3/20/2024	Karachi Malir	48.406
2023-24 713	Construction of ECE Class Rooms / Rehabilitation /Up-gradation of Various Schools of UC 1 to 19 (SDG#4) (Revised on 18.05.2023)	Satisfactory	9/20/2023	Education and Literacy, GOS	11/10/2023	Karachi South	118.827
2023-24 718	Rehabilitation & Provision of Missing Facilities in Existing GBHS Baberlo, GGHS Luqman, GBHSS Talpur Wada & GHSS FaizKotdiji (04 Units) (Revised on 22.05.2023) (SDG#4)	Satisfactory	3/8/2024	Education and Literacy, GOS	6/3/2024	Khairpur	80.87
2023-24 726	Establishment of Government Secondary School (Boys & Girls)in Chuhar Jamali Sujawal District (RGC)	Un-Satisfactory	2/27/2024	Education and Literacy, GOS	5/10/2024	Sujawal	205.5
2023-24 836	Establishment of Girls Degree College at Rohri District Sukkur(C: 152.375+ R:15.00) (SDG#4) Revised 03.01.2023	Satisfactory	3/26/2024	Education and Literacy, GOS	4/26/2024	Sukkur	167.375
2023-24 836	Establishment of Girls Degree College at Rohri District Sukkur(C: 152.375+ R:15.00) (SDG#4) Revised 03.01.2023	Un-Satisfactory	9/7/2023	Education and Literacy, GOS	1/8/2024	Sukkur	167.375
2023-24 850	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Thatta (SDG#4)	Un-Satisfactory	12/27/2023	Education and Literacy, GOS	2/13/2024	Thatta	52.08
2023-24 858	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Sukkur (SDG#4) (Revised on 08.03.2023)	Satisfactory	11/1/2023	Education and Literacy, GOS	2/16/2024	Sukkur	124.818
2023-24 867	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi West (SDG#4)	Un-Satisfactory	10/19/2023	Education and Literacy, GOS	12/19/2023	Karachi West	29.586

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 868	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi Central(SDG#4)	Satisfactory	4/23/2024	Education and Literacy, GOS	5/17/2024	Karachi Central	47.412
2023-24 868	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi Central (SDG#4)	Un-Satisfactory	11/15/2023	Education and Literacy, GOS	1/2/2024	Karachi Central	47.412
2023-24 869	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi East (SDG#4)	Un-Satisfactory	10/17/2023	Education and Literacy, GOS	1/3/2024	Karachi East	65.995
2023-24 871	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi Korangi (SDG#4)	Un-Satisfactory	11/21/2023	Education and Literacy, GOS	1/2/2024	Karachi Korangi	41.433
2023-24 872	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Keamari Karachi (SDG#4)	Satisfactory	11/22/2023	Education and Literacy, GOS	1/8/2024	Karachi Keamari	19.989
2023-24 874	Establishment of Shaheed Naseem Ahmed Kharal Government Degree College Ripri Taluka Gambat District Khairpur (SDG#4)(C: 97.325 + R: 8.620)	Satisfactory	11/7/2023	Education and Literacy, GOS	2/15/2024	Khairpur	105.945
2023-24 877	Establishment of Degree College at Shadani Hyat Pitafi TalukaMirpur Mathelo District Ghotki (SDG#4) (C: 90.946 + R: 8.690)	Un-Satisfactory	10/19/2023	Education and Literacy, GOS	2/23/2024	Ghotki	100
2023-24 887	Rehabilitation & Provision of Missing Facilities in Existing GBDC/ GGDC Naudero District Larkano (Revised on 08.03.2023)	Satisfactory	10/5/2023	Education and Literacy, GOS	6/28/2024	Larkana	113.77
2023-24 891	Establishment of Girls Degree College Ubauro District Ghotki(SDG#4) (C: 154.126 + R: 10.826)	Un-Satisfactory	9/15/2023	Education and Literacy, GOS	1/5/2024	Ghotki	164.953
2023-24 892	Establishment of Girls Degree College at New Saeedabad Taluka New Saeedabad District Matiari (SDG#4)	Un-Satisfactory	10/16/2023	Education and Literacy, GOS	4/26/2024	Matiari	98.788
2023-24 925	Construction of Building for existing Degree College Daulatpur District Sh.Benazirabad (C:88.480 + R:9.000) (SDG#4) (ADP2021-22 S. No.492)	Un-Satisfactory	10/25/2023	Education and Literacy, GOS	3/6/2024	Shaheed Benazirabad	97.48
2023-24 979	Remaining Works of Cadet College Ghotki (C:861.698 +R:67.243) (Re-Revised on 12.02.2016) (SDG#4)	Satisfactory	11/23/2023	Education and Literacy, GOS	5/6/2024	Ghotki	928.941
2023-24 988	Restoration of rain/ flood damages and Construction of female staff Hostel, Male Staff Hostel, Model school (pre Nusrary-7) and Horse Riding club at Bakhtawa Girls Cadet College Shaheed Benazirabad	Satisfactory	3/18/2024	Education and Literacy, GOS	5/9/2024	Shaheed Benazirabad	250
2023-24 990	Establishment of Special Education & Rehabilitation Complex at Tando M. Khan	Satisfactory	10/18/2023	Education and Literacy, GOS	11/23/2023	Tando Muhammad Khan	406.783
2023-24 995	Establishment of Autism Rehabilitation & Training Centre atShaheed Benazirabad (C: 86.895 + R:10.024) (SDG#4)	Satisfactory	10/26/2023	Education and Literacy, GOS	5/3/2024	Shaheed Benazirabad	96.919
2022-23 194	Construction of Buildings for Shelterless Primary Schools (05Units) (C:69.745 + R:6.895) (SDG#4)	Satisfactory	3/27/2023	Education and Literacy, GOS	11/8/2023	Naushero Feroz	76.64
2022-23 200	Construction of Buildings for Shelterless Primary Schools (03 Units) (C:42.061 + R: 4.137) (SDG#4) [First Visit]	Un-Satisfactory	7/18/2023	Education and Literacy, GOS	2/16/2024	Qambar Shahdadkot	46.198
2022-23 341	Miscellaneous Immediate Works of Public School Hyderabad(C:554.871 +R:51.189) (SDG#4).	Satisfactory	11/13/2023	Education and Literacy, GOS	1/11/2024	Hyderabad	606.06
2022-23 353	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.712 + R: 4.295) (SDG#4)	Satisfactory	7/26/2023	Education and Literacy, GOS	11/21/2023	Tando Muhammad Khan	44.007
2022-23 365	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.685 + R: 1.940) (SDG#4).	Satisfactory	11/3/2022	Education and Literacy, GOS	11/10/2023	Karachi East	109.598
2022-23 385	Up-gradation of Middle School to High School (01 Unit)(C:25.572 + R:4.091) (SDG#4)	Satisfactory	5/22/2023	Education and Literacy, GOS	10/6/2023	Karachi South	29.663
2022-23 386	Up-gradation of Middle Schools to High Schools (02 Units) (C:55.205 +R:8.182) (SDG#4)	Satisfactory	5/23/2023	Education and Literacy, GOS	11/8/2023	Karachi East	65.387
2022-23 387	Up-gradation of Middle School to High School (01 Unit)(C:25.379 + R:4.091)(SDG#4)	Satisfactory	5/24/2023	Education and Literacy, GOS	11/8/2023	Karachi Central	29.47
2022-23 420	Up-gradation of Government Girls Lower Secondary School toSecondary School at Punhal Khan Chandio (01 Unit) (SDG#4)	Satisfactory	7/25/2023	Education and Literacy, GOS	11/21/2023	Shaheed Benazirabad	56.809
2022-23 432	Rehabilitation / Renovation and Provision of Missing Facilities toexisting GBHS Ghulam Muhammad Laghari Taluka Shahdadpur (C: 34.837 + R: 6.428)	Satisfactory	4/12/2023	Education and Literacy, GOS	11/27/2023	Sanghar	41.265
2022-23 548	Rehabilitation & Provision of Missing Facilities inExisting GBPS & GBLSS Police Line and GBHS Sanghar (C:177.828 + R: 12.945) (03 Units)	Satisfactory	4/17/2023	Education and Literacy, GOS	2/13/2024	Sanghar	190.773
2022-23 688	Rehabilitation & Provision of Missing Facilities in ExistingColleges in District Karachi South(SDG#4)	Satisfactory	1/9/2024	Education and Literacy, GOS	3/28/2024	Karachi South	86.336

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 688	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi South (SDG#4)	Un-Satisfactory	3/30/2023	Education and Literacy, GOS	7/14/2023	Karachi South	86.336
2022-23 704	Addition of Class Rooms in Existing Govt. Girls Degree College Shah Nawaz Shar Gulshan Town Karachi East	Satisfactory	4/13/2023	Education and Literacy, GOS	7/18/2023	Karachi East	39.389
2022-23 748	Establishment of Special Education & Rehabilitation Complex at Tando M. Khan (SDG#4) (Director sb assignemnt)	Un-Satisfactory	6/15/2023	Education and Literacy, GOS	8/21/2023	Tando Muhammad Khan	406.783
2021-22 332	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.603 + R: 3.757)(SDG#4)	Un-Satisfactory	4/14/2022	Education and Literacy, GOS	11/10/2023	Karachi West	43.36
2021-22 341	Construction of Girls Hostel in Public School Gadap, Karachi (C:150.227 + 10.509) (SDG#4) (LTBC)	Un-Satisfactory	5/13/2022	Education and Literacy, GOS	10/5/2023	Karachi Malir	160.736
2021-22 398	Construction of Building for existing degree College @Mansoor District Matiari (01 Unit)	Un-Satisfactory	11/14/2023	Education and Literacy, GOS	5/30/2024	Matiari	86.669
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/15/2024	Energy, GOS	4/23/2024	Hyderabad	440.11
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/13/2024	Energy, GOS	4/18/2024	Matiari	440.11
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/12/2024	Energy, GOS	4/18/2024	Tando Allahyar	440.11
2022-23 884	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Un-Satisfactory	10/24/2022	Energy, GOS	1/9/2024	Tando Allahyar	440.11
2022-23 884	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Un-Satisfactory	10/21/2022	Energy, GOS	1/10/2024	Matiari	440.11
2022-23 884	Sindh Solar Energy Project (SSEP) (Total Est: CostRs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank 96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Un-Satisfactory	10/17/2022	Energy, GOS	1/10/2024	Hyderabad	440.11
2023-24 1207	Construction of Offices of Excise & Taxation in New Districts (5units)	Satisfactory	10/2/2023	Excise & Taxation, GOS	1/3/2024	Tando Allahyar	86.476
2023-24 1209	Renovation of Excise and Taxation Office Thatta (Cap: Rs.23.860 + Rev: Rs. 2.557)	Satisfactory	9/7/2023	Excise & Taxation, GOS	5/13/2024	Thatta	26.417
2021-22 701	Construction of offices of Excise & taxation in new districts(5units) (Tando allah Yar, TM Khan, Umerkot, Matiari & Jamshoro)	Satisfactory	3/24/2023	Excise & Taxation, GOS	10/17/2023	Umerkot	86
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	4/10/2023	Food, GOS	5/13/2024	Sukkur	634.843
2023-24 1227	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	10/16/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Ghotki	3016.35
2023-24 1227	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	10/10/2023	Forest, Wildlife & CDA, GOS	5/11/2024	Dadu	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	9/29/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Shaheed Benazirabad	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	9/18/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Naushero Feroz	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	9/13/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Khairpur	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m)	Satisfactory	9/5/2023	Forest, Wildlife & CDA, GOS	1/1/2024	Sukkur	3016.35
2022-23 959	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki,	Un-Satisfactory	9/18/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Naushero Feroz	708

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	N.Feroze, T.M. Khan,, Umerkot, Thar,Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG # 15)						
2022-23 959	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki, N.Feroze, T.M. Khan, Umerkot, Thar,Badin, T.A.Yar, Kamber, Larkano & Jacobabad)	Un-Satisfactory	11/28/2022	Forest, Wildlife & CDA, GOS	2/26/2024	Sujawal	708
2022-23 961	Satellite Based Mapping of Forest Areas and Follow-up Satellite Service for Implementation of Sindh Sustainable Forest Management Policy 2019 (SDG # 15)	Un-Satisfactory	7/27/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Larkana	320
2022-23 961	Satellite Based Mapping of Forest Areas and Follow-up Satellite Service for Implementation of Sindh Sustainable Forest Management Policy 2019 (SDG # 15)	Un-Satisfactory	4/10/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Ghotki	320
2020-21 548	Demarcation Reforestation & Regeneration of Vacted Forest Land (SDG 15)	Satisfactory	8/18/2023	Forest, Wildlife & CDA, GOS	11/2/2023	Hyderabad	135
2023-24 1239	Construction of Warehouse at Dr. Ruth K.M.Pfau Civil Hospital, Karachi (C: 85.368 + R: 21.397)(SDG #3, 4)	Un-Satisfactory	2/23/2024	Health, GOS	5/17/2024	Karachi	106.765
2023-24 1240	Re-construction of Underground Tank with Pumping room at NICH,Karachi (C: 44.676) (SDG #3)	Satisfactory	2/6/2024	Health, GOS	4/18/2024	Karachi	44.676
2023-24 1240	Re-construction of Underground Tank with Pumping room at NICH, Karachi (C: 44.676) (SDG #3)	Un-Satisfactory	9/18/2023	Health, GOS	11/24/2023	Karachi	44.676
2023-24 1246	Strengthening of Neonatal Intensive Care Unit at PMC Hospital, Shaheed Benazirabad.(C: 3.170 + R: 147.170)	Un-Satisfactory	9/25/2023	Health, GOS	4/29/2024	Shaheed Benazirabad	150.34
2023-24 1268	Construction of 100 bedded Hospital at PIB Colony, Karachi (C:397.710+R: 261.948)	Satisfactory	10/18/2023	Health, GOS	3/28/2024	Karachi	659.658
2023-24 1271	Establishment of Rehabilitation Centre for Burns Patients at Landhi, Karachi. (C: 149.534+R: 211.337)	Un-Satisfactory	10/16/2023	Health, GOS	1/3/2024	Karachi	360.871
2023-24 1272	Construction of Divisional Warehouse at Karachi.(C:88.930+R:5.312)(SDG #3)	Un-Satisfactory	1/11/2024	Health, GOS	5/17/2024	Karachi	94.242
2023-24 1277	Construction of 20 bedded Maternity Home at Tharo MengalGoth, District Malir, Karachi. (C:119.186+R:69.772)(SDG#3) (Revised on 09.12.22)	Un-Satisfactory	4/16/2024	Health, GOS	6/28/2024	Karachi	188.958
2023-24 1280	Establishment of Dispensaries at UC-03, New Sabzi Mandi Taluka City Hyderabad, UC-05 at New Hyderabad City and New Manthar Petrol pump Hala Naka City Hyderabad & Up gradation of BHU to 10 Bedded Mother & Child Healthcare Center UC-16at Liaquat Colony Hyd	Un-Satisfactory	11/3/2023	Health, GOS	6/7/2024	Hyderabad	48.385
2023-24 1303	Up gradation of RHC to the level of THQ/Model Hospital ChoharJamali (C:385.087 + R:105.573)	Satisfactory	2/27/2024	Health, GOS	4/18/2024	Sujawal	490.66
2023-24 1316	Up gradation of BHU to RHC at Khanwahan(C:62.422+R:32.818)(SDG# 3)	Satisfactory	11/22/2023	Health, GOS	4/24/2024	Naushero Feroz	95.24
2023-24 1358	Up-gradation of THQ Hospital to the level of DHQ Hospital (03Nos) at Matiari, Qamber & Umerkot	Un-Satisfactory	11/13/2023	Health, GOS	5/29/2024	Matiari	2483.861
2023-24 1444	Establishment of Nursing & Paramedical School at Syed Abdullah Shah Institute of Medical Sciences, SehwanSharif (SDG #3,4,6) (C: 357.653 M + R: 68.554m)	Satisfactory	11/20/2023	Health, GOS	5/14/2024	Jamshoro	426.207
2022-23 1006	Construction of 50 bedded hospital at Gulshan-e-Hadeed, Malir,Karachi (C:191.994+R:81.161) (SDG#3)	Satisfactory	5/11/2023	Health, GOS	11/22/2023	Karachi	273.155
2022-23 1016	Construction of Divisional Warehouse at Sukkur.(C:88.930+R:5.312)(SDG#3)	Un-Satisfactory	4/10/2023	Health, GOS	1/11/2024	Sukkur	94.242
2022-23 1022	Construction of Diagnostic Centre with OPD/Referral services at Village Adur Narejo, UC Golo Wahan, Taluka Gambat, DistrictKhairpur (Revised on 05.01.21)(C:37.611+R:13.342) (SDG #3)	Un-Satisfactory	7/10/2023	Health, GOS	1/10/2024	Khairpur	50.953
2022-23 1035	Establishment of THQ Hospital at Ghorabari (C:342.609 +R:99.047) (SDG #3)	Satisfactory	8/23/2022	Health, GOS	2/13/2024	Thatta	441.656
2022-23 1036	Renovation and Rehabilitation of Paramedical Institute, Larkano.(C: 47.948+R: 19.785) (SDG #3)	Un-Satisfactory	3/10/2023	Health, GOS	12/1/2023	Larkana	67.733
2022-23 1038	Establishment of Thalassemia Day Care Centre at Dargah JaralShah, Larkano. (C:13.224+R:8.762)	Un-Satisfactory	7/26/2023	Health, GOS	4/3/2024	Larkana	21.986
2022-23 1079	Up gradation of Health facility at Village Ber Sharif, Taluka Kamber.	Un-Satisfactory	3/17/2023	Health, GOS	5/22/2024	Qambar Shahdadkot	13.495
2022-23 1085	Expansion & Improvement of DHQ Hospitals (06 Nos) at Thatta, Dadu, N. Feroze, Mirpurkhas, Sanghar & Mirpur Mathelo at Ghotki (Revised on 07.11.17).(C: 2749.885+R: 2114.021) (SDG#3)	Satisfactory	10/10/2022	Health, GOS	7/6/2023	Thatta	4863.906
2022-23 1086	Up gradation of THQ Hospitals to the level of DHQ Hospitals (03 Nos) at Matiari, Kamber & Umerkot (Revised on 22.01.16).(C: 1875.856+R: 608.005)	Satisfactory	8/11/2023	Health, GOS	10/6/2023	Umerkot	2483.861
2022-23 1086	Up gradation of THQ Hospitals to the level of DHQ Hospitals (03 Nos) at Matiari, Kamber & Umerkot (Revised on 22.01.16).(C: 1875.856+R: 608.005)	Un-Satisfactory	3/9/2023	Health, GOS	7/6/2023	Umerkot	2483.861
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285)	Un-Satisfactory	3/8/2023	Health, GOS	7/10/2023	Qambar Shahdadkot	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.).	Un-Satisfactory	3/7/2023	Health, GOS	7/10/2023	Shikarpur	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285)	Un-Satisfactory	3/7/2023	Health, GOS	7/10/2023	Jacobabad	3334.161

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Qambar Shahdadkot.	Un-Satisfactory	11/24/2022	Health, GOS	11/14/2023	Qambar Shahdadkot	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	11/23/2022	Health, GOS	1/10/2024	Sujawal	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Gari Kharo & Thull.	Un-Satisfactory	11/23/2022	Health, GOS	11/13/2023	Jacobabad	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285). Johi, K.Nshah & Mehar.	Un-Satisfactory	11/22/2022	Health, GOS	11/13/2023	Dadu	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	11/21/2022	Health, GOS	7/6/2023	Matiari	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Ratodero & Dokri.	Un-Satisfactory	11/21/2022	Health, GOS	11/14/2023	Larkana	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Lakhi Ghulam & Garhi Yaseen.	Un-Satisfactory	11/21/2022	Health, GOS	11/13/2023	Shikarpur	3334.161
2022-23 1181	Establishment of Child Health Care Institute Sukkur (Revised on 01.02.21) (GoS:162.792+Korean soft loan: 6386.547-6549.339)(SDG #3)	Satisfactory	3/22/2023	Health, GOS	9/12/2023	Sukkur	162.792
2022-23 970	Construction of Warehouse at Dr. Ruth K.M.Pfau Civil Hospital, Karachi (C: 85.368 + R: 21.397) (SDG #3, 4)	Un-Satisfactory	7/20/2023	Health, GOS	11/24/2023	Karachi	106.765
2021-22 737	Establishment of Gastroenterology & Neuropsychiatry unit at NICH, Karachi.	Satisfactory	9/14/2022	Health, GOS	2/13/2024	Karachi	103.109
2021-22 771	Construction of Divisional Warehouse at Karachi. (C:88.930+R:5.312)(LTBC)	Un-Satisfactory	5/18/2022	Health, GOS	8/17/2023	Karachi	94.242
Non-ADP	Up-gradation to the level of RHC at Unerpur (Ward Block / OPDBlock) Taluka Manjhand District Jamshoro	Un-Satisfactory	8/17/2023	Health, GOS	12/19/2023	Jamshoro	20
2023-24 1466	Construction of Special Investigation Complex for 10 Nos Police Station	Un-Satisfactory	10/9/2023	Home, GOS	12/7/2023	Karachi	134.584
2023-24 1467	Improvement / Strengthening of Security to SBB ATIRazzakabad Karachi (Construction of RCC Compound Wall 15 height with Watch Towers)	Satisfactory	12/11/2023	Home, GOS	3/27/2024	Karachi	433.126
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	2/29/2024	Home, GOS	5/14/2024	Ghotki	292.136
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	2/21/2024	Home, GOS	5/13/2024	Shaheed Benazirabad	292.136
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	1/26/2024	Home, GOS	6/28/2024	Naushero Feroz	292.136
2023-24 1509	Establishment of Forensic Laboratory in Sindh at Karachi (SDG# 16) (Revised on 21-04-2022)	Satisfactory	10/16/2023	Home, GOS	11/24/2023	Karachi	5426.409
2023-24 1561	Construction of Residences for Anti-Terrorism Courts Judges, Prisons Officers / Staff at Central Prison Karachi (SDG # 16)	Satisfactory	12/15/2023	Home, GOS	12/19/2023	Karachi	890.848
2022-23 1188	Construction of Buildings for Sindh Police at various locations under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, Shaheed Benazir Abad, Kamber & Sukkur)(Revised) (SDG # 16)..	Satisfactory	5/19/2023	Home, GOS	11/27/2023	Hyderabad	642.101
2022-23 1208	Construction of Police Station (Category-C) & Bachelor Barracks (Ground + 1) at Nindo District Badin (859 of 2017-18) (Remaining work).	Satisfactory	3/13/2023	Home, GOS	10/18/2023	Badin	37.198
2022-23 1236	Construction of new Watch Towers (10) Nos including construction of consultant, Jailor & Record Rooms, external lavatory blocks and replacement of various roofs of barracks at Central Prison Karachi.	Satisfactory	7/12/2023	Home, GOS	10/6/2023	Karachi	53.132
2022-23 1242	Construction of Affidavit Centre, Pray Area, General Bathroom, Bar Room, Library, Prosecutor Chamber, and Public Cafeteria at ATC Courts, Central Prison, Karachi.	Satisfactory	7/13/2023	Home, GOS	10/10/2023	Karachi	98.109
2021-22 909	Improvement / Strengthening of Security to SCTC Sakrand (Compound Wall with Watch Towers) (SDG # 16)	Satisfactory	3/14/2023	Home, GOS	4/24/2024	Shaheed Benazirabad	48.629
2021-22 917	construction of Polce Station Building at PS Dehi (SDG No. 16)	Satisfactory	4/26/2023	Home, GOS	2/26/2024	Badin	34.1
2023-24 1567	Human Rights Complaint Management System (R: 80.362)(Revised on 10.05.23)(SDG # 10 & 16)	Un-Satisfactory	2/1/2024	Human Rights, GOS	2/14/2024	Karachi South	80.362
2023-24 1567	Human Rights Complaint Management System (R: 80.362)(Revised on 10.05.23)(SDG # 10 & 16)	Un-Satisfactory	9/6/2023	Human Rights, GOS	12/20/2023	Karachi South	80.362
2022-23 1281	Provision of basic facilities of Sewerage / CC Drain / CC topping in different Katchi Abadis in Sindh	Un-Satisfactory	12/7/2023	Human Settlement, Spatial Development & Social Housing	5/17/2024	Karachi	40

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1578	Improvement of Basic Infrastructure at Industrial Park, ShershahKarachi (4.68 acre land)	Satisfactory	2/15/2024	Industrial & Commerce, GOS	5/13/2024	Karachi	49.11
2023-24 1592	Rehabilitation of Infrastructure and Development at S.I.T.E.Sukkur	Un-Satisfactory	10/11/2023	Industrial & Commerce, GOS	3/8/2024	Sukkur	439.366
2022-23 1315	Establishment of Museum of Antique Printing & Allied Machinesin Sindh Government Press, Karachi. (Revised on 24.09.21)	Un-Satisfactory	4/14/2023	Industrial & Commerce, GOS	12/19/2023	Karachi	89.557
2021-22 992	Construction of District Information office at Matiari (C:11.982+R: 01.762)	Satisfactory	6/7/2022	Information & Archives, GOS	1/3/2024	Matiari	13.744
2021-22 995	Construction of District Information office at Thatta (C:11.138+R: 01.762)(LTBC) (As per request of the department)	Satisfactory	6/9/2022	Information & Archives, GOS	11/24/2023	Thatta	12.9
2023-24 1638	Boring & Installation of 250 Nos Tubewells of 2.0 Cusecs onSolar Energy (SDG # 6)	Un-Satisfactory	12/13/2023	Irrigation (Water & Drainage), GOS	5/29/2024	Sukkur	2087.11
2023-24 1667	Construction of Sub-Drain parallel to Nara Canal from RD-450.0to 574 (Revised on 22.05.23)	Un-Satisfactory	12/11/2023	Irrigation (Water & Drainage), GOS	5/10/2024	Khairpur	598.579
2023-24 1670	Construction of Tubewells & Pumping Stations on Solar EnergySystem of Drainage Division SBA.	Un-Satisfactory	10/23/2023	Irrigation (Water & Drainage), GOS	5/2/2024	Shaheed Benazirabad	498.228
2023-24 1678	Rehabilitation and Improvement of Left Bank Outfall DrainageSystem (Inland LBOD System)	Un-Satisfactory	12/14/2023	Irrigation (Water & Drainage), GOS	5/31/2024	Sanghar	4416.134
2023-24 1686	Installation Tubewells of 06 Villages of U.Cs Soomar Khan, Gupchani, Jhooro Khan Shar and Abdul Hassan: Village Zahid Ali Jamali, Deh 14 Nasrat, UC Soomar Khan, Village Nawab Khan Brohi, Deh 14 Nasrat, U.C Soomar Khan, Village MeerMahar, U.C Soomar Khan	Satisfactory	1/30/2024	Irrigation (Water & Drainage), GOS	6/10/2024	Shaheed Benazirabad	51.766
2023-24 1718	CC Lining of Shah Nawaz Wah from RD-0.0 to 53, Rahuja MinorRD-9+5 to 25+0, Kanasera Minor, Junki Minor, and Retaining Wall along Faiz Wah - Revised on 29.05.20 (SDG # 6)	Un-Satisfactory	12/12/2023	Irrigation (Water & Drainage), GOS	5/13/2024	Khairpur	694.412
2023-24 1732	Constructing Stone Pitching at RD-9+00 to 15+00 RMC B/S and Downstream Fall Structure 16, 17, 18, 19 & 20 B/Sides (Revised22-02-22).	Un-Satisfactory	9/8/2023	Irrigation (Water & Drainage), GOS	4/25/2024	Sukkur	378.078
2023-24 1761	Construction of J- Spurs U/S Left Guide Bank to Centralize theFlow of Indus River Water under Thatta Sujawal Road Bridge (Doolah Bridge) in Kalri Baghar Division Thatta	Satisfactory	3/7/2024	Irrigation (Water & Drainage), GOS	5/10/2024	Thatta	1947.576
2023-24 1761	Construction of J- Spurs U/S Left Guide Bank to Centralize theFlow of Indus River Water under Thatta Sujawal Road Bridge (Doolah Bridge) in Kalri Baghar Division Thatta.	Satisfactory	12/7/2023	Irrigation (Water & Drainage), GOS	1/11/2024	Thatta	1947.576
2023-24 1763	Construction of C.C. Lining from Head to Tail of Pubjo Minor &Kazi Ahmed Minor including allied structures in Dad Division.	Un-Satisfactory	9/28/2023	Irrigation (Water & Drainage), GOS	2/21/2024	Shaheed Benazirabad	418.335
2023-24 1782	C.C. Lining of Sultani Branch & its 6 Nos. off-taking channels.	Satisfactory	11/13/2023	Irrigation (Water & Drainage), GOS	5/9/2024	Badin	2342.5
2023-24 1798	Construction of New Road Bridge over Kalri Baghar FeederUpper at RD-120	Satisfactory	11/21/2023	Irrigation (Water & Drainage), GOS	2/14/2024	Thatta	116.574
2022-23 1420	Providing Stone Pitching along PFL RD 120 to 130 IP side RD 135 to 140 NIP side, RD 152 to 160 and 161 to 163 NIP side Village Abral and Re- Sectioning of Gunj Bahar Branch and Repair of Head Regulator, Road Bridge, dumping of stonepitching and Rehabilita	Un-Satisfactory	10/3/2022	Irrigation (Water & Drainage), GOS	1/9/2024	Tando Muhammad Khan, Sujawal	679.9
2022-23 1434	Renovation / Re-Construction of road Bridge over Mirwah Canal at RD-33 near Railway Station Begmangi, Installation of Steel grill over Retaining Wall along Mirwah Canal B/S RD-69 to 79, 70+200, 72+180, 73+450, 74+200, 75+150, 76+200, 77+15 &78+570 Both	Satisfactory	4/7/2023	Irrigation (Water & Drainage), GOS	10/18/2023	Khairpur	450.271
2022-23 1446	Constructinn Stone Pitching along RMC from RD-25 to 191.2 @Eroded Portion. (Revised on 23.02.22)	Un-Satisfactory	4/28/2023	Irrigation (Water & Drainage), GOS	9/12/2023	Khairpur	339.006
2019-20 939	Rehabilitation of Sub Drain M.I.L & Resectioning of MirpurkhasMain Drain	Satisfactory	1/23/2024	Irrigation (Water & Drainage), GOS	6/7/2024	Mirpurkhas	83.377
2023-24 1857	Revamping & Rehabilitation of Occupational Safety & HealthCentre at Karachi	Satisfactory	12/19/2023	Labour Dept, GOS	3/27/2024	Karachi	22.302
2022-23 1591	Construction of Record Room alongwith Store Room & Provision of Elevator / Lift Facilities and Construction of Cafeteria at HighCourt Circuit, Larkana(Cap: 57.00 + Rev: 2.100)	Satisfactory	3/13/2023	Law P.A, & Prosecution	7/13/2023	Larkana	59.1
2022-23 1592	Construction of Bar Room, Bar Library and Additional ten (10)No. Courts at District Court Building, Malir(Cap: 241.368 + Rev: 39.373)	Satisfactory	3/21/2023	Law P.A, & Prosecution	10/5/2023	Karachi Malir	280.741
2023-24 1924	C.C Lining of Jiskani Distry-I from RD- 000 to 46+500 RDs (SDG# 6)	Satisfactory	9/29/2023	Lining of Main Canals	5/10/2024	Shaheed Benazirabad	349.524

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1926	C.C Lining of Lundki from RD-00 to Tail and Gachero Minor from RD-00 to 14+500 (SDG # 6)	Satisfactory	11/30/2023	Lining of Main Canals	5/13/2024	Shaheed Benazirabad, Naushero Feroz	841.094
2023-24 1930	Cement Concrete Lining of Kunner- II Distry from RD-0+000 toRD-21+000 (SDG # 6) (Revised on 10.05.23)	Satisfactory	4/22/2024	Lining of Main Canals	6/28/2024	Hyderabad	517.143
2023-24 1936	Cement Concrete Lining from Head to Tail of Karampur Distryand Ghar Marho Distry (SDG # 6)	Un-Satisfactory	11/27/2023	Lining of Main Canals	3/20/2024	Thatta	376.338
2023-24 1939	Cement Concrete Lining from Head to Tail of Ghar Machi Minor,Hala Minor, Sonada Distry	Satisfactory	5/13/2024	Lining of Main Canals	5/23/2024	Thatta	414.892
2023-24 1939	Cement Concrete Lining from Head to Tail of Ghar Machi Minor,Hala Minor, Sonada Distry (SDG # 6)	Un-Satisfactory	11/22/2023	Lining of Main Canals	3/20/2024	Thatta	414.892
2023-24 1947	C.C Lining Along Faiz Ganj Wah 80 to 163+ / CC Lining ofHalepota Minor from RD-0+00 to 9+400 & CC Lining of Ali Nawaz Wah from RD.64+ to 139+200 (SDG # 6)	Satisfactory	9/11/2023	Lining of Main Canals	3/6/2024	Khairpur	1177.139
2023-24 1960	C.C Lining Khairpur Feeder East Canal RD-12.8 to 42.8 (SDG #6)	Satisfactory	12/12/2023	Lining of Main Canals	5/14/2024	Khairpur	1200
2023-24 1964	Construction of C.C. Lining of Let Minor from RD-0+00 to 59+00and Poran Minor RD - 0+00 to 13+800	Satisfactory	12/22/2023	Lining of Main Canals	5/14/2024	Naushero Feroz	475
2022-23 1609	C.C Lining of Menglo Minor from RD- 0.000 to 38+200 (SDG #6)	Satisfactory	7/25/2023	Lining of Main Canals	11/23/2023	Naushero Feroz	227.702
2022-23 1612	Cement Concrete Lining along Dalipota -Minor from RD-0+000 to45+100 (SDG # 6)	Satisfactory	7/24/2023	Lining of Main Canals	2/21/2024	Naushero Feroz	265.5
2022-23 1614	Cement Concrete Lining of Kunner- II Distry from RD-0+000 toRD-21+000 (SDG # 6)	Un-Satisfactory	7/25/2023	Lining of Main Canals	2/27/2024	Hyderabad	517.143
2022-23 1625	Cement Concrete Lining along Padhar Minor from RD-0+00 to43+350 (SDG # 6)	Satisfactory	11/25/2022	Lining of Main Canals	11/23/2023	Badin	278.787
2023-24 1979	Establishment of Veterinary Centres in Sindh - Phase-II (SBA,Shikarpur, Tharparkar, T.M.Khan, Larkano, Ghotki, Dadu & Khairpur) (C:69.614 + R:30.250) (SDG # 2)	Satisfactory	10/19/2023	Livestock and Fisheries, GOS	4/30/2024	Larkana, Dadu	99.864
2023-24 1982	Save Buffalo Calves (Karachi, Badin, Hyderabad, Dadu,Sukkur, Khairpur, Ghotki, Larkano, Kamber at S. Kot, Kashmir at K. Kot, Shikarpur & Jacobabad) (R:407.878) (SDG #7)..	Un-Satisfactory	1/5/2024	Livestock and Fisheries, GOS	4/16/2024	Shikarpur, Jacobabad	407.878
2023-24 1982	Save Buffalo Calves (Karachi, Badin, Hyderabad, Dadu,Sukkur, Khairpur, Ghotki, Larkano, Kamber at S. Kot, Kashmir at K. Kot, Shikarpur & Jacobabad) (R:407.878) (SDG #7)	Un-Satisfactory	12/5/2023	Livestock and Fisheries, GOS	5/17/2024	Qambar Shahdadkot, Larkana	407.878
2023-24 1983	Fattening of Calves (Jamshoro, SBA, Dadu, Sukkur, Khairpur,Ghotki, Larkano, Kamber at S.Kot, Kashmir at K.Kot, Shikarpur & Jacobabad) (R:222.110) (SDG #2)	Satisfactory	10/24/2023	Livestock and Fisheries, GOS	4/2/2024	Jamshoro	222.11
2023-24 1998	Rehabilitation & Renovation of Karachi Fish Harbour - External Services(2nd revised on 21.03.18) (C: 1374.147 +R: 242.237)(SDG #14)	Un-Satisfactory	1/4/2024	Livestock and Fisheries, GOS	1/17/2024	Karachi	1616.384
2023-24 1998	Rehabilitation & Renovation of Karachi Fish Harbour - ExternalServices (2nd revised on 21.03.18) (C: 1374.147 +R: 242.237) (SDG #14)	Un-Satisfactory	10/5/2023	Livestock and Fisheries, GOS	12/19/2023	Karachi	1616.384
2022-23 1658	Establishment of Sindh Institute of Animal Health atKarachi(C:176.199 + R.40.780) (SDG #13)	Satisfactory	7/11/2023	Livestock and Fisheries, GOS	3/27/2024	Karachi	631.798
2022-23 1660	Switching Traditional / Conventional Livestock Farming toContemporary (R:131.970) (SDG #2)	Satisfactory	7/20/2023	Livestock and Fisheries, GOS	11/8/2023	Dadu	131.97
2022-23 1660	Switching Traditional / Conventional Livestock Farming toContemporary (R:131.970) (SDG #2))	Satisfactory	7/13/2023	Livestock and Fisheries, GOS	11/29/2023	Ghotki	131.97
2022-23 1660	Switching Traditional / Conventional Livestock Farming toContemporary (R:131.970) (SDG #2)	Satisfactory	4/5/2023	Livestock and Fisheries, GOS	9/12/2023	Larkana	131.97
2022-23 1661	Establishment of Rural / Backyard Poultry farming in DistrictGhotki & Larkano (R: 99.995) (SDG #2)	Satisfactory	7/21/2023	Livestock and Fisheries, GOS	4/17/2024	Larkana	99.995
2022-23 1663	Fattening of Calves (R:222.110) (Jamshoro, SBA, Dadu, Sukkur,Khairpur, Ghotki, Larkano, Kamber at S.Kot, Kashmir at K.Kot, Shikarpur & Jacobabad (SDG #2).	Un-Satisfactory	3/28/2023	Livestock and Fisheries, GOS	8/25/2023	Jamshoro	222.11
2022-23 1687	Introduction of Bio-Floc Aquaculture in Sindh (Jamshoro, Thatta,Badin, Sujawal, TM Khan, Ghotki & Larkana) (R: 100.000) (SDG #2)..	Satisfactory	10/20/2023	Livestock and Fisheries, GOS	4/17/2024	Larkana	100
2023-24 2031	Up-gradation of old and new Pumping stations of Gharo, DistrictThatta	Un-Satisfactory	10/11/2023	Local Government, GOS	12/7/2023	Thatta	329.736
2023-24 2065	Improvement of Water supply line and Installation of Sewerageline and Paver Block, Road Carpeting in UC-38	Un-Satisfactory	2/12/2024	Local Government, GOS	6/4/2024	Karachi West	170.26
2023-24 2065	Improvement of Water supply line and Installation of Sewerageline and Paver Block, Road Carpeting in UC-38.	Un-Satisfactory	10/10/2023	Local Government, GOS	12/19/2023	Karachi West	170.26
2023-24 2066	Improvement of Water supply line and Installation of Sewerageline and Paver Block, Road Carpeting in UC-39.	Un-Satisfactory	11/13/2023	Local Government, GOS	1/3/2024	Karachi West	173.518

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 2078	Rehabilitation / Improvement of Road / Sewerage Line & WaterSystem	Un-Satisfactory	12/12/2023	Local Government, GOS	3/20/2024	Karachi Korangi	96.805
2023-24 2091	Rehabilitation of Drainage Works & Construction of New CCflooding in Village Ber Sharif, Taluka Kamber (Revised) (SDG#6)	Satisfactory	1/15/2024	Local Government, GOS	6/5/2024	Qambar Shahdadkot	99.682
2023-24 2094	Widening/Reconditioning of asphalt Concrete Road from Main City gatge Chuhar Jamali Road to by-pass Chowk shah Aqeeq Road Via Main City Road including RCC Drain Nala/C.C PaverBlock Taluka Chuhar Jamali District Sujawal	Un-Satisfactory	2/28/2024	Local Government, GOS	5/10/2024	Sujawal	424.447
2023-24 2104	Providing & Laying of C.C Paver & Drainage at Village Retti/NewRetti, Taluka Ubauro, District Ghotki @ Mirpur Mathelo	Satisfactory	3/13/2024	Local Government, GOS	6/4/2024	Ghotki	94.103
2023-24 2457	Construction of Civic Centre at Mula Fazal Auditorium HallChawkiwara Road Lyari	Satisfactory	1/11/2024	Local Government, GOS	6/28/2024	Karachi	434.627
2023-24 2484	Construction of Dumlottee Road from Dumlottee Well to M-9 &M-5 Link Road (12.3 Km)	Satisfactory	1/16/2024	Local Government, GOS	3/28/2024	Karachi	798.323
2023-24 2486	Reconditioning of road from Majeed Kerio- Mehrabpur road to VillDado Gohram Faqeer Zardari, UC Marvi, Taluka Sakrand Mile 0/0-3/5 (5.80 Km) (Revised on 03.01.23)	Satisfactory	11/27/2023	Local Government, GOS	5/2/2024	Shaheed Benazirabad	167.79
2023-24 2505	Construction of roads alongwith drainage, Sewerage,Pipes andpaving blocks in UC-2 Muslimabad, Malir Karachi	Un-Satisfactory	3/4/2024	Local Government, GOS	6/4/2024	Karachi Malir	118.3
2023-24 2505	Construction of roads alongwith drainage, Sewerage, Pipes andpaving blocks in UC-2 Muslimabad, Malir Karachi	Un-Satisfactory	10/5/2023	Local Government, GOS	12/19/2023	Karachi Malir	118.3
2023-24 2506	Improvement & Reconstruction of Roads in UC-36, 35,30Fishermen Chowrangi to Nasir Colony	Un-Satisfactory	2/13/2024	Local Government, GOS	6/4/2024	Karachi Korangi	157
2023-24 2506	Improvement & Reconstruction of Roads in UC-36, 35, 30Fishermen Chowrangi to Nasir Colony	Un-Satisfactory	10/18/2023	Local Government, GOS	12/19/2023	Karachi Korangi	157
2023-24 2517	Construction of road village Abdul Kareem Lashari, Construction of road village Mubarak Lashari, Construction of road village Muhammad Khan Katiyar, Construction of road village Mitho Lashari to Ragwah Mori, Construction of main road Ghulamullahto Dargah	Worst	10/10/2023	Local Government, GOS	11/24/2023	Thatta	63.5
2023-24 2520	Construction of Bridge Over Malir Nadi near Goth Siddiquejokhio, UC Choohar, District Malir Karachi	Un-Satisfactory	12/15/2023	Local Government, GOS	5/17/2024	Karachi Malir	175
2023-24 2523	Rehabilitation and Reconstruction of Roads & Laying of CCflooding / Paver Block at different areas of PS-97	Satisfactory	11/14/2023	Local Government, GOS	3/28/2024	Karachi Korangi	147.75
2023-24 2524	Improvement & Reconstruction of Roads in UC-37 Ward 1	Un-Satisfactory	11/3/2023	Local Government, GOS	12/19/2023	Karachi Korangi	81.007
2023-24 2530	Rehabilitation of road Mewa Shah Graveyard & surroundingarea of District West	Satisfactory	2/15/2024	Local Government, GOS	2/28/2024	Karachi West	200.92
2023-24 2621	Construction of internal road of Shah Inayat Village KiranHospital Road PS100	Un-Satisfactory	3/12/2024	Local Government, GOS	5/17/2024	Karachi East	29.895
2023-24 2621	Construction of internal road of Shah Inayat village KiranHospital Road PS-100	Un-Satisfactory	11/2/2023	Local Government, GOS	1/2/2024	Karachi East	29.895
2023-24 2624	Dualization of road 15 Check post G.T. Road to War MubarakTaluka Rohri	Un-Satisfactory	11/14/2023	Local Government, GOS	2/23/2024	Sukkur	80
2023-24 2625	Widening / Reconditioning of Road from Sukkur Barrage toRohri City (Dual carriageway)	Satisfactory	5/10/2024	Local Government, GOS	5/27/2024	Sukkur	495
2023-24 2625	Widening / Reconditioning of Road from Sukkur Barrage toRohri City (Dual carriageway)	Un-Satisfactory	11/2/2023	Local Government, GOS	2/12/2024	Sukkur	495
2023-24 2791	Constt: of 05 Nos. Union Council Offices in PS-73(C:40.000+R:5.000) (SDG # 11)	Un-Satisfactory	11/15/2023	Local Government, GOS	4/26/2024	Jamshoro	45
2023-24 2792	Establishment of Theme Park at Khairpur City (Revised on12.08.21)	Un-Satisfactory	11/17/2023	Local Government, GOS	5/29/2024	Khairpur	198.195
2023-24 2797	Development of Ghazi Abdul Rasheed Park Sukkur	Satisfactory	10/12/2023	Local Government, GOS	4/24/2024	Sukkur	199.998
2023-24 2798	Establishment of Dispensaries & Parks and Grounds in DifferentUCs of NA-249	Un-Satisfactory	10/12/2023	Local Government, GOS	12/19/2023	Karachi Keamari	195.364
2023-24 2799	Rehabilitation of Grounds & Parks, Eid Gah Ground Ward-2, Railway Ground Ward-3, Qalandari Ground Ward-7, Park in Railway Colony Bulbul Barrick Ward-3	Un-Satisfactory	10/20/2023	Local Government, GOS	12/20/2023	Karachi South	132.477

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
	Park in Chandio village Adjoued to Dada Bhai village, Park in Kaleem Qazi Ground Ward-7						
2023-24 2800	Rehabilitation of Public Parks and Public Grounds, UC-16, 19,24 & UC-26, District West Karachi	Un-Satisfactory	12/18/2023	Local Government, GOS	3/20/2024	Karachi West	80
2023-24 2803	Rehabilitation & Beautification of Different Areas of Rohri City District Sukkur	Satisfactory	2/12/2024	Local Government, GOS	5/20/2024	Sukkur	99.81
2023-24 2823	Installation, Upgradation & Automation of existing Traffic Signals in Karachi and Beautification of Shahra-e-Faisal and Adjacent areas of Karachi	Satisfactory	1/15/2024	Local Government, GOS	5/13/2024	Karachi	198.7
2023-24 2824	Establishment of Zoological Park at Khairpur (Ph-II) (SDG#8)(ADP #1419 of 2020-21)	Un-Satisfactory	11/10/2023	Local Government, GOS	2/13/2024	Khairpur	54.827
2022-23 1713	Rehabilitaioion of the existing distribution system in Hyderabad(Providing Lyaing Jointing & Testing 4	Satisfactory	7/5/2023	Local Government, GOS	11/23/2023	Hyderabad	399.747
2022-23 1715	CC Block Roads in Various Villages of Qasimabad PS-47 (SDG# 9)	Satisfactory	11/11/2022	Local Government, GOS	11/2/2023	Hyderabad	299
2022-23 1717	Improvement & Enhancement of Sewerage System in Taluka City Area District Hyderabad	Satisfactory	7/6/2023	Local Government, GOS	11/23/2023	Hyderabad	414.135
2022-23 1729	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage System including Pumping Stations in District Central, Karachi	Satisfactory	10/3/2023	Local Government, GOS	11/10/2023	Karachi	149.978
2022-23 1730	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District South, Karachi	Satisfactory	6/19/2023	Local Government, GOS	10/6/2023	Karachi	133.771
2022-23 1735	Construction of Cover Drain/Repair of exisitbg Drain Ward No.1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur	Satisfactory	5/2/2024	Local Government, GOS	5/27/2024	Sukkur	82.797
2022-23 1735	Construction of Cover Drain/Repair of exisitbg Drain Ward No.1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur	Un-Satisfactory	4/12/2023	Local Government, GOS	12/6/2023	Sukkur	82.797
2022-23 1748	Construction / Rehabilitation of Main / Internal Roads, providing, sewerage line of 12 dia PE Pipe and installation of Paver blocks/ CC flooring & Street Lights in Jannat Gul Town, Al-Azam Town, Qayyum Abad, Hasan Noman Colony, Machar Colony, Allah Bux G	Satisfactory	11/9/2022	Local Government, GOS	10/13/2023	Karachi East	96.466
2022-23 1750	Construction / Rehabilitation of Main / Internal Roads, Providing Sewerage line of 12	Un-Satisfactory	5/30/2023	Local Government, GOS	12/19/2023	Karachi East	98.666
2022-23 1755	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12	Satisfactory	11/11/2022	Local Government, GOS	7/17/2023	Karachi East	96.17
2022-23 1757	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12	Satisfactory	11/14/2022	Local Government, GOS	7/17/2023	Karachi East	100
2022-23 1761	Construction of Double Road from Pehlwan Goth to Johar Police Station Gulistan-e-Johar including street lights, footpath with paving blocks, Cat eyes road markings including Sewerage line of 12	Un-Satisfactory	4/3/2023	Local Government, GOS	1/8/2024	Karachi East	98.881
2022-23 1762	Construction of Road & Installation of Paver Blocks, Sewerage & Water Supply Line, Akhtar Colony & Kashmir Colony (UC-01)	Un-Satisfactory	1/8/2024	Local Government, GOS	5/13/2024	Karachi East	98.608
2022-23 1762	Construction of Road & Installation of Paver Blocks, Sewerage & Water Supply Line, Akhtar Colony & Kashmir Colony (UC-01)	Un-Satisfactory	11/30/2022	Local Government, GOS	10/6/2023	Karachi East	98.608
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Satisfactory	5/26/2023	Local Government, GOS	10/10/2023	Karachi East	84.749
2022-23 1767	Providing and laying of Water Supply 4	Satisfactory	4/5/2023	Local Government, GOS	10/10/2023	Karachi East	89.893
2022-23 1783	CC Flooring, Sewerage Line, Water Supply Line & Establishment of Basic Health Center (Dispensary) in UC-II Baloch Goth.	Satisfactory	3/20/2023	Local Government, GOS	7/18/2023	Karachi West	122.284
2022-23 1787	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-17, UC-27 & UC-28	Satisfactory	6/13/2023	Local Government, GOS	7/6/2023	Karachi West	117.577
2022-23 1789	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-20, UC-21 & UC-22.	Satisfactory	4/10/2023	Local Government, GOS	7/17/2023	Karachi West	86.039
2022-23 1791	Construction of Roads, laying of Paver Blocks, Installation of Sewerage System in UC-16, Ghaziabad	Un-Satisfactory	12/19/2022	Local Government, GOS	1/2/2024	Karachi West	46.91
2022-23 1796	Improvement of Sewerage line Boosting Pump, Drainage line and Carpeting of Road in UC-2 Labour Square	Satisfactory	4/12/2023	Local Government, GOS	10/13/2023	Karachi West	81.093
2022-23 1798	Improvement of Water Supply, Sewerage line and Road carpeting in UC-5 Pak Colony	Satisfactory	3/21/2023	Local Government, GOS	7/6/2023	Karachi West	56.222

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1826	Providing & Laying of Paver Block in Different Streets of UC-41,UC-42, UC-43, UC-44, UC-45 and UC-46 in DMC Keamari	Satisfactory	5/26/2023	Local Government, GOS	7/6/2023	Karachi Keamari	95.99
2022-23 1830	Paver Block and Carpeting of Road in different areas of UC-2Mowach Goth.	Un-Satisfactory	10/6/2022	Local Government, GOS	4/18/2024	Karachi Keamari	96.326
2022-23 1832	Improvement of Water Supply and installation of Sewerage lineand Carpeting of Road in UC-3 Keamari Town.	Un-Satisfactory	6/14/2023	Local Government, GOS	11/24/2023	Karachi Keamari	106.576
2022-23 1834	Providing / Laying Paver R.C.C Sewerage Pipe Line and C.C.Flooring I/C Cleaning of Nallahs at different places of UC-41, UC-42, UC-43, UC-44, UC-45 & UC-46 in DMC Keamari	Un-Satisfactory	5/30/2023	Local Government, GOS	8/16/2023	Karachi Keamari	92.88
2022-23 1837	Improvement of Water Supply and installation of Sewerage lineand Carpeting of Road in UC-30 & 31 Baldia Town.	Satisfactory	5/29/2023	Local Government, GOS	9/12/2023	Karachi Keamari	146.796
2022-23 1846	Providing / Laying & Replacement of Damaged & UnserviceableSewerage lines in different areas of PS-97	Satisfactory	3/27/2023	Local Government, GOS	10/13/2023	Karachi Korangi	75.857
2022-23 1857	Rehabilitation / Improvement of Road / Sewerage Line & WaterSystem in the area of PS-123, 124	Un-Satisfactory	3/5/2024	Local Government, GOS	5/17/2024	Karachi Central	96.9
2022-23 1857	Rehabilitation / Improvement of Road / Sewerage Line & WaterSystem in the area of PS-123, 124,	Un-Satisfactory	10/13/2022	Local Government, GOS	12/19/2023	Karachi Central	96.9
2022-23 1866	Providing & Laying of Paver Block at Various Streets / Roads of UC-1, UC-2, UC-22 to UC-39 and UC-45 to UC-50 and Ward Ito 9 Cantt: Taluka City Hyderabad	Satisfactory	7/10/2023	Local Government, GOS	5/17/2024	Hyderabad	292.952
2022-23 1870	Providing & Laying of Paver Block in Hingorno Town TalukaSindhri 8000 RFT	Satisfactory	7/11/2023	Local Government, GOS	11/22/2023	Mirpurkhas	44.477
2022-23 1872	Providing Sewerage Lines in Various wards / UCs of Taluka Nawabshah Juma Khan Zardari, Village Ghazi Khan Hoat and village Khairshah, Haqani Colony, Badal Colony, Sumera Colony, Ghulam Hyder Shah Colony, Bhattai Colony, HousingSociety, Society & Hanif Ka	Satisfactory	9/21/2023	Local Government, GOS	4/24/2024	Shaheed Benazirabad	72.593
2022-23 1874	Improvement of Drainage and Paving Block from TownCommittee Via Phulji Station..	Satisfactory	9/12/2023	Local Government, GOS	6/28/2024	Dadu	98.613
2022-23 1875	Improvement of Drainage and Paving Block of Piyaro StationRoad...	Satisfactory	9/13/2023	Local Government, GOS	6/28/2024	Dadu	98.826
2022-23 1876	Improvement of Road from Indus Highway Degree College to Theba VIP Road Mehar Link to Dua Hospital i/c Drainage onboth sides & Paving Block	Satisfactory	7/7/2023	Local Government, GOS	5/3/2024	Dadu	98.4
2022-23 1898	Construction of Paver Block Road at different streets of Town Khanpur, Village Abdu, Dahar, Mangria Muhalla, Master Bhayo House, Town Committee Chak, Qasim Bhayo & DifferentVillages of UC Mungrani & UC Ruk	Un-Satisfactory	9/21/2023	Local Government, GOS	4/29/2024	Shikarpur	98.781
2022-23 1900	Providing & Laying of Paver Block in Various Links of Muhallah Osta Gahi, Muhallah Dabar, Muhallah Shaikh and Internal Streets of Muhallah Bhurgari upto Bhurgari Regular Khairpurincluding Masonery Structure (340426 Sft) Taluka Khairpur	Un-Satisfactory	3/20/2023	Local Government, GOS	2/20/2024	Khairpur	80
2022-23 1904	Providing of Drainage System & Paver Block City Pir Ezzo U.C.Kamal Dero Taluka Gambat,	Un-Satisfactory	4/17/2023	Local Government, GOS	12/11/2023	Khairpur	50
2022-23 1906	Providing & Laying of CC Paver from Civil Hospital to MangrioPetro Pump Daharki City	Satisfactory	7/14/2023	Local Government, GOS	11/14/2023	Ghotki	106.34
2022-23 1907	Providing & Laying of CC Paver Mirpur Mathelo City	Satisfactory	3/21/2023	Local Government, GOS	4/24/2024	Ghotki	112.605
2022-23 2100	Establishment of City Hall at Khairpur (SDG # 9)	Un-Satisfactory	3/5/2024	Local Government, GOS	6/10/2024	Khairpur	142
2022-23 2100	Establishment of City Hall at Khairpur (SDG # 9)	Satisfactory	4/3/2023	Local Government, GOS	10/20/2023	Khairpur	142
2022-23 2146	Improvement / Rehabilitation of Mubarak Shaheed Road fromCantt General Hospital to Shahrh-e-Faisal, Karachi (2.65 Km) (Revised on 04.06.21)	Satisfactory	7/10/2023	Local Government, GOS	10/13/2023	Karachi	224.612
2022-23 2157	Construction/Rehabilitation of Roads , Sewerage and C.C.Flooring in Dumba Goth, District Malir, Karachi (Revised on 19.05.22)	Un-Satisfactory	4/10/2023	Local Government, GOS	1/3/2024	Karachi	311.883
2022-23 2174	Construction of roads alongwith drainage, Sewerage, Pipes andpaving blocks in UC-1 Sherpao, Malir Karachi	Un-Satisfactory	6/15/2023	Local Government, GOS	10/6/2023	Karachi Malir	79.905
2022-23 2181	Reconstruction / Rehabilitation of roads, Drain work and PaverBlocks C.C flooring at UC45 Gulshan e Sikandarabad District Keamari Karachi	Satisfactory	5/29/2023	Local Government, GOS	7/6/2023	Karachi Keamari	99.493

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2184	Construction / Rehabilitation of Roads, Drain Work and PaverBlocks C.C flooring at UC 42 Machar Colony District Keamari Karachi	Un-Satisfactory	5/31/2023	Local Government, GOS	11/8/2023	Karachi Keamari	49.809
2022-23 2196	Construction asphalt road (New / Repair) various roads with drainage Municipal Committee Rohri. Repair of Pedestrian path ways. Roads surface and repairing of old Sukkur Channel and lands down bridge, road	Satisfactory	10/26/2022	Local Government, GOS	7/13/2023	Sukkur	99.144
2022-23 2201	Widening & reconditioning of road, paver block streets and drainage at Moro city	Satisfactory	10/18/2023	Local Government, GOS	2/27/2024	Naushero Feroz	160.062
2022-23 2207	Recond: / Imp: of Road Naoukot Fazal Bhambro Road to Nafees Nagar to Ali Hassan Gurgez to Shanker Bheel to Shadman Gurgez.	Satisfactory	7/14/2023	Local Government, GOS	11/22/2023	Mirpurkhas	139.552
2022-23 2214	Construction / Rehabilitation of various Roads in PS-64 Ganjo Takar Phatak to New Ali Asgarabad Phatak, Ganjo Takar Phatak to Allah Dino Khumarn, Village Jani Rind Road to Noonari Goth & UC 86,87,91,92,94 & Other City Areas Taluka Latifabad Hyderabad	Satisfactory	7/17/2023	Local Government, GOS	6/10/2024	Hyderabad	174.332
2022-23 2216	Construction of road from Seerani Kadhan road @ point Ahmed Shah Mori to Lakho Pir along with inspection path of Noor Wah (12.00 Km)	Satisfactory	7/19/2023	Local Government, GOS	11/22/2023	Badin	99.316
2022-23 2217	Construction of road from Iqbal Sarejo Umer Mallah road to Village Mir Hoat Haji Vikio Khaskheli and Bakar Mori upto Arab Mallah i/c link Ramzan Mandhro (11.80 Km)	Satisfactory	7/19/2023	Local Government, GOS	4/2/2024	Badin	99.331
2022-23 2218	Improvement / Construction of road from Badin Seerani road to connect Pathan Parhyar road via Haji Parhyar (Construction 3.40 Km, improvement 9.00 Km)	Un-Satisfactory	7/20/2023	Local Government, GOS	5/3/2024	Badin	99.323
2022-23 2219	Improvement / Construction of road from water supply post office road to abu Shaikha (Allah Dino Soomro) i/c link road from Badin Seerani road Ghulam Rasool Lutter (Construction 6.00 Km, improvement 7.60 Km)	Satisfactory	7/20/2023	Local Government, GOS	2/14/2024	Badin	99.215
2022-23 2241	Construction of Roads Paver Block Street and improvement of Sewerage system in UC Khaldabad and UC Cattal Colony (PS-90) District Malir, Karachi	Un-Satisfactory	6/15/2023	Local Government, GOS	10/6/2023	Karachi Malir	92.256
2022-23 2252	Construction / Rehabilitation of Primary & Secondary Roads of Sukkur District	Satisfactory	9/4/2023	Local Government, GOS	4/25/2024	Sukkur	198.95
2022-23 2393	Rehabilitation & Completion of Remaining Civil Works of Cattle Colony at Sukkur (C:179.187 & R:19.767)	Satisfactory	4/20/2023	Local Government, GOS	2/20/2024	Sukkur	198.954
2022-23 2395	Establishment of Cattle Colony at Rohri	Satisfactory	9/5/2023	Local Government, GOS	4/24/2024	Sukkur	399.939
2022-23 2397	Providing and Fixing of Animatronics\ Dinos at Safari Park -Karachi (Revised on 21.01.22)	Satisfactory	7/3/2023	Local Government, GOS	6/28/2024	Karachi	99.956
2022-23 2405	Beautification of M.C Rohri District Sukkur	Satisfactory	12/16/2022	Local Government, GOS	2/20/2024	Sukkur	51.953
2022-23 2412	Construction of Park and Playground in UC -30 & 31	Satisfactory	6/16/2023	Local Government, GOS	7/6/2023	Karachi South	100
2022-23 2448	Development of Township in Major Urban Centers (50,000 120 Square Yard Plots with All Civic Services (Chairman sb Directives)	Un-Satisfactory	6/9/2023	Local Government, GOS	12/11/2023	Jamshoro	9420.88
2022-23 2448	Development of Township in Major Urban Centers (50,000 120 Square Yard Plots with All Civic Services..	Un-Satisfactory	6/7/2023	Local Government, GOS	12/11/2023	Khairpur	9420.88
2021-22 1377	Providing Sewerage lines in PS-24 (SDG # 6.)	Satisfactory	6/22/2023	Local Government, GOS	10/23/2023	Shaheed Benazirabad	60.409
2021-22 1416	Main Water Supply System in Block 13-A to 11-A & Block 11-B to Block-2, 3 & 3-A of Hawksbay Scheme-42 LDA Karachi	Un-Satisfactory	2/21/2022	Local Government, GOS	1/3/2024	Karachi	150.986
2021-22 1421	Rehabilitation/Replacement/Improvement of Water Supply System by P/L 12	Satisfactory	6/20/2023	Local Government, GOS	10/10/2023	Karachi	35.91
2021-22 1423	Rehabilitation / Improvement and replacement of water and sewerage system in UC-29, 30 and 31 Saddar, DMC South	Satisfactory	6/21/2023	Local Government, GOS	10/10/2023	Karachi	29.13
2023-24 3255	Repair / Rehabilitation of Storm Water Drain in Karachi Phase-II	Satisfactory	11/15/2023	Mega Schemes for Karachi City	3/27/2024	Karachi	999.967
2022-23 2469	Construction of U-Turn at Natha Khan Bridge (SDG # 9)	Un-Satisfactory	6/1/2023	Mega Schemes for Karachi City	1/8/2024	Karachi	214.466
2022-23 2471	Rehabilitation / Reconstruction of Shahrah-e-Noor Jehan from Abdullah College to Qalandaria Chowk	Satisfactory	6/2/2023	Mega Schemes for Karachi City	10/23/2023	Karachi	1303.83
2022-23 2474	Reconstruction of Rafiqi Shaheed Road and Kalapul Road from Shahrah-e-Faisal to Main Korangi Road	Satisfactory	10/6/2022	Mega Schemes for Karachi City	7/17/2023	Karachi	208.473

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2475	Rehabilitation & Widening of Road from Razakabad to SheediGoth Power House,	Satisfactory	10/17/2022	Mega Schemes for Karachi City	7/6/2023	Karachi	209.335
2022-23 2479	Construction of Flyover and Underpass at Johar ChowranglIntersection	Un-Satisfactory	6/6/2023	Mega Schemes for Karachi City	1/2/2024	Karachi	2046.301
2022-23 2485	Improvement / Rehabilitation of Shaheed-e-Millat Expressway from KPT Flyover to Manzoor Colony Fire Station (Both Track)including Service road at District East	Un-Satisfactory	6/9/2023	Mega Schemes for Karachi City	8/18/2023	Karachi	516
2022-23 2486	Improvement of roads from MA Jinnah Road to I I Chundrigar Road (Mumtaz Hassan road, Hasrat Mohani road, Paper Marketroad) District South	Satisfactory	7/3/2023	Mega Schemes for Karachi City	6/28/2024	Karachi South	62.797
2023-24 3303	Rehabilitation / Renovation of Temple & Satsang Hall at VillageDoonhon Ibrahim Shah Taluka Babarloi District Khairpur	Satisfactory	9/12/2023	Minorities & Affairs, GOS	2/23/2024	Khairpur	19.835
2023-24 3304	Rehabilitation / Renovation of Domes & Finishing Work i/c FloorTile of Shri Krishana Mandir at Gambat District Khairpur	Satisfactory	11/10/2023	Minorities & Affairs, GOS	1/3/2024	Khairpur	19.812
2023-24 3306	Rehabilitation / Renovation of Jindpir Darbar old Sukkur	Satisfactory	9/8/2023	Minorities & Affairs, GOS	2/21/2024	Sukkur	19.815
2023-24 3310	Rehabilitation of Hindu Massan at Hayat Pitafi Mirpur MatheloDistrict Ghotki	Satisfactory	12/28/2023	Minorities & Affairs, GOS	5/6/2024	Ghotki	19.8
2023-24 3311	Repair & Renovation of Daharki Darbar District Ghotki	Satisfactory	12/29/2023	Minorities & Affairs, GOS	5/13/2024	Ghotki	20
2022-23 2534	Extension Work of Dharamshala, Larkana City	Satisfactory	7/27/2023	Minorities & Affairs, GOS		Larkana	19.835
2021-22 1941	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkano, N.Feroze,Khairpur Mirs, Matiari & T.Allahyar) (Revised	Satisfactory	8/21/2023	Minorities & Affairs, GOS	3/8/2024	Larkana	75.829
2021-22 1944	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad,Jamshoro, Thatta, Shikarp	Satisfactory	3/22/2024	Minorities & Affairs, GOS	5/31/2024	Ghotki	704.565
2023-24 3421	Reconstruction of District & Sub Divisional Field offices-cumResidences of Sindh Bureau of Statistics at Khairpur, Tharimirwah, Kotdiji	Satisfactory	1/8/2024	Planning & Development, GoS	5/14/2024	Khairpur	82.03
2022-23 2621	Reconstruction, Renovation & Rehabilitation of Divisional/ District & Sub-Divisional Offices-cum-Residences of Bureau of Statistics, Sindh. (Hyderabad, Jamshoro, Dadu, SBA, Badin, T.M.Khan, Sukkur, Ghotki, Larkano, Jacobabad, Shikarpur,Mirpurkhas, Tharp	Un-Satisfactory	3/25/2024	Planning & Development, GoS	5/24/2024	Larkana	302.15
2022-23 2621	Reconstruction, Renovation & Rehabilitation of Divisional/ District & Sub-Divisional Offices-cum-Residences of Bureau of Statistics, Sindh. (Hyderabad, Jamshoro, Dadu, SBA, Badin, T.M.Khan, Sukkur, Ghotki, Larkano, Jacobabad, Shikarpur,Mirpurkhas, Th	Un-Satisfactory	9/26/2023	Planning & Development, GoS	12/7/2023	Larkana	23.022
2022-23 2622	ADP No: 3416 2023-24 Construction / Re-Construction ofDistrict Office Cum Residence of Sindh Bureau Of Statistics At Kamber	Un-Satisfactory	9/26/2023	Planning & Development, GoS	11/24/2023	Qambar Shahdadkot	21.87
2022-23 2643	Rehabilitation of RTI, Karachi (C:39.77+R:26.149) (SDG # 3,5)	Satisfactory	1/15/2024	Population Welfare, GOS	3/28/2024	Karachi	65.919
2022-23 2643	Rehabilitation of RTI, Karachi (C:39.77+R:26.149) (SDG # 3, 5)	Un-Satisfactory	7/12/2023	Population Welfare, GOS	11/24/2023	Karachi	65.919
2022-23 2645	Remaining works of RHS-A Centre at Dokri (C:2.847) (SDG # 3,5)	Satisfactory	6/7/2023	Population Welfare, GOS	9/7/2023	Larkana	2.847
2022-23 2657	Construction of Office Building at Thatta (Compliance)	Satisfactory	3/6/2024	Provincial Ombudsman, GOS	5/10/2024	Thatta	53.059
2022-23 2657	Construction of Office Building at Thatta	Un-Satisfactory	11/21/2022	Provincial Ombudsman, GOS	12/19/2023	Thatta	32.943
2023-24 3469	Rehabilitation of Urban Water Supply Scheme ChuharJamali(SDG # 6)	Satisfactory	2/29/2024	Public Health Engineering, GOS	5/13/2024	Sujawal	100.982
2023-24 3483	Water Supply Scheme Arazi Via Bubuk and adjoining 26 NosVillages from Indus Source Taluka Sehwan (SDG # 6)	Satisfactory	2/19/2024	Public Health Engineering, GOS	4/30/2024	Jamshoro	491.134
2023-24 3484	Improvement & Extension Water Supply/Sewerage System Bhitshah (SDG#6)	Worst	11/13/2023	Public Health Engineering, GOS	5/24/2024	Matiari	391.1
2023-24 3485	Improvement and Extention of Urban Water Supply Scheme T.M.Khan City (SDG#6)	Un-Satisfactory	1/16/2024	Public Health Engineering, GOS	6/4/2024	Tando Muhammad Khan	197.624
2023-24 3487	Water Supply Scheme of Village and Union Council KhabriBhitt (Revised on 16.05.23)	Satisfactory	12/5/2023	Public Health Engineering, GOS	6/28/2024	Shikarpur	77.799

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 3490	Construction of 3.0 MGD Filtration Plant i/c distribution network for Water Supply Scheme Rohri Taluka Sukkur (Revised on19.04.2023)	Un-Satisfactory	12/6/2023	Public Health Engineering, GOS	4/30/2024	Sukkur	641.518
2023-24 3496	Urban Water Supply Scheme Shah Purchakar Phase-II	Satisfactory	10/5/2023	Public Health Engineering, GOS	4/25/2024	Sanghar	306.405
2023-24 3537	Water Supply Scheme (Filtration) Sakrand Town (SDG # 6) ADPNo.2068 (2021-22).	Satisfactory	10/27/2023	Public Health Engineering, GOS	4/3/2024	Shaheed Benazirabad	400.473
2023-24 3582	Improvement & Extension of Urban Drainage Scheme Tando	Un-Satisfactory	1/22/2024	Public Health Engineering, GOS	6/6/2024	Hyderabad	100
2023-24 3587	Construction of Drainage Scheme Garho City (SDG # 6).	Un-Satisfactory	9/4/2023	Public Health Engineering, GOS	6/28/2024	Thatta	89.647
2023-24 3588	Construction of Drainage Scheme Kati Bandar (SDG # 6).	Un-Satisfactory	9/26/2023	Public Health Engineering, GOS	12/6/2023	Thatta	72.498
2023-24 3611	Rural Drainage Scheme Saeed Khan Laghari UC BhanoteTaluka Hala (SDG#6).	Un-Satisfactory	10/6/2023	Public Health Engineering, GOS	4/25/2024	Matari	38.449
2023-24 3619	Construction of Drainage Scheme at Various areas of Newpind and Micro Tower Sukkur and Qureshi Goth (Revised on16.05.23)	Un-Satisfactory	11/14/2023	Public Health Engineering, GOS	4/26/2024	Sujawal	176.775
2023-24 3624	Improvement & Extension of Drainage Scheme Khipro. (SDG #6)	Satisfactory	10/9/2023	Public Health Engineering, GOS	2/21/2024	Sanghar	333.584
2023-24 3625	Improvement & Extension of Urban Drainage Scheme ShahpurChakkar (SDG#6).	Satisfactory	10/10/2023	Public Health Engineering, GOS	2/20/2024	Sanghar	199.447
2023-24 3627	Construction of Drainage Scheme Fazal Hussain Chakarani & Khair Mohammad Road Taluka Tando Adam (SDG # 6).	Satisfactory	10/13/2023	Public Health Engineering, GOS	2/20/2024	Sanghar	38.922
2023-24 3634	Paver Block and C.C Drain in Various villages of TalukaMirokhan and Sujawal and Kamber (SDG # 6).	Satisfactory	10/23/2023	Public Health Engineering, GOS	5/20/2024	Qambar Shahdadkot	137.12
2023-24 3641	Improvement & Extension of Drainage Scheme Aadilpurincluding Shaikh Muhalla Taluka Ghotki (SDG # 6) (Revised)	Satisfactory	2/26/2024	Public Health Engineering, GOS	5/20/2024	Ghotki	97.455
2023-24 3643	Drainage Scheme for Tharu Shah Taluka Bhiria (SDG # 6.)	Un-Satisfactory	10/17/2023	Public Health Engineering, GOS	2/27/2024	Naushero Feroz	159
2023-24 3696	Construction of Surface Drains, CC Block and Paver Block at different Mohallas of Town Committee Hingorja, UC Sami, Village Niwaro UC Meerak, Village Razal Memon, UC Madd, Village Haji Abdul Rahim Bhutto UC Rasolabad, Abbasi Mohallaand Mir Mohalla Commi	Satisfactory	2/13/2024	Public Health Engineering, GOS	6/28/2024	Khairpur	62.789
2023-24 3698	Drainage & paver scheme in various villages of Taluka Khairpur, Pipri, village Arbab Shaikh, village Muhammad Saleh Katohar & village Muhammad Murad, drainage, village Bhano Goth, scheme, village Sanjar Katohar, Drainage, village GajjanPahore, Eidal Phul	Un-Satisfactory	1/4/2024	Public Health Engineering, GOS	5/3/2024	Khairpur	150
2023-24 3705	Improvement Extension Drainage Scheme Kazi Ahmed(SDG#6)	Satisfactory	3/18/2024	Public Health Engineering, GOS	6/28/2024	Shaheed Benazirabad	431.378
2023-24 3707	Improvement & Extension of Urban Drainage Scheme Kandiaro, Taluka Kandiaro (SDG#6).	Satisfactory	1/23/2024	Public Health Engineering, GOS	6/28/2024	Naushero Feroz	269.982
2023-24 3741	Rural Drainage Scheme Mashak (old) Mashak (New) & Abdul Hameed para, UC-Gohram Mari, Taluka Sakrand (SDG#6) ADPNo.2175 (2021-22).	Satisfactory	12/15/2023	Public Health Engineering, GOS	3/8/2024	Shaheed Benazirabad	62.209
2023-24 3878	Rehabilitation of Non-functional Water Supply & DrainageSchemes in District Ghotki @ Mirpur Mathelo (Phase-II) (SDG # 6).	Satisfactory	12/8/2023	Public Health Engineering, GOS	2/26/2024	Ghotki	110.958
2022-23 2664	Installation of 10 Reverse Osmosis Plant (RO Plants) in UCGabo Pat Keamari Town Karachi (SDG # 6).	Satisfactory	5/9/2023	Public Health Engineering, GOS	5/13/2024	Karachi	97.876
2022-23 2674	Construction of RCC Underground Reservoir for R.O Plant,Improvement / Extension of Distribution Network for Mithi and Islamkot (SDG # 6)	Un-Satisfactory	9/5/2023	Public Health Engineering, GOS	4/2/2024	Tharparkar	485.69
2022-23 2675	Water Supply Scheme Sokliyo to Veeranio Sokliyo to BehraoVia Rahirari (SDG # 6)	Satisfactory	9/6/2023	Public Health Engineering, GOS	5/10/2024	Tharparkar	36.9
2022-23 2677	Improvement of Water Supply Scheme in Town CommitteeChhachhro & Town Committee Kheme-jo-Par (SDG # 6)...	Satisfactory	4/28/2023	Public Health Engineering, GOS	11/2/2023	Tharparkar	65.833
2022-23 2694	Improvement & Extension of Water Supply Scheme for Kotri City(SDG # 6)	Satisfactory	4/7/2023	Public Health Engineering, GOS	11/27/2023	Jamshoro	160.9

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2710	Improvement & Extension Water Supply Scheme Bhirya City(Revised on 20.04.17) (SDG # 6).	Satisfactory	7/18/2023	Public Health Engineering, GOS	5/6/2024	Naushero Feroz	98.37
2022-23 2716	Water Supply Scheme (Filtration) Dadu (SDG # 6)	Satisfactory	7/5/2023	Public Health Engineering, GOS	2/23/2024	Dadu	754.737
2022-23 2722	Installation of 02 Nos R.O Plant for Village Hashim Chawro UC Ratokot, Jaro Khan Jogi UC Kothi Kandhoro Taluka Larkano 09 Nos. of Culverts for Village Sabzal Mugheri, Taj Muhammad Mugheri (Bado Wah.), Mahi Khan Talo Khan Jagirani (Bdo Wah)Kirrir Khan Mug	Satisfactory	4/12/2023	Public Health Engineering, GOS	1/10/2024	Larkana	35
2022-23 2770	Construction of New Drainage System & CC Blocks at UCHalepoto, UC Seri & UC Almani. (SDG # 6)	Un-Satisfactory	9/12/2023	Public Health Engineering, GOS	3/6/2024	Hyderabad	78.019
2022-23 2782	Improvement & Extension of Urban Drainage Scheme VerTaluka Ghorabari(SDG # 6).	Satisfactory	12/6/2023	Public Health Engineering, GOS	3/28/2024	Thatta	118.252
2022-23 2782	Improvement & Extension of Urban Drainage Scheme VerTaluka Ghorabari (SDG # 6).	Un-Satisfactory	12/13/2022	Public Health Engineering, GOS	7/6/2023	Thatta	118.252
2022-23 2805	Rehabilitation of Urban Drainage Scheme Chuhar Jamali DistrictSujawal (RGC)	Un-Satisfactory	2/29/2024	Public Health Engineering, GOS	5/13/2024	Sujawal	77.143
2022-23 2812	CC Paving Blocks & Drains for Various Villages of UC LoungBhatti Taluka Rohri (SDG # 6).	Un-Satisfactory	3/17/2023	Public Health Engineering, GOS	2/23/2024	Sukkur	80
2022-23 2818	Construction of Drainage Scheme at Bachal Shah Miani Sukkur(SDG # 6).	Un-Satisfactory	2/26/2024	Public Health Engineering, GOS	4/30/2024	Sukkur	133.3
2022-23 2820	Construction of Drainage Scheme Allahabad Colony Sukkur(SDG # 6).	Satisfactory	3/22/2023	Public Health Engineering, GOS	5/2/2024	Sukkur	90.793
2022-23 2831	Rural Drainage Scheme Khabri Taluka Lakhi (SDG # 6)(Revised on 29.04.22)	Un-Satisfactory	9/22/2023	Public Health Engineering, GOS	4/26/2024	Shikarpur	35.996
2022-23 2844	Improvement & Extension of Drainage Scheme Mehar TalukaMehar (SDG # 6)	Satisfactory	7/20/2023	Public Health Engineering, GOS	4/2/2024	Dadu	339
2022-23 2846	Rural Drainage Scheme Mubarakpur Taluka Miro Khan (SDG #6).	Satisfactory	5/26/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shahdadkot	15
2022-23 2848	Construction of C.C Drains and Paver Blocks in UC\'s (05 Nos.)of Taluka Shahdadkot (SDG # 6).	Satisfactory	7/10/2023	Public Health Engineering, GOS	2/14/2024	Qambar Shahdadkot	100
2022-23 2850	Paver Block and C.C Drains in Various Muhallas of MirokhanCity (SDG # 6).	Un-Satisfactory	9/30/2023	Public Health Engineering, GOS	3/8/2024	Qambar Shahdadkot	52.18
2022-23 2868	Paver Block & CC Drains from Allah Park Tower to Shahdadkot Naka Bab-e-Zulifiqar via Rest House and Kamber Lashari Road(2.0 Kms) at Taluka Ratodero (SDG # 6).	Satisfactory	7/11/2023	Public Health Engineering, GOS	1/9/2024	Larkana	66.508
2022-23 2869	Paver Block & CC Drains from Allah Wali Masjid to AbdulWahid Soomro Gate via New Eid Gah and Massan (1.50 kms) at Taluka Ratodero (SDG # 6).	Un-Satisfactory	9/29/2023	Public Health Engineering, GOS	5/2/2024	Larkana	45.734
2022-23 2877	Drainage Scheme Village Pir Muhammad Bhutto, UC Ranwati,Taluka Ubauro (SDG # 6).	Satisfactory	7/13/2023	Public Health Engineering, GOS	11/29/2023	Ghotki	72.966
2022-23 2880	Drainage Scheme Mirpur Mathelo (SDG # 6)	Un-Satisfactory	9/14/2023	Public Health Engineering, GOS	2/28/2024	Ghotki	380.884
2022-23 2882	Rural Drainage for Village Syed Ibrahim Shah UC-BucheryTaluka Daur (SDG # 6).	Satisfactory	11/17/2022	Public Health Engineering, GOS	10/17/2023	Shaheed Benazirabad	26.15
2022-23 2883	Drainage Scheme for Various Wards of Nawabshah City(SDG#6)	Satisfactory	7/31/2023	Public Health Engineering, GOS	2/15/2024	Shaheed Benazirabad	118.835
2022-23 2885	Improvement & Extension of Urban Drainage Scheme SakrandTown (Phase-III) (SDG # 6.)	Satisfactory	1/30/2024	Public Health Engineering, GOS	4/24/2024	Shaheed Benazirabad	196.234
2022-23 2885	Improvement & Extension of Urban Drainage Scheme SakrandTown (Phase-III) (SDG # 6).	Un-Satisfactory	7/31/2023	Public Health Engineering, GOS	12/6/2023	Shaheed Benazirabad	196.234
2022-23 2890	Paver Block and Drains Town Committees Naushehro Ferozeand Mithiani (SDG#6).	Satisfactory	7/21/2023	Public Health Engineering, GOS	11/23/2023	Naushero Feroz	86.3
2022-23 2894	Construction of Surface Drains, CC Topping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Municipal CommitteeMoro Taluka Moro (SDG # 6).	Satisfactory	7/19/2023	Public Health Engineering, GOS	11/29/2023	Naushero Feroz	142.255
2022-23 2914	Drainage and Paver Schemes in Various Villages of Khairpurand Kotdiji (SDG # 6)	Un-Satisfactory	4/4/2023	Public Health Engineering, GOS	2/15/2024	Khairpur	94.02

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2991	Providing and Installation of Solar System for Rural WaterSupply and Drainage Schemes in Sindh Phase II (SDG # 6)	Un-Satisfactory	11/14/2022	Public Health Engineering, GOS	2/13/2024	Badin	1575.944
2022-23 3040	Construction of Road from Main Shaikh Bhirkioy Road toMukhan Morri via Buksho Leghari to Link Road Village Urs Talpur via Gothana Minor side UC Tando Mari.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	6/28/2024	Hyderabad	20
2022-23 3044	Construction of Road from Link Road Muhammad Thebo toKhari Mir Khadim Hussain via Haji Bux Ali Tangri.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	6/28/2024	Hyderabad	20
2022-23 3047	Reconditioning of Road and Retaining Wall from Indus Highway to Watio Khoso Road and Improvement of Road from IndusHighway to Village Khudad Pathan.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	12/1/2023	Dadu	20
2022-23 3057	Reconditioning of Road from Village Khairo Dhero to Village Allah Bux Hakro via Lashari Bridge including Paver Block andCC Drain, Taluka Ratodero.	Un-Satisfactory	7/6/2023	Public Health Engineering, GOS	4/25/2024	Larkana	110
2022-23 3058	Reconditioning of Road from Wasayo Bhutto Road to VillageJan Muhammad Arbani Taluka Ratodero.	Satisfactory	4/12/2023	Public Health Engineering, GOS	10/17/2023	Larkana	10
2022-23 3066	Electrification of Off Grid areas through Solar Technology.Schools & Villages (R:2000.000) (SDG # 7)	Un-Satisfactory	4/10/2023	Public Health Engineering, GOS	12/19/2023	Matiari	2000
Non-ADP	Replacement Of Damaged Outdated Rising Main forSaleemAbad Disposal Work Khairpur	Satisfactory	7/22/2022	Public Health Engineering, GOS	7/13/2023	Khairpur	30.479
2021-22 2071	Water Supply Scheme Mir Mushtaque Ahmed Bijarani UCKarampur Taluka Tangwani	Satisfactory	3/22/2023	Public Health Engineering, GOS	9/7/2023	Kashmore	10
2021-22 2077	Water Supply Scheme Village Kot Ghulam Shah UC RowantiTaluka Kamber (SDG # 6).	Satisfactory	5/31/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shahdadkot	15
2021-22 2161	Rural Drainage Scheme Aali Khabhar UC Khabhar TalukaWarah (SDG # 6).	Satisfactory	5/23/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shahdadkot	20
Non-ADP	Rural Drainage Scheme Dodo Khan khaskheli & Mureed KhnanZardari	Un-Satisfactory	12/14/2023	Public Health Engineering, GOS	5/23/2024	Shaheed Benazirabad	19.71
2020-21 1727	Construction of Drainage Schme Bughan City UC Ketu BanderThatta (ADP No.2081 2017-18)	Worst	2/19/2024	Public Health Engineering, GOS	5/17/2024	Thatta	34.145
2019-20 2069	Rehabilitation of Water Supply Scheme Saban Balhoro.(ADPNo.2036 2017-18)	Un-Satisfactory	3/8/2023	Public Health Engineering, GOS	10/23/2023	Dadu	7.956
2018-19 1653	Contrucion of RCC covered Nala from Railway Phatak to TajColony disposal work Nawabshah (SDG # 6)	Satisfactory	12/15/2023	Public Health Engineering, GOS	6/28/2024	Shaheed Benazirabad	22.113
2017-18 2145	Construction of CC Drains and CC Block at various UCs ofLarkana (20 Villages) (SDG # 6)	Un-Satisfactory	4/28/2023	Public Health Engineering, GOS	4/30/2024	Larkana	40
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13)(C:861.338+R:30.515)	Satisfactory	3/26/2024	Rehabilitation (PDMA), GOS	5/13/2024	Shaheed Benazirabad	891.853
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13)(C:861.338+R:30.515) (as per directives of Chairman sb)	Satisfactory	3/18/2024	Rehabilitation (PDMA), GOS	5/13/2024	Larkana	891.853
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13)(C:861.338+R:30.515)	Satisfactory	3/13/2024	Rehabilitation (PDMA), GOS	5/13/2024	Mirpurkhas	891.853
2023-24 4024	Maintenance & Repair of 333 Flats at Railway Station and PBCLandhi Karachi(SDG # 9)	Un-Satisfactory	2/1/2024	S.G.A.and Coordination, GOS	2/20/2024	Karachi	358.542
2023-24 4024	Maintenance & Repair of 333 Flats at Railway Station and PBCLandhi Karachi (SDG # 9)	Un-Satisfactory	10/25/2023	S.G.A.and Coordination, GOS	12/19/2023	Karachi	358.542
2023-24 4049	Establishment of Central Record Room (CRR) in SGA&CD(Revised on 06.05.21) (SDG # 9)	Un-Satisfactory	11/8/2023	S.G.A.and Coordination, GOS	1/3/2024	Karachi	185.395
2023-24 4065	Establishment of Rehabilitation Center for Drug Addicts atKarachi(C:63.238 + R:10.690) (SDG # 3)	Satisfactory	11/7/2023	Social Welfare, GOS	1/2/2024	Karachi Central	73.928
2023-24 4069	Establishment of Rehabilitation Center for Senior Citizens inDistrict Thatta (C:61.220 + R: 17.086) (SDG # 5 & 10)	Satisfactory	9/5/2023	Social Welfare, GOS	11/24/2023	Thatta	78.306
2022-23 3120	Establishment & Strengthening of Darul Atfal & Rehabilitation of Street Children through Civil Society Organization, Korangi #5, Karachi (Revised on 23.02.18) (C:173.916+R:91.104) (SDG # 1)	Un-Satisfactory	7/4/2023	Social Welfare, GOS	8/18/2023	Karachi Korangi	265.02
2021-22 2464	Establishment of Rehabilitation Center for Drug Addicts atKarachi (C:63.238 + R:10.690) (SDG # 3)	Un-Satisfactory	3/29/2022	Social Welfare, GOS	8/17/2023	Karachi Central	73.928
2023-24 996	Establishment of Autism Rehabilitation & Training Centre atSukkur C: 79.976 + R:10.024) (SDG#4)	Satisfactory	11/3/2023	Special Education	2/20/2024	Sukkur	90
2023-24 4083	Construction of Athletic Track and Football Ground at Karachi,Sukkur & Larkano	Un-Satisfactory	9/7/2023	Sports & Youth Affairs, GOS	4/26/2024	Sukkur	579.874

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4092	Construction of Grassy Cricket Ground with Pavilion at Adilpur.	Satisfactory	2/29/2024	Sports & Youth Affairs, GOS	5/15/2024	Ghotki	43,997
2023-24 4092	Construction of Grassy Cricket Ground with Pavilion at Adilpur	Un-Satisfactory	9/14/2023	Sports & Youth Affairs, GOS	12/19/2023	Ghotki	43,997
2023-24 4104	Construction of Multipurpose Sports Hall i/c Walking TrackMakhdoom Bilawal Cooperative Housing Society (Revised on 14.04.23)	Satisfactory	1/22/2024	Sports & Youth Affairs, GOS	3/27/2024	Karachi Korangi	153,996
2023-24 4107	Construction of Mini Stadium Bhambha Remaining Work i/cExternal Electrification at village Bhambha, Taluka Sehwan (Revised on 22.03.22)	Satisfactory	11/2/2023	Sports & Youth Affairs, GOS	5/10/2024	Jamshoro	100
2023-24 4110	Establishment of Indoor Sports Complex at Pakistan Steel CadetCollege	Satisfactory	10/25/2023	Sports & Youth Affairs, GOS	4/18/2024	Karachi Malir	55
2023-24 4111	Construction of Futsal Ground for Ladies at Government GirlsCollege..	Satisfactory	1/24/2024	Sports & Youth Affairs, GOS	6/28/2024	Jacobabad	44
2023-24 4116	Construction of Grassy Cricket Ground at Sahib Khan Lund.	Satisfactory	1/19/2024	Sports & Youth Affairs, GOS	5/10/2024	Ghotki	49,499
2023-24 4202	Construction of Youth Development Centre at District Matiari	Satisfactory	9/18/2023	Sports & Youth Affairs, GOS	4/26/2024	Kashmore	85.23
2023-24 4203	Construction of Youth Development Centre at District N. Feroze	Satisfactory	11/20/2023	Sports & Youth Affairs, GOS	1/8/2024	Naushero Feroz	85.23
2023-24 4206	Construction of Youth Development Centre at District Sukkur	Satisfactory	11/14/2023	Sports & Youth Affairs, GOS	5/2/2024	Sukkur	85.23
2023-24 4209	Construction of Youth Development Centre at DistrictTharparkar	Satisfactory	9/21/2023	Sports & Youth Affairs, GOS	4/29/2024	Tharparkar	85.23
2023-24 4213	Construction of Youth Development Centre at District Korangi	Un-Satisfactory	1/24/2024	Sports & Youth Affairs, GOS	5/13/2024	Karachi Korangi	85.23
2023-24 4216	Construction of Youth Development Centre at District Malir	Satisfactory	1/10/2024	Sports & Youth Affairs, GOS	6/28/2024	Karachi Malir	85.23
2022-23 3167	Construction of Sports Ground at Dahrki District Ghtoki(C:36.575)	Satisfactory	4/11/2023	Sports & Youth Affairs, GOS	1/5/2024	Ghotki	36,575
2022-23 3176	Missing Facilities Gulistan-e- Scouts Training Centre Abul HasanAsfahani Road Gulshan-e-Iqbal	Satisfactory	5/15/2023	Sports & Youth Affairs, GOS	10/10/2023	Karachi	55
2022-23 3180	Construction of Players Hostel at KHA Ground NIPA	Satisfactory	7/5/2023	Sports & Youth Affairs, GOS	11/10/2023	Karachi East	200
2022-23 3183	Construction & Rehabilitation of Cricket Ground at JinnahGovernment College and Installation of Net around the Boundary Wall of Annu Bhai Cricket Ground Nazimabad.	Satisfactory	3/27/2023	Sports & Youth Affairs, GOS	7/17/2023	Karachi Central	65,995
2022-23 3187	Construction of Ladies Gym & Indoor Hall at Ghotki	Satisfactory	3/21/2024	Sports & Youth Affairs, GOS	6/28/2024	Ghotki	55
2022-23 3188	Establishment of Indoor Sports Complex at Pakistan Steel CadetCollege	Un-Satisfactory	3/24/2023	Sports & Youth Affairs, GOS	7/6/2023	Karachi Malir	55
2022-23 3191	Laying of Football Turf and Allied Works at Lyari InternationalGround, Phase -I	Satisfactory	10/4/2023	Sports & Youth Affairs, GOS	11/22/2023	Karachi South	99.8
2022-23 3196	Rehabilitation and Up-gradation of Sports Ground at Karsaz	Satisfactory	3/28/2023	Sports & Youth Affairs, GOS	7/18/2023	Karachi East	44
2021-22 2569	Construcion of Youth Development Center at Kambar(C:54.978+R:5.022)	Satisfactory	3/9/2023	Sports & Youth Affairs, GOS	10/18/2023	Qambar Shahdadkot	60
2023-24 1067	Establishment of Vocational Centres for girls (04 Units), (i)Village Punhal Khan Chandio Taluka Sakrand District S.B.A	Satisfactory	5/17/2024	STEVA, GOS	6/3/2024	Shaheed Benazirabad	90,363
2020-21 1891	Boring & Installation of 150 Nos Tube wells on Solar Energy for Assured Supply of 100 cusecs for Thar Coal from LBOD SpinalDrain RD-362 (Revised)	Un-Satisfactory	10/5/2023	Thar Coal Infrastructure Development	10/19/2023	Umerkot, Sanghar, Badin	1936,266
2018-19 1858	Construction of Pre-Treatment System for RO Plant LBODWater Supply Scheme at Nabisar for Thar Coal Power Project	Un-Satisfactory	10/3/2023	Thar Coal Infrastructure Development	10/19/2023	Tharparkar	3250,15
2016-17 2214	Water Carrier from Nabisar Reservoir to Thar Coal Field-II(Revised)	Un-Satisfactory	10/4/2023	Thar Coal Infrastructure Development	11/16/2023	Tharparkar	15652,69
2022-23 3290	Upgradation of Traffic Signals in Karachi, Hyderabad, Sukkur,Larkana and Mirpurkhas (Phase-1).@Sukkkur	Un-Satisfactory	12/30/2022	Transport & Comm. (Roads), GOS	2/16/2024	Sukkur	143,22

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1112	Establishment of Khairpur College of Agriculture and Management Sciences Khairpur Mirr	Satisfactory	5/20/2024	Universities and Boards	6/3/2024	Khairpur	1392.513
2023-24 1112	Establishment of Khairpur College of Agriculture and Management Sciences Khairpur Mirr	Un-Satisfactory	11/17/2023	Universities and Boards	3/11/2024	Khairpur	1392.513
2023-24 4287	Establishment of Women Development Complex at SBA(Revised on 29.09.20) (R: 44.767) (SDG # 1, 4, 5, 8 & 9)	Un-Satisfactory	2/20/2024	Women Development, GOS	6/28/2024	Shaheed Benazirabad	44.767
2022-23 3315	Repair / Renovation and Improvement of Services of DarulAman Sukkur (C:14.160 + R:15.840) (SDG # .2)	Un-Satisfactory	4/6/2023	Women Development, GOS	1/5/2024	Sukkur	30
2018-19 1869	Implementation of Gender Reforms Action Plan(GRAP) Sindh (Revised) (R:544.770) (Karachi, SBA, Shikarpur, Sukkur,Larkana, Mirpurkhas, Jamshoro & Hyderabad)	Un-Satisfactory	3/29/2023	Women Development, GOS	11/8/2023	Hyderabad	544.77
2018-19 1872	Advocacy for Women Empowerment in Sindh (All Districts).	Satisfactory	3/30/2023	Women Development, GOS	11/1/2023	Mirpurkhas, Jamshoro, Hyderabad	49.346
Non-ADP	Rehabilitation of Road from Ghulam Nabi Chhutto to VillageHadi Bux Chutto 3.2km in District Jamshoro (Sujawal)	Satisfactory	11/22/2023	Work and Service, GOS	4/25/2024	Jamshoro	149.331
2023-24 4307	W/R of road National Highway to Tando Adam via Bhit Shahmile 0/0-17/0 (27.20 Kms)	Satisfactory	11/24/2023	Work and Service, GOS	6/11/2024	Matiari	747.346
2023-24 4310	W/R of road from Arrore Bachal Shah to Choundko (32.18 Kms))	Satisfactory	8/7/2023	Work and Service, GOS	9/6/2023	Sukkur	540.878
2023-24 4319	(i).Reconstruction of Pre-stressed Bridge 400 RFT (121.91 Meter) onÁ Nae Sukhan @ mileÁ 6/5, (ii).Á Reconstruction of pre-stressed Bridge 50 RFT (15.24 meter) onÁ Rain Nala @ mile 2/0@ link road connectingÁ (NationalÁ HighwayÁ N-5Á toMotorway M-9) @ Kat	Satisfactory	5/2/2024	Work and Service, GOS	5/13/2024	Karachi	149.429
2023-24 4319	(i).Reconstruction of Pre-stressed Bridge 400 RFT (121.91 Meter) onÁ Nae Sukhan @ mileÁ 6/5, (ii).Á Reconstruction of pre-stressed Bridge 50 RFT (15.24 meter) onÁ Rain Nala @ mile 2/0@ link road connectingÁ (NationalÁ HighwayÁ N-5Á toMotorway M-9) @ K	Un-Satisfactory	11/16/2023	Work and Service, GOS	2/13/2024	Karachi	149.429
2023-24 4343	Rehabilitation / Widening and Reconditioning of road Rohri Interchange M-5 to Salehpat City Dual Carriageway (Due to Heavy Traffic existing 24 proposed 50) (0.80 Kms) (Revised on25.01.23)	Un-Satisfactory	10/9/2023	Work and Service, GOS	5/30/2024	Sukkur	456.195
2023-24 4344	Rehabilitation / Reconditioning of road from Ghulam Bund toDhandi via Faqirabad (11.00 Kms) (Revised on 08.05.23)	Satisfactory	9/6/2023	Work and Service, GOS	5/3/2024	Sukkur	159.371
2023-24 4347	Rehabilitation of various roads at village Serai Piyaro Khan, Nazar Mohammad Gaho, Imam Bux Palh, sahib Khan Chakrani, Shadi Shaheed road, Rattal Bhambhro and Babar Wada Jhangoroad to Ahdi Rajper (15.00 Kms) (Revised on 08.05.23)	Satisfactory	11/8/2023	Work and Service, GOS	4/2/2024	Khairpur	196.88
2023-24 4349	Reconditioning of road from Jalal Jee Stop Mehran N/Highway to village Pholirhi via Bhango Behan, UC Bhango (11.60 Kms)(Revised on 08.05.23)	Un-Satisfactory	11/9/2023	Work and Service, GOS	4/3/2024	Khairpur	148.922
2023-24 4351	Rehabilitation / Construction of road from Odha More to Ali Murad Jamali via Amanullah Odho. Paraocha Ulro, G. Nibo Ulro, Muhammad Hayat Ulro, Shaman Ulra, Mehmood Odho mile0/0-7/4, (12.06 Kms) (Revised on 22.05.23)	Un-Satisfactory	11/16/2023	Work and Service, GOS	5/2/2024	Khairpur	202.457
2023-24 4355	Improvement of road from Fakirabad to Jan Muhammad Gopang to Old N.H Way road mile 0/0-2/4 (4.00 Kms) Rehabilitation of road from Jhanda Shakh to Fakirabad upto GIMS road mile0/0-5/0 (8.00 Kms) (Revised on 22.05.23)	Satisfactory	11/30/2023	Work and Service, GOS	2/27/2024	Khairpur	211.403
2023-24 4372	Widening / Reconditioning of road from Haji Ali Nawaz Deeparto Achhi Masjid approach link village Budak (10.00 Kms) (Revised on 14.04.23)	Satisfactory	9/20/2023	Work and Service, GOS	2/21/2024	Naushero Feroz	241.998
2023-24 4380	W/R / Construction of road from N.H.A Sarkari Khooh to connect Aumb Junejo road via Bachalpur, Muhammad Ismail Bhand road (16.00 Kms) (with 5cm thick Asphalt surface) (Revised on14.04.23)	Satisfactory	9/22/2023	Work and Service, GOS	1/8/2024	Shaheed Benazirabad	388.982
2023-24 4382	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms) (Revised on14.04.23)	Satisfactory	9/21/2023	Work and Service, GOS	1/3/2024	Shaheed Benazirabad	243.155
2023-24 4388	Reconditioning of road from Nawabshah - Kazi Ahmed road toconnect Nawabshah - Sakrand road @ Landhi Stop Via Bildo Magsi, Khair Shah & Ghulam Qadir Jatoi 5.00 Kms (With 2	Satisfactory	12/20/2023	Work and Service, GOS	5/17/2024	Shaheed Benazirabad	66.183
2023-24 4389	Reconditioning of road from Mehran Highway @ Bhooral Shah Stop to village Abdullah Bughio via Gabol Stop and villagejeeand Khan Gabol mile 0/0-3/6 - 6.03 Kms (With 2	Satisfactory	10/26/2023	Work and Service, GOS	5/2/2024	Shaheed Benazirabad	97.369
2023-24 4393	W/R of road from Dengan Bhurgari to Jhuluri (9.00 Kms)(Revised on 14.04.23)	Satisfactory	9/27/2023	Work and Service, GOS	5/13/2024	Mirpurkhas	234.815

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4395	Reconditioning of link road from village Bego Kaka Chowk roadto Sarhari RaoJ via village Bhale Dino Kaka road mile 0/0-7/0 (11.20 Kms) (Modified)(Revised on 14.04.23)	Satisfactory	1/24/2024	Work and Service, GOS	6/4/2024	Matiari	269.93
2023-24 4413	Reconditioning of Asphalt Concrete road from Hyderabad - Mirpurkhas road at point Rahuki Bus Stop to Hyderabad - Shaikh Bhirkio road via Bhindo Sharif & Reconditioning of Asphalt Conrete road from Mirpurkhas - Hyderabad road tovillage Wali Muhammad Khask	Satisfactory	9/28/2023	Work and Service, GOS	2/23/2024	Hyderabad	96.501
2023-24 4418	Reconditioning of road from Gharo Mori to Panjtana (6.20 Kms) (Revised on 13.04.23)	Satisfactory	12/4/2023	Work and Service, GOS	4/30/2024	Tando Muhammad Khan	79.318
2023-24 4421	Improvement of road from Dumbalo to Kapri Mori mile 0/0-7/0(11.263 Kms) (Revised on 14.04.23)	Satisfactory	12/6/2023	Work and Service, GOS	6/10/2024	Badin	240.87
2023-24 4424	Widening / Reconditioning of link road from Chach Jahan Khan -Mian Usman Quba road @ 5.00 Kms to village Haji Ali Muhammad Jat Warri - 0.00-7.30 Kms (Revised on 13.04.23)	Satisfactory	11/22/2023	Work and Service, GOS	6/12/2024	Sujawal	201.908
2023-24 4439	W/R of road from Indus Highway to Choukhandi via Ali BuxJunejo village Towards Boriri village, i/c Paver Block & Drain mile 0/0-3/0 (4.83 Kms) (Revised on 18.04.23)	Un-Satisfactory	11/10/2023	Work and Service, GOS	5/29/2024	Dadu	137.49
2023-24 4443	Widening & Reconditioning of road from Walwani Chodagi toTharri Jado Shaheed via Phulji village (8.50 Kms) (Revised on 18.04.23)	Satisfactory	2/27/2024	Work and Service, GOS	6/28/2024	Dadu	172.443
2023-24 4454	Reconditioning of road from Dasori link road to Tayyab Thebo Hazoor Bux Thebo via Habib House, Soothar House mile0/0-1/2 (2.00 Kms) (1	Satisfactory	11/14/2023	Work and Service, GOS	5/17/2024	Tando Allahyar	20.035
2023-24 4457	W/R of road from Tando Allahyar to Mirwah road at BelaroShakh Stop mile 0/0-20/4 (33.00 Kms) (18 to 24 with 2	Satisfactory	11/7/2023	Work and Service, GOS	5/17/2024	Tando Allahyar	1342.916
2023-24 4459	W/R of road from Tando Allahyar Mirwah road to Qazi NoorMuhammad 0/0-1/4 (2.40 Kms)	Satisfactory	11/8/2023	Work and Service, GOS	2/26/2024	Tando Allahyar	53.335
2023-24 4460	W/R of road Nawabshah - Sanghar road @ 3 Water Stop to JamSahib 0.00 - 19.00 Kms (Revised on 24.05.23)	Satisfactory	12/21/2023	Work and Service, GOS	6/6/2024	Shaheed Benazirabad	970.956
2023-24 4463	Rehabilitation of Inter City road / Paving Block various streets ofThatta City i/c Drain Nali	Satisfactory	3/7/2024	Work and Service, GOS	5/10/2024	Thatta	440.519
2023-24 4463	Rehabilitation of Inter- City road / Paving Block various streets ofThatta City i/c Drain Nali	Un-Satisfactory	10/23/2023	Work and Service, GOS	12/20/2023	Thatta	440.519
2023-24 4484	Reconditioning of road from Perumal Tando Mitha Khan via 18 Mile to village Tharoo Khaskheli road. 0.00-10.00 Kms (With1-1/2	Satisfactory	9/20/2023	Work and Service, GOS	3/11/2024	Sanghar	163.194
2023-24 4516	Construction / Improvement of road from Marowala to GulabChowk (Taken up length upto Ayoub Shar) (3.50 Kms)	Satisfactory	3/28/2024	Work and Service, GOS	6/5/2024	Ghotki	70.498
2023-24 4560	Reconditioning of road from Tando Adam Bhit Shah road to Hala Shahdadpur road via Kunb Darhoon, Giddar Ahpan, Baran Hazari. Malook Ahpan and Makhan Ahpan road Mile 0/0-7/5(12.20 Kms) with 1-1/2	Satisfactory	3/11/2024	Work and Service, GOS	5/17/2024	Sanghar	155.962
2023-24 4566	Reconditioning of road from Shahpur Chakar - Chowdagi roadmile 2/4-5/5 (5.00 Kms) (18 width 1-1/2	Satisfactory	3/6/2024	Work and Service, GOS	6/7/2024	Sanghar	114.701
2023-24 4715	Reconditioning of Road from Phull to Bodlo Dahri Rode Mile0/0-7/4	Satisfactory	2/23/2024	Work and Service, GOS	6/6/2024	Naushero Feroz	180
2023-24 4783	Widening & Recondition of Road from Thatta to Jhampir ViaSatyoon Baradabad road. KM-0.00-40.00-40.00 KMs	Satisfactory	3/8/2024	Work and Service, GOS	6/28/2024	Thatta	2052.536
2023-24 4807	Reconditioning / Construction of road from Main National Highway to Kameja Shakh via Goth Hamzo Babbar, Azam Shah, Goth Khad Hajano & Reconditioning of Road from Dargah Bilawal to Bhanoth Road Mile 0/0-7/4 (1	Satisfactory	11/23/2023	Work and Service, GOS	6/3/2024	Matiari	299.383
2023-24 4829	Construction of various roads in UCs of Taluka NaseerabadKamber Warah & Miro Khan (5.00 Kms) (Phase-1)	Un-Satisfactory	11/16/2023	Work and Service, GOS	4/30/2024	Qambar Shahdadkot	808.704
2023-24 4868	Construction of various roads in Taluka Warah (19.95 Kms)	Satisfactory	4/26/2024	Work and Service, GOS	6/3/2024	Qambar Shahdadkot	216.783
2023-24 4876	Construction / Reconditioning of road from Mehran Highway @ Munjla Naako to connect Malhar mangrio, road via village Shaman Lashari & village Muhammad Bux Mojai (9.00 KM) (Revised on 08.05.23)	Satisfactory	1/24/2024	Work and Service, GOS	5/31/2024	Khairpur	183.185
2023-24 4888	Construction of road from Mirpurkhas-Sindhri to Patoyoon roadto link various villages Union Council Old Mirpur & Ahmed Bux Narejo (Length - 8.30 Kms) (Revised on 08.05.23)	Satisfactory	1/15/2024	Work and Service, GOS	6/3/2024	Mirpurkhas	137.1
2023-24 4892	Construction of road from Mureed Khaskhally to Sonharo Dal viaHassan Shah Baghban (4.00 km) (Revised on 11.04.23)	Satisfactory	12/26/2023	Work and Service, GOS	5/20/2024	Umerkot	81.254
2023-24 4910	Construction of road from Tando Muhammad Khan Badin road@ mile 42/2 to village Suwali Dangno along Dokia Wah mile 0/0-6/2 (10.00 Kms) (Revised on 13.04.23)	Satisfactory	1/17/2024	Work and Service, GOS	6/10/2024	Tando Muhammad Khan	186.049

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4921	Construction / Rehabilitation of various roads of UC-11,UC-12,Taluka Thatta, District Thatta (Revised on 13.04.23)	Satisfactory	3/11/2024	Work and Service, GOS	6/3/2024	Thatta	126.759
2023-24 4921	Construction / Rehabilitation of various roads of UC-11, UC-12,Taluka Thatta, District Thatta (Revised on 13.04.23)	Un-Satisfactory	9/27/2023	Work and Service, GOS	12/20/2023	Thatta	126.759
2023-24 4928	Construction of road Network upgradation of 17 existing roads,connecting to Chuhar Jamali (203 Kms) (RGC)	Un-Satisfactory	2/27/2024	Work and Service, GOS	5/17/2024	Sujawal	3905.919
2023-24 4937	Construction of different roads / streets of Taluka Qasimabadand Union Councils Hatari , Barchani, Bahram & Masu (19.70 Kms)	Satisfactory	12/25/2023	Work and Service, GOS	5/30/2024	Hyderabad	311.858
2023-24 4940	Construction of road from Oon Jo Wandhio to village Bhako viaKharoro (8.00 Kms)	Satisfactory	3/5/2024	Work and Service, GOS	6/28/2024	Tharparkar	236.363
2023-24 4942	Construction of road from Jhngal Malik to village Baloch KhanChang (3.00 Kms)	Un-Satisfactory	1/16/2024	Work and Service, GOS	5/2/2024	Ghotki	44.513
2023-24 5066	Construction of road from Bharchondi to Sui Sharif (Taken uplength upto Koro Chachar) (7.20 Kms)	Satisfactory	3/25/2024	Work and Service, GOS	6/28/2024	Ghotki	131.586
2022-23 3326	Improvement / Construction of Road from National HighwayBogo Wah on Both site (10.00 Kms) (SDG # 9)	Un-Satisfactory	11/23/2022	Work and Service, GOS	5/13/2024	Ghotki	260.815
2022-23 3354	W/R of road from N-55 Jail Chowrangi to Mari Chowk via Shahi Bagh and approach to Court Complex at City Shikarpur (7.0Kms) (SDG # 9)	Un-Satisfactory	11/29/2022	Work and Service, GOS	12/1/2023	Shikarpur	165.277
2022-23 3364	Rehabilitation of Station road Madeji City Portion upto RiceCanal (Carpeting & Paver Block) (5.00 Kms)	Un-Satisfactory	4/10/2023	Work and Service, GOS	6/6/2024	Shikarpur	76.285
2022-23 3375	Improvement of road from Shahdadkot Motorway Bypass (M-8)road @ Point Police Chowki to village Meenhoon Khan Leghari (Old Railway Track) via Juneja and Brohi (11.00 Kms)	Satisfactory	9/19/2023	Work and Service, GOS	1/8/2024	Qambar Shahdadkot	109.939
2022-23 3396	Reconditioning / Construction of road from Khanpur Thikratho road to Ibrahim Mahtam via Khameso Bhatti, Ali Madad Mahtam, Ucheer enclsloed various links and Kabil Mahtam (9.00Kms)	Satisfactory	10/27/2022	Work and Service, GOS	7/14/2023	Sukkur	96.134
2022-23 3413	Reconditioning of road from Pacca Chang to Karoondi viaHussain Shah & via Sijawal Khaskheli (5.20 Kms)	Satisfactory	11/29/2022	Work and Service, GOS	7/14/2023	Khairpur	48.969
2022-23 3429	Reconditioning of road from Kandiaro Bus Stop to Saeed KhanLakho via Siddique Lakho (10.00 Kms)	Satisfactory	7/20/2023	Work and Service, GOS	2/27/2024	Naushero Feroz	114.911
2022-23 3437	W/R of road from Dejarja to Chowdagi (with Asphalt) (11.50Kms)	Satisfactory	9/19/2023	Work and Service, GOS	1/8/2024	Naushero Feroz	204.421
2022-23 3450	Reconditioning of road from Nawabshah - Sanghar road tovillage Ali Jan Brohi road (3.40 Kms)	Satisfactory	11/16/2022	Work and Service, GOS	10/20/2023	Shaheed Benazirabad	45.519
2022-23 3451	Widening / Reconditioning / Construction of road from Varr Stop to Connect Nawabshah - Ghupchani Shakal Jamali road via Khando Stop, Dost Pir, Hassan Jamali & Baksho Jamali (15.00Kms) (with 5 cm Thick Asphalt Surface)	Satisfactory	11/17/2022	Work and Service, GOS	9/18/2023	Shaheed Benazirabad	239.6
2022-23 3487	Construction / Improvement of road from Umerkot to Kunri viaDiggu / Gapno Phase-II (18.40 Kms)	Satisfactory	8/11/2022	Work and Service, GOS	10/23/2023	Umerkot	185.954
2022-23 3518	Widening / Reconditioning of Asphalt Concrete road from TandoFazal to Seri road mile 0/0-5/4 (8.80 Kms), Taluka Rural Hyderabad	Satisfactory	10/17/2022	Work and Service, GOS	1/9/2024	Hyderabad	240.117
2022-23 3565	Improvement / Construction of roads of Taluka Manjhand:(i) Indus Highway to village Tangyani via Shah Awais village Golara, village Qaim Khan Khoso & Mureedani i/c M/S mile 0/0-11/4 (18.507 Kms) (ii) Indus Highway to Qubi via FaqeerBux Fanani Khoso, i/c	Satisfactory	9/26/2023	Work and Service, GOS	4/2/2024	Jamshoro	173.605
2022-23 3613	Improvement of road from Naukot to Nabisar via Noohato mile0/0-27/4 (44.00 Kms)	Satisfactory	9/25/2023	Work and Service, GOS	3/6/2024	Tharparkar	1076.447
2022-23 3857	Construction of road from New Bypass Larkana Miro Khan toKamber, Mirokhan road (3.00 Kms)	Satisfactory	9/18/2023	Work and Service, GOS	4/29/2024	Qambar Shahdadkot	179.153
2022-23 3874	Construction of road from Murad Ghoto link road to Bakro Wah,Deh Hussain Beli (2.00 Kms)	Un-Satisfactory	7/17/2023	Work and Service, GOS	12/21/2023	Ghotki	25.137
2022-23 3875	Construction of road from Izzat Wari to village Kaman Mahar viaRaza Muhammad Mahar and village Aleem Malik (8.00 Kms)	Un-Satisfactory	7/14/2023	Work and Service, GOS	12/21/2023	Ghotki	111.69
2022-23 3910	Construction of road from Muhammad Hassan Makrani to villageHaji Afzal Mehar Taluka Shujabad (5.60 KMS)	Satisfactory	7/25/2023	Work and Service, GOS	5/13/2024	Mirpurkhas	79.555
2022-23 3912	Construction of road from Siloor Mori to Adam Mori via VillageSoomar Junejo, Taluka Jhudo (16.00 Kms)	Satisfactory	7/25/2023	Work and Service, GOS	5/10/2024	Mirpurkhas	198.285
2022-23 3927	Construction of road from Dhalo jo Tar to Jetrar road (7.00 Kms)	Satisfactory	4/14/2023	Work and Service, GOS	9/18/2023	Umerkot	154.062
2022-23 3928	Construction of road from Tar Ahmed to Samoon Rind viaUmaid Ali Rind Faqir Tar (7.00 Kms)	Satisfactory	4/13/2023	Work and Service, GOS	9/18/2023	Tharparkar	112
2022-23 3963	Reconditioning / Widening of Road from Jarri Mori to Dando to Village Nazar Khoso via Haji Khan Stop (7.10 Kms)	Satisfactory	7/24/2023	Work and Service, GOS	11/29/2023	Tando Muhammad Khan	99.994
2022-23 3964	Reconditioning / Widening of Road from Digh Mori SoomerkiShakh to Village Jan Muhammad Wassan to Peeru Wassan to Village Bashir Brohi via Nawab Pakko (6.00 Kms)	Satisfactory	7/24/2023	Work and Service, GOS	1/3/2024	Tando Muhammad Khan	127.186

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3973	Construction of road from Malkani City via Mehrab Regulator to Mehrab Shahar i/c link road to Babar Kaloi from Malkani Roopo Rebari road (3.42 Kms)	Satisfactory	7/21/2023	Work and Service, GOS	6/5/2024	Badin	99.997
2022-23 3974	Construction of road from Badin Nindo road to Talho Khan Bhurgri, Otiya Rai Singh, Saeed Khan Bhurgri, Haji Abdul Karim Bhurgri i/c Mir Muhammad Rind, Zubair Rind, via Karo Wahconnect Tando Bago Nindo road 6.15 Kms	Satisfactory	7/21/2023	Work and Service, GOS	1/3/2024	Badin	99.856
2022-23 3994	Construction / Reconditioning of road from Salhani City CheckPost Pano Akil Cantt to Sultanpur road at Bridge Check post Pano Akil Cantt (Strategic Road) (4.00 Kms)	Satisfactory	7/10/2023	Work and Service, GOS	2/26/2024	Sukkur	165.221
2022-23 4145	Construction of Overhead Bridge on Railway Line between KotriCity and the Industrial Area Kotri (SDG # 9)	Un-Satisfactory	6/7/2023	Work and Service, GOS	7/6/2023	Hyderabad	1274.449
2022-23 4146	Construction of Pre-stressed Bridge Karachi 262.50 (80 m) on Sukhan Nadi near Haji Sheedi Goth to Pir Sarhandi Goth road	Satisfactory	5/31/2023	Work and Service, GOS	11/22/2023	Karachi	89.03
2022-23 4157	Repair and Renovation of Residential Colony and office Building of Camp Office, Sindh Coal Authority at Mithi.	Satisfactory	4/13/2023	Work and Service, GOS	3/6/2024	Tharparkar	335.996
2022-23 4775	W/R of road from Thariri Jado Shaheed Road to New Gaj(4/0-18/0-26.00 Kms)	Satisfactory	1/16/2023	Work and Service, GOS	4/29/2024	Dadu	653.892
2022-23 4844	Construction of road from Garhi Khuda Bux Bhutto Ratoderoroad to Bahman Plot along with Sim Drain (8.00 Kms) 24' wide 2	Satisfactory	1/15/2023	Work and Service, GOS	1/31/2024	Larkana	527.76
Non-ADP	CONSTRUCTION OF ROAD FROM NAWAB BHAWAL ROAD TO VILLAGE GULAB KHAN KHASKHELI TO VILLAGE HAJI ALLAH DINO KHASKHELI 0/0 TO 1	Satisfactory	3/15/2023	Work and Service, GOS	2/27/2024	Shaheed Benazirabad	19.964
Non-ADP	Construction of Rooms and Maintenance of Community Center Mehar.	Satisfactory	3/15/2023	Work and Service, GOS	7/4/2023	Dadu	19.02
Non-ADP	Remaining work / Missing facilities in Gym Khana Dadu	Satisfactory	3/16/2023	Work and Service, GOS	7/4/2023	Dadu	30
Non-ADP	Construction of Road From Mahar Road to Muhammad Usman Mahar	Satisfactory	5/18/2023	Work and Service, GOS	7/20/2023	Sukkur	19.77
2021-22 2652	W/R Sanghar to Khipro via Chotiariyon Tando Mitha Khan & Loon Khan Road (53.10 Kms) (With Asphalt Surface)	Satisfactory	5/9/2023	Work and Service, GOS	10/19/2023	Sanghar	1479
2021-22 2653	W/R / Construction of road from Kumb to Malheer Patto via Bkahu Khan Lashari Rais Bangal Khan Chandio upto Old N.H.Way Kotdiji road mile 0/0-12/6 (20.50 kms) (SDG # 9)	Satisfactory	5/4/2023	Work and Service, GOS	10/19/2023	Khairpur	301.255
2021-22 2767	Rehabilitation / Reconditioning of road from Water Works (Bunder road to Bhosa Line via Tanga Stand, Royal road, Nawab Tikka Shop, Qureshi road, Numaish Police Station Chowk i/c link road NADRA Office Local Board (2	Satisfactory	9/29/2022	Work and Service, GOS	10/18/2023	Sukkur	116.352
2021-22 3081	Construction of link road from main Piromal road to village Turk Bhugti link road to village Karim Bhugti (6.00 Kms) (SDG # 9).	Satisfactory	5/10/2023	Work and Service, GOS	11/27/2023	Sanghar	59.5
2021-22 3100	Construction / Rehabilitation of road from Shahpur to Sardar Garh road (17.00 Kms) (SDG # 9)	Un-Satisfactory	11/17/2023	Work and Service, GOS	12/4/2023	Ghotki	189.864
2021-22 3110	Construction of road from link road village Abdul Rasheed to village Ghulam Muhammad village Muhammad Sharif village Juma Khan Jagirani (4.82 Kms) ((SDG # 9)	Un-Satisfactory	2/24/2023	Work and Service, GOS	12/21/2023	Khairpur	59.046
Non-ADP	Remaining work at Irrigation Public Park Dadu	Satisfactory	3/14/2023	Work and Service, GOS	7/4/2023	Dadu	10

Annexure (B)

LIST OF RE-VISITED SCHEMES IN FY 2023-24

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 34	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted) (Total:30139.75 including IDA Share:18686.64, GoS Share:6120.00 & FarmersShare:5333.11)	Un-Satisfactory	12/5/2023	Agriculture, GOS	6/28/2024	Karachi	6120
2023-24 34	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted) (Total:30139.75 including IDA Share:18686.64, GoS Share:6120.00 & Farmers Share:5333.11)	Satisfactory	11/9/2023	Agriculture, GOS	5/3/2024	Tando Muhammad Khan, Jamshoro, Hyderabad	6120
2023-24 35	Construction of Office Building for On -Farm Water Managementstaff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore & Jamshoro)	Un-Satisfactory	9/11/2023	Agriculture, GOS	5/23/2024	Dadu	96.389
2022-23 11	Construction of Additional Building Components of ATI, Jacobabad (U/R)	Un-Satisfactory	7/31/2023	Agriculture, GOS	2/14/2024	Jacobabad	99.939
2022-23 37	Construction of Office Building for On -Farm Water Managementstaff (Badin, Mirpurkhas, Sanghar, SBA, Sukkur, Khairpur, Shikarpur, Dadu, Ghotki, Kashmore .& Jamshoro).	Un-Satisfactory	4/17/2023	Agriculture, GOS	1/9/2024	Shaheed Benazirabad	96.389
2018-19 69	Construction of Office of the Department of Antiquities atKarachi and Sub-Offices at Jamshoro and Sukkur (Revised) (C:330.794+R:17.206) (SDG # 4,11)	Un-Satisfactory	12/11/2023	Antiquities, GOS	5/17/2024	Karachi	348
2023-24 50	Construction & Provision of Allied Facilities at DargahSare-Faqeer Hadi Gham Kusar Taluka Kingri District Khairpur (Revised on 17-09-2021)	Un-Satisfactory	10/30/2023	Auqaf, GOS	5/29/2024	Khairpur	95.569
2023-24 59	Construction / Repair / Renovation of Janaza Gha Bakara Peeri Singo Lane.	Satisfactory	11/20/2023	Auqaf, GOS	1/3/2024	Karachi	25
2022-23 50	Construction of Compound Wall and other Allied Facilities at Dargah & Graveyard Shaikh Tayyab Nangal District Khairpur .	Un-Satisfactory	9/12/2023	Auqaf, GOS	1/3/2024	Khairpur	8.093
2022-23 52	Rehabilitation & Reconstruction of Dargah Adham Sultan (Abu Bin Abdullah) Taluka Kot Diji District Khairpur Mirs	Un-Satisfactory	9/13/2023	Auqaf, GOS	2/27/2024	Khairpur	11.95
2022-23 61	Construction / Rehabilitation of Dargah Syed Sachal Shah Bukhari village Naoabad Taluka Bakrani.	Un-Satisfactory	9/25/2023	Auqaf, GOS	5/22/2024	Larkana	15
2022-23 69	Construction of Boundary wall & Allied Facilities at Dargah Sakhi Sarwar Model Colony Airport Raod.	Satisfactory	7/11/2023	Auqaf, GOS	10/13/2023	Karachi	20
2022-23 72	Construction / Repair / Renovation of Dargah Miran Peer Baghdadi	Satisfactory	1/16/2024	Auqaf, GOS	3/28/2024	Karachi	30
2022-23 77	Construction & Provision of Allied Facilities at Dargah Mian Mangho village Mian Illyas Muhammad UC Fareedabad.	Un-Satisfactory	9/27/2023	Auqaf, GOS	5/22/2024	Larkana	15
2022-23 79	Construction & Provision of Allied Facilities at Dargah Sain Yousuf Shah Jillani UC Ratokot...	Satisfactory	9/28/2023	Auqaf, GOS	4/29/2024	Larkana	15
2023-24 103	Missing Allied facilities of Cultural Complex at Sukkur. (Revised 18.02.21) (C:124.650+R:53.85)	Un-Satisfactory	12/13/2023	Culture, GOS	5/29/2024	Sukkur	178.5
2023-24 111	Establishment of Auditorium at Badin. (Revised on 23.05.23) (C:160.87+R:29.130)	Satisfactory	2/12/2024	Culture, GOS	6/3/2024	Badin	190
2023-24 114	Provision of Allied Facilities at Cultural Complex Thatta. (C:64.564+R:14.941)	Satisfactory	12/5/2023	Culture, GOS	3/26/2024	Thatta	79.505
2023-24 136	Establishment & Improvement of Sambara Inn Larkano (Revised on 29.05.20) (C:127.516+R:20.308)	Satisfactory	10/25/2023	Culture, GOS	5/3/2024	Larkana	452.014

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 153	Conservation & Restoration of Khudabad Masjid at District Dadu. (Revised on 15.02.23) (C:539.407)	Un-Satisfactory	11/7/2023	Culture, GOS	5/23/2024	Dadu	539.407
2018-19 69	Construction of Office of the Department of Antiquities at Karachi and Sub-Offices at Jamshoro and Sukkur (Revised)(C:330.794+R:17.206) (SDG # 4,11)	Un-Satisfactory	12/8/2023	Culture, GOS	5/31/2024	Sukkur	348
2017-18 115	Construction of Guest house for writers and artists in Hyderabad	Satisfactory	12/7/2023	Culture, GOS	6/28/2024	Hyderabad	40
2023-24 1105	Establishment of Quaid-e-Awam University of Engineering Science & Technology, Constituent College / Campus at Larkano (C:1131.925 + R:1504.983) (SDG#4)	Un-Satisfactory	11/14/2023	Education and Literacy, GOS	5/23/2024	Larkana	2636.908
2023-24 1106	Construction of Shaheed Benazir Bhutto Hostel Blocks, Security Arrangements (Electronic Equipment), Sewerage Treatment Facilities, Beautification & Improvement of QUEST at Shaheed Benazirabad (C:121.602 + R:31.862) (SDG#4)	Un-Satisfactory	10/30/2023	Education and Literacy, GOS	2/26/2024	Shaheed Benazirabad	153.464
2023-24 1128	Establishment of Sufism & Modern Sciences University at Bhit Shah	Un-Satisfactory	11/15/2023	Education and Literacy, GOS	5/29/2024	Matiari	1042.776
2023-24 181	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	10/17/2023	Education and Literacy, GOS	5/31/2024	Sujawal	24.923
2023-24 183	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (04 Units) (SDG#4)	Satisfactory	10/18/2023	Education and Literacy, GOS	2/21/2024	Tando Allahyar	24.879
2023-24 184	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Satisfactory	10/19/2023	Education and Literacy, GOS	2/20/2024	Jamshoro	24.017
2023-24 186	Construction of Building for Shelterless Primary School (01 Unit) (Revised on 19.05.2023) (C: 22.392, R: 2.012) (SDG#4)	Satisfactory	10/20/2023	Education and Literacy, GOS	6/28/2024	Hyderabad	24.404
2023-24 188	Construction of Building for Shelterless Primary School (01 Unit) (C: 18.492, R: 1.379) (Revised on 19.05.2023) (SDG#4)	Satisfactory	10/23/2023	Education and Literacy, GOS	6/12/2024	Tando Allahyar	19.871
2023-24 193	Construction of Buildings for Shelterless Primary Schools (02 Units) (C:35.838 + R:2.758) (Revised on 20.05.2023) (SDG#4)	Satisfactory	9/25/2023	Education and Literacy, GOS	11/10/2023	Thatta	38.596
2023-24 238	Up-gradation of Primary Schools to Elementary Schools (06 Units) (C:74.483 + R:15.192) (SDG#4)	Un-Satisfactory	1/17/2024	Education and Literacy, GOS	6/28/2024	Karachi East	89.675
2023-24 244	Construction of Building of Government Boys Lower Secondary School at Muhammad Bux Narejo Taluka Hussain Bux Mari (Revised on 23.05.2023) (SDG#4) (C:17.813 + R:2.532)	Satisfactory	11/8/2023	Education and Literacy, GOS	4/30/2024	Mirpurkhas	20.345
2023-24 248	Up-gradation of Girls Primary Schools to Elementary Schools at Saeed Khan Laghari & Construction of Additional Class Rooms at GBPS Saeed Khan Laghari Taluka Hala (02 Units) (C:48.363+ R:3.448) (SDG#4) (Revised on 04.01.23)	Satisfactory	11/30/2023	Education and Literacy, GOS	4/30/2024	Matiari	51.811
2023-24 412	Establishment of Public Schools in Sindh (05 Units) (C: 1243.851 + R: 88.760) (Revised on 20.08.09) (Re-revised on 15.07.21) (SDG#4)	Un-Satisfactory	1/2/2024	Education and Literacy, GOS	4/30/2024	Tando Muhammad Khan	2169.038
2023-24 417	Establishment of Public School at Kamber-Shahdadkot (C:544.779 + R:52.245) (Revised on 18.05.16) (SDG#4)	Un-Satisfactory	10/2/2023	Education and Literacy, GOS	4/29/2024	Qambar Shahdadkot	597.024
2023-24 420	Immediate Needs for Public School Gadap Town, Karachi (C: 231.328 + R: 59.364) (SDG#4)	Un-Satisfactory	9/19/2023	Education and Literacy, GOS	1/3/2024	Karachi	290.692
2023-24 427	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.782 + R: 3.134) (SDG#4)	Un-Satisfactory	1/12/2024	Education and Literacy, GOS	5/22/2024	Matiari	42.916

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 436	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (02 Units) (Revised on 22.05.2023)(C: Rs. 105.431 + R: 3.310) (SDG#4)	Satisfactory	3/4/2024	Education and Literacy, GOS	5/13/2024	Sukkur	108.741
2023-24 441	Construction of Girls Hostel in Public School Gadap, Karachi (C: 150.227 + 10.509) (SDG#4)	Un-Satisfactory	2/22/2024	Education and Literacy, GOS	5/17/2024	Karachi Malir	160.736
2023-24 486	Re-construction of Compound Wall and other missing facilities at Bahria Public School Naushahro Feroze (01 Unit) (Revised on 23.05.2023) (SDG#4)	Satisfactory	1/25/2024	Education and Literacy, GOS	6/28/2024	Naushero Feroz	52.171
2023-24 496	Provision of Missing Facilities at Government School, PAF Base Korangi Creek(01 Unit) (SDG#4)	Un-Satisfactory	12/26/2023	Education and Literacy, GOS	3/20/2024	Karachi Malir	48.406
2023-24 713	Construction of ECE Class Rooms / Rehabilitation /Up-gradation of Various Schools of UC 1 to 19 (SDG#4) (Revised on 18.05.2023)	Satisfactory	9/20/2023	Education and Literacy, GOS	11/10/2023	Karachi South	118.827
2023-24 718	Rehabilitation & Provision of Missing Facilities in Existing GBHS Baberlo, GGHS Luqman, GBHSS Talpur Wada & GHSS FaizKotdiji (04 Units) (Revised on 22.05.2023) (SDG#4)	Satisfactory	3/8/2024	Education and Literacy, GOS	6/3/2024	Khairpur	80.87
2023-24 726	Establishment of Government Secondary School (Boys & Girls) in Chuhar Jamali Sujawal District (RGC)	Un-Satisfactory	2/27/2024	Education and Literacy, GOS	5/10/2024	Sujawal	205.5
2023-24 836	Establishment of Girls Degree College at Rohri District Sukkur (C: 152.375+ R:15.00) (SDG#4) Revised 03.01.2023	Satisfactory	3/26/2024	Education and Literacy, GOS	4/26/2024	Sukkur	167.375
2023-24 850	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Thatta (SDG#4)	Un-Satisfactory	12/27/2023	Education and Literacy, GOS	2/13/2024	Thatta	52.08
2023-24 858	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Sukkur (SDG#4) (Revised on 08.03.2023)	Satisfactory	11/1/2023	Education and Literacy, GOS	2/16/2024	Sukkur	124.818
2023-24 867	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi West (SDG#4)	Un-Satisfactory	10/19/2023	Education and Literacy, GOS	12/19/2023	Karachi West	29.586
2023-24 868	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi Central(SDG#4)	Satisfactory	4/23/2024	Education and Literacy, GOS	5/17/2024	Karachi Central	47.412
2023-24 869	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi East (SDG#4)	Un-Satisfactory	10/17/2023	Education and Literacy, GOS	1/3/2024	Karachi East	65.995
2023-24 871	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi Korangi SDG#4)	Un-Satisfactory	11/21/2023	Education and Literacy, GOS	1/2/2024	Karachi Korangi	41.433
2023-24 872	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Keamari Karachi (SDG#4)	Satisfactory	11/22/2023	Education and Literacy, GOS	1/8/2024	Karachi Keamari	19.989
2023-24 874	Establishment of Shaheed Naseem Ahmed Kharal Government Degree College Ripri Taluka Gambat District Khairpur (SDG#4) (C: 97.325 + R: 8.620)	Satisfactory	11/7/2023	Education and Literacy, GOS	2/15/2024	Khairpur	105.945
2023-24 887	Rehabilitation & Provision of Missing Facilities in Existing GBDC/ GGDC Naudero District Larkano (Revised on 08.03.2023)	Satisfactory	10/5/2023	Education and Literacy, GOS	6/28/2024	Larkana	113.77
2023-24 891	Establishment of Girls Degree College Ubauro District Ghotki (SDG#4) (C: 154.126 + R: 10.826)	Un-Satisfactory	9/15/2023	Education and Literacy, GOS	1/5/2024	Ghotki	164.953
2023-24 892	Establishment of Girls Degree College at New Saeedabad Taluka New Saeedabad District Matiari (SDG#4) (C: 89.879 + R: 8.909)	Un-Satisfactory	10/16/2023	Education and Literacy, GOS	4/26/2024	Matiari	98.788
2023-24 925	Construction of Building for existing Degree College Daulatpur District Sh.Benazirabad (C:88.480 + R:9.000) (SDG#4) (ADP 2021-22 S. No.492)	Un-Satisfactory	10/25/2023	Education and Literacy, GOS	3/6/2024	Shaheed Benazirabad	97.48

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 979	Remaining Works of Cadet College Ghotki (C:861.698 + R:67.243) (Re-Revised on 12.02.2016) (SDG#4)	Satisfactory	11/23/2023	Education and Literacy, GOS	5/6/2024	Ghotki	928.941
2023-24 988	Restoration of rain/ flood damages and Construction of female staff Hostel, Male Staff Hostel, Model school (pre Nusrary-7) and Horse Riding club at Bakhtawa Girls Cadet College Shaheed Benazirabad (SDG#4)	Satisfactory	3/18/2024	Education and Literacy, GOS	5/9/2024	Shaheed Benazirabad	250
2023-24 990	Establishment of Special Education & Rehabilitation Complex at Tando M. Khan (SDG#4)	Satisfactory	10/18/2023	Education and Literacy, GOS	11/23/2023	Tando Muhammad Khan	406.783
2023-24 995	Establishment of Autism Rehabilitation & Training Centre at Shaheed Benazirabad (C: 86.895 + R:10.024) (SDG#4)	Satisfactory	10/26/2023	Education and Literacy, GOS	5/3/2024	Shaheed Benazirabad	96.919
2022-23 194	Construction of Buildings for Shelterless Primary Schools (05 Units) (C:69.745 + R:6.895) (SDG#4)	Satisfactory	3/27/2023	Education and Literacy, GOS	11/8/2023	Naushero Feroz	76.64
2022-23 200	Construction of Buildings for Shelterless Primary Schools (03 Units) (C:42.061 + R: 4.137) (SDG#4) [First Visit]	Un-Satisfactory	7/18/2023	Education and Literacy, GOS	2/16/2024	Qambar Shahdadkot	46.198
2022-23 341	Miscellaneous Immediate Works of Public School Hyderabad (C:554.871 +R:51.189) (SDG#4).	Satisfactory	11/13/2023	Education and Literacy, GOS	1/11/2024	Hyderabad	606.06
2022-23 353	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.712 + R: 4.295)(SDG#4)	Satisfactory	7/26/2023	Education and Literacy, GOS	11/21/2023	Tando Muhammad Khan	44.007
2022-23 365	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.685 + R: 1.940)(SDG#4).	Satisfactory	11/3/2022	Education and Literacy, GOS	11/10/2023	Karachi East	109.598
2022-23 385	Up-gradation of Middle School to High School (01 Unit) (C:25.572 + R:4.091) (SDG#4)	Satisfactory	5/22/2023	Education and Literacy, GOS	10/6/2023	Karachi South	29.663
2022-23 386	Up-gradation of Middle Schools to High Schools (02 Units) (C:55.205 +R:8.182) (SDG#4)	Satisfactory	5/23/2023	Education and Literacy, GOS	11/8/2023	Karachi East	65.387
2022-23 387	Up-gradation of Middle School to High School (01 Unit) (C:25.379 + R:4.091)(SDG#4)	Satisfactory	5/24/2023	Education and Literacy, GOS	11/8/2023	Karachi Central	29.47
2022-23 420	Up-gradation of Government Girls Lower Secondary School to Secondary School at Punhal Khan Chandio (01 Unit) (SDG#4)	Satisfactory	7/25/2023	Education and Literacy, GOS	11/21/2023	Shaheed Benazirabad	56.809
2022-23 432	Rehabilitation / Renovation and Provision of Missing Facilities to existing GBHS Ghulam Muhammad Laghari Taluka Shahdadpur(C: 34.837 + R: 6.428) (SDG#4)	Satisfactory	4/12/2023	Education and Literacy, GOS	11/27/2023	Sanghar	41.265
2022-23 548	Rehabilitation / Renovation & Provision of Missing Facilities in Existing GBPS & GBLSS Police Line and GBHS Sanghar(C:177.828 + R: 12.945) (03 Units) (SDG#4)	Satisfactory	4/17/2023	Education and Literacy, GOS	2/13/2024	Sanghar	190.773
2022-23 688	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi South(SDG#4)	Satisfactory	1/9/2024	Education and Literacy, GOS	3/28/2024	Karachi South	86.336
2021-22 332	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 39.603 + R: 3.757)(SDG#4)	Un-Satisfactory	4/14/2022	Education and Literacy, GOS	11/10/2023	Karachi West	43.36
2021-22 398	Construction of Building for existing degree College @ Mansoor District Matiari (01 Unit)	Un-Satisfactory	11/14/2023	Education and Literacy, GOS	5/30/2024	Matiari	86.669

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est. Cost Rs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/15/2024	Energy, GOS	4/23/2024	Hyderabad	440.11
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est. Cost Rs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/13/2024	Energy, GOS	4/18/2024	Matiali	440.11
2023-24 1155	Sindh Solar Energy Project (SSEP) (Total Est. Cost Rs.12,848.11 M including Rs. 7,952.9 M as FEC)(World Bank96.57% Rs.12408.00 M, GoS 3.43% Rs. 440.110 M)	Satisfactory	3/12/2024	Energy, GOS	4/18/2024	Tando Allahyar	440.11
2023-24 1207	Construction of Offices of Excise & Taxation in New Districts (5 units) (SDG # 9)	Satisfactory	10/2/2023	Excise & Taxation, GOS	1/3/2024	Tando Allahyar	86.476
2023-24 1209	Renovation of Excise and Taxation Office Thatta (Cap. Rs. 23,860 + Rev. Rs. 2,557) ((SDG # 9)	Satisfactory	9/7/2023	Excise & Taxation, GOS	5/13/2024	Thatta	26.417
2021-22 701	Construction of offices of Excise & taxation in new districts(5 units) (Tando Allah Yar, TM Khan, Umerkot, Matiali & Jamshoro)	Satisfactory	3/24/2023	Excise & Taxation, GOS	10/17/2023	Umerkot	86
2022-23 954	Construction of Open Platforms/ Plinth for Grain Storage in Sindh (SDG # 2)	Un-Satisfactory	4/10/2023	Food, GOS	5/13/2024	Sukkur	634.843
2023-24 1227	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	10/16/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Ghotki	3016.35
2023-24 1227	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	10/10/2023	Forest, Wildlife & CDA, GOS	5/11/2024	Dadu	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	9/29/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Shaheed Benazirabad	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	9/18/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Naushero Feroz	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	9/13/2023	Forest, Wildlife & CDA, GOS	11/8/2023	Khairpur	3016.35
2022-23 958	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoSshare Rs. 3016.350 m	Satisfactory	9/5/2023	Forest, Wildlife & CDA, GOS	1/1/2024	Sukkur	3016.35
2022-23 959	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiali, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki, N.Feroze, T.M. Khan,, Umerkot, Thar,Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG # 15)	Un-Satisfactory	9/18/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Naushero Feroz	708

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 959	Enhancing Tree Cover on State Forest Lands in Sindh (Revised) (Jamshoro, Dadu, Matiari, SBA, Sanghar, Shikarpur, Kashmore, Sukkur, Khairpur, Ghotki, N.Feroze, T.M. Khan, Umerkot, Thar,Badin, T.A.Yar, Kamber, Larkano & Jacobabad) (SDG #15)	Un-Satisfactory	11/28/2022	Forest, Wildlife & CDA, GOS	2/26/2024	Sujawal	708
2022-23 961	Satellite Based Mapping of Forest Areas and Follow-up Satellite Service for Implementation of Sindh Sustainable ForestManagement Policy 2019 (SDG #15)	Un-Satisfactory	7/27/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Larkana	320
2022-23 961	Satellite Based Mapping of Forest Areas and Follow-up Satellite Service for Implementation of Sindh Sustainable ForestManagement Policy 2019 (SDG #15)	Un-Satisfactory	4/10/2023	Forest, Wildlife & CDA, GOS	2/12/2024	Ghotki	320
2020-21 548	Demarcation Reforestation & Regeneration of Vacted Forest Land (SDG 15)	Satisfactory	8/18/2023	Forest, Wildlife & CDA, GOS	11/2/2023	Hyderabad	135
2023-24 1239	Construction of Warehouse at Dr. Ruth K.M.Pfau Civil Hospital, Karachi (C: 85.368 + R: 21.397)(SDG #3, 4)	Un-Satisfactory	2/23/2024	Health, GOS	5/17/2024	Karachi	106.765
2023-24 1240	Re-construction of Underground Tank with Pumping room at NICH,Karachi (C: 44.676) (SDG #3)	Satisfactory	2/6/2024	Health, GOS	4/18/2024	Karachi	44.676
2023-24 1246	Strengthening of Neonatal Intensive Care Unit at PMC Hospital, Shaheed Benazirabad.(C: 3.170 + R: 147.170) (SDG #3, 4)	Un-Satisfactory	9/25/2023	Health, GOS	4/29/2024	Shaheed Benazirabad	150.34
2023-24 1268	Construction of 100 bedded Hospital at PIB Colony, Karachi (C: 397.710+R: 261.948) Revised on 06.06.22(SDG #3)	Satisfactory	10/18/2023	Health, GOS	3/28/2024	Karachi	659.658
2023-24 1272	Construction of Divisional Warehouse at Karachi.(C:88.930+R:5.312)(SDG #3)	Un-Satisfactory	1/11/2024	Health, GOS	5/17/2024	Karachi	94.242
2023-24 1280	Establishment of Dispensaries at UC-03, New Sabzi Mandi Taluka City Hyderabad, UC-05 at New Hyderabad City and New Manthar Petrol pump Hala Naka City Hyderabad & Up gradation of BHU to 10 Bedded Mother & Child Healthcare Center UC-16at Liaquat Colony Hyd	Un-Satisfactory	11/3/2023	Health, GOS	6/7/2024	Hyderabad	48.385
2023-24 1303	Up gradation of RHC to the level of THQ/Model Hospital Chohar Jamali (C:385.087 + R:105.573) (SDG #3)	Satisfactory	2/27/2024	Health, GOS	4/18/2024	Sujawal	490.66
2023-24 1316	Up gradation of BHU to RHC at Khanwahan (C:62.422+R:32.818)(SDG# 3)	Satisfactory	11/22/2023	Health, GOS	4/24/2024	Naushero Feroz	95.24
2023-24 1358	Up-gradation of THQ Hospital to the level of DHQ Hospital (03 Nos) at Matiari, Qamber & Umerkot	Un-Satisfactory	11/13/2023	Health, GOS	5/29/2024	Matiari	2483.861
2023-24 1444	Establishment of Nursing & Paramedical School at Syed Abdullah Shah Institute of Medical Sciences, SehwanSharif.(SDG #3,4,6) (C: 357.653 M + R: 68.554 M)	Satisfactory	11/20/2023	Health, GOS	5/14/2024	Jamshoro	426.207
2022-23 1006	Construction of 50 bedded hospital at Gulshan-e-Hadeed, Malir, Karachi (C:191.994+R:81.161) (SDG#3)	Satisfactory	5/11/2023	Health, GOS	11/22/2023	Karachi	273.155
2022-23 1016	Construction of Divisional Warehouse at Sukkur. (C:88.930+R:5.312)(SDG#3)	Un-Satisfactory	4/10/2023	Health, GOS	1/11/2024	Sukkur	94.242
2022-23 1022	Construction of Diagnostic Centre with OPD/Referral services atVillage Adur Narejo, UC Golo Wahan, Taluka Gambat, District Khairpur (Revised on 05.01.21)(C:37.611+R:13.342) (SDG #3)	Un-Satisfactory	7/10/2023	Health, GOS	1/10/2024	Khairpur	50.953
2022-23 1035	Establishment of THQ Hospital at Ghorabari (C:342.609 + R:99.047) (SDG #3)	Satisfactory	8/23/2022	Health, GOS	2/13/2024	Thatta	441.656
2022-23 1036	Renovation and Rehabilitation of Paramedical Institute, Larkano. (C: 47.948+R: 19.785) (SDG #3)	Un-Satisfactory	3/10/2023	Health, GOS	12/1/2023	Larkana	67.733

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1038	Establishment of Thalassemia Day Care Centre at Dargah Jaral Shah, Larkano. (C:13.224+R:8.762)(SDG #3,9)	Un-Satisfactory	7/26/2023	Health, GOS	4/3/2024	Larkana	21.986
2022-23 1079	Up gradation of Health facility at Village Ber Sharif, Taluka Kamber. (C:10.679+R:2.816)(SDG #3)	Un-Satisfactory	3/17/2023	Health, GOS	5/22/2024	Qambar Shahdadkot	13.495
2022-23 1085	Expansion & Improvement of DHQ Hospitals (06 Nos) at Thatta, Dadu, N. Feroze, Mirpurkhas, Sanghar & Mirpur Mathelo at Ghotki (Revised on 07.11.17).(C: 2749.885+R: 2114.021) (SDG#3)	Satisfactory	10/10/2022	Health, GOS	7/6/2023	Thatta	4863.906
2022-23 1086	Up gradation of THQ Hospitals to the level of DHQ Hospitals (03 Nos) at Matiari, Kamber & Umerkot (Revised on 22.01.16).(C: 1875.856+R: 608.005) (SDG #3)	Satisfactory	8/11/2023	Health, GOS	10/6/2023	Umerkot	2483.861
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	3/8/2023	Health, GOS	7/10/2023	Qambar Shahdadkot	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	3/7/2023	Health, GOS	7/10/2023	Shikarpur	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	3/7/2023	Health, GOS	7/10/2023	Jacobabad	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) QambarShahdadkot.	Un-Satisfactory	11/24/2022	Health, GOS	11/14/2023	Qambar Shahdadkot	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	11/23/2022	Health, GOS	1/10/2024	Sujawal	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Gari Kharo &Thull.	Un-Satisfactory	11/23/2022	Health, GOS	11/13/2023	Jacobabad	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Johi , K.Nshah & Mehar.	Un-Satisfactory	11/22/2022	Health, GOS	11/13/2023	Dadu	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQHospitals (41 Nos.). (C: 1415.876+ R: 1918.285) (SDG #3)	Un-Satisfactory	11/21/2022	Health, GOS	7/6/2023	Matiari	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Ratodero &Dokri.	Un-Satisfactory	11/21/2022	Health, GOS	11/14/2023	Larkana	3334.161
2022-23 1089	Up gradation & Revamping of THQ Hospitals (39 Nos.) & Construction of Emergency Cum Trauma Centres in THQ Hospitals (41 Nos.). (C: 1415.876+ R: 1918.285) Lakhi Ghulam& Garhi Yaseen.	Un-Satisfactory	11/21/2022	Health, GOS	11/13/2023	Shikarpur	3334.161
2022-23 1181	Establishment of Child Health Care Institute Sukkur (Revised on 01.02.21) (GoS:162.792+Korean soft loan: 6386.547-6549.339)(SDG #3)	Satisfactory	3/22/2023	Health, GOS	9/12/2023	Sukkur	162.792
2021-22 737	Establishment of Gastroenterology & Neuropsychiatry unit at NICH, Karachi.	Satisfactory	9/14/2022	Health, GOS	2/13/2024	Karachi	103.109

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
Non-ADP	Up-gradation to the level of RHC at Unerpur (Ward Block / OPD Block) Taluka Manjhand District Jamshoro	Un-Satisfactory	8/17/2023	Health, GOS	12/19/2023	Jamshoro	20
2023-24 1466	Construction of Special Investigation Complex for 10 Nos Police Station(SDG # 16)	Un-Satisfactory	10/9/2023	Home, GOS	12/7/2023	Karachi	134.584
2023-24 1467	Improvement / Strengthening of Security to SBB ATI Razzakabad Karachi (Construction of RCC Compound Wall 15height with Watch Towers) (SDG # 16)	Satisfactory	12/11/2023	Home, GOS	3/27/2024	Karachi	433.126
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	2/29/2024	Home, GOS	5/14/2024	Ghotki	292.136
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	2/21/2024	Home, GOS	5/13/2024	Shaheed Benazirabad	292.136
2023-24 1472	Construction of Mall Khana in various Districts of Sindh	Satisfactory	1/26/2024	Home, GOS	6/28/2024	Naushero Feroz	292.136
2023-24 1509	Establishment of Forensic Laboratory in Sindh at Karachi (SDG # 16) (Revised on 21-04-2022)	Satisfactory	10/16/2023	Home, GOS	11/24/2023	Karachi	5426.409
2023-24 1561	Construction of Residences for Anti-Terrorism Courts Judges, Prisons Officers / Staff at Central Prison Karachi (SDG # 16)	Satisfactory	12/15/2023	Home, GOS	12/19/2023	Karachi	890.848
2022-23 1188	Construction of Buildings for Sindh Police at various locations under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, Shaheed Benazir Abad, Kamber & Sukkur)(Revised) (SDG # 16)..	Satisfactory	5/19/2023	Home, GOS	11/27/2023	Hyderabad	642.101
2022-23 1208	Construction of Police Station (Category-C) & Bachelor Barracks (Ground + 1) at Nindo District Badin (859 of 2017-18)(Remaining work).	Satisfactory	3/13/2023	Home, GOS	10/18/2023	Badin	37.198
2022-23 1236	Construction of new Watch Towers (10) Nos including construction of consultant, Jailor & Record Rooms, external lavatory blocks and replacement of various roofs of barracks at Central Prison Karachi.	Satisfactory	7/12/2023	Home, GOS	10/6/2023	Karachi	53.132
2022-23 1242	Construction of Affidavit Centre, Pray Area, General Bathroom, Bar Room, Library, Prosecutor Chamber, and Public Cafeteria at ATC Courts, Central Prison, Karachi.	Satisfactory	7/13/2023	Home, GOS	10/10/2023	Karachi	98.109
2021-22 909	Improvement / Strengthening of Security to SCTC Sakrand (Compound Wall with Watch Towers) (SDG # .16)	Satisfactory	3/14/2023	Home, GOS	4/24/2024	Shaheed Benazirabad	48.629
2021-22 917	construction of Polce Station Building at PS Dehi (SDG No. 16)	Satisfactory	4/26/2023	Home, GOS	2/26/2024	Badin	34.1
2023-24 1567	Human Rights Complaint Management System (R: 80.362) (Revised on 10.05.23)(SDG # 10 & 16)	Un-Satisfactory	2/1/2024	Human Rights, GOS	2/14/2024	Karachi South	80.362
2022-23 1281	Provision of basic facilities of Sewerage / CC Drain /CC topping in different Katchi Abadis in Sindh	Un-Satisfactory	12/7/2023	Human Settlement, Spatial Development & Social Housing	5/17/2024	Karachi	40
2023-24 1578	Improvement of Basic Infrastructure at Industrial Park, Shershah Karachi (4.68 acre land)	Satisfactory	2/15/2024	Industrial & Commerce, GOS	5/13/2024	Karachi	49.11
2023-24 1592	Rehabilitation of Infrastructure and Development at S.I.T.E Sukkur	Un-Satisfactory	10/11/2023	Industrial & Commerce, GOS	3/8/2024	Sukkur	439.366
2021-22 992	Construction of District Information office at Matiari (C: 11.982+R: 01.762)	Satisfactory	6/7/2022	Information & Archives, GOS	1/3/2024	Matiari	13.744
2021-22 995	Construction of District Information office at Thatta (C: 11.138+R: 01.762)(LTBC) (As per request of the department)	Satisfactory	6/9/2022	Information & Archives, GOS	11/24/2023	Thatta	12.9
2023-24 1638	Boring & Installation of 250 Nos Tubewells of 2.0 Cusecs on Solar Energy (SDG # 6)	Un-Satisfactory	12/13/2023	Irrigation (Water & Drainage), GOS	5/29/2024	Sukkur	2087.11

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1667	Construction of Sub-Drain parallel to Nara Canal from RD-450.0 to 574 (Revised on 22.05.23)	Un-Satisfactory	12/11/2023	Irrigation (Water & Drainage), GOS	5/10/2024	Khairpur	598.579
2023-24 1686	Installation Tubewells of 06 Villages of U.Cs Soomar Khan, Gupchani, Jhooro Khan Shar and Abdul Hassan: Village Zahid Ali Jamali, Deh 14 Nasrat, UC Soomar Khan, Village Nawab Khan Brohi, Deh 14 Nasrat, U.C Soomar Khan, Village MeerMahar, U.C Soomar Khan	Satisfactory	1/30/2024	Irrigation (Water & Drainage), GOS	6/10/2024	Shaheed Benazirabad	51.766
2023-24 1718	CC Lining of Shah Nawaz Wah from RD-0.0 to 53, Rahuja Minor RD-9+5 to 25+0, Kanasera Minor, Junki Minor, and Retaining Wall along Faiz Wah - Revised on 29.05.20 (SDG # 6)	Un-Satisfactory	12/12/2023	Irrigation (Water & Drainage), GOS	5/13/2024	Khairpur	694.412
2023-24 1732	Constructing Stone Pitching at RD-9+00 to 15+00 RMC B/S and Downstream Fall Structure 16, 17, 18, 19 & 20 B/Sides (Revised 22-02-22).	Un-Satisfactory	9/8/2023	Irrigation (Water & Drainage), GOS	4/25/2024	Sukkur	378.078
2023-24 1761	Construction of J- Spurs U/S Left Guide Bank to Centralize the Flow of Indus River Water under Thatta Sujawal Road Bridge (Doolah Bridge) in Kalri Baghar Division Thatta	Satisfactory	3/7/2024	Irrigation (Water & Drainage), GOS	5/10/2024	Thatta	1947.576
2023-24 1763	Construction of C.C. Lining from Head to Tail of Pubjo Minor & Kazi Ahmed Minor including allied structures in Dad Division.	Un-Satisfactory	9/28/2023	Irrigation (Water & Drainage), GOS	2/21/2024	Shaheed Benazirabad	418.335
2023-24 1782	C.C. Lining of Sultani Branch & its 6 Nos. off-taking channels.	Satisfactory	11/13/2023	Irrigation (Water & Drainage), GOS	5/9/2024	Badin	2342.5
2023-24 1798	Construction of New Road Bridge over Kalri Baghar Feeder Upper at RD-120	Satisfactory	11/21/2023	Irrigation (Water & Drainage), GOS	2/14/2024	Thatta	116.574
2022-23 1420	Providing Stone Pitching along PFL RD 120 to 130 IP side RD 135 to 140 NIP side, RD 152 to 160 and 161 to 163 NIP side Village Abrial and Re-Sectioning of Gunj Bahar Branch and Repair of Head Regulator, Road Bridge, dumping of stonepitching and Rehabilita	Un-Satisfactory	10/3/2022	Irrigation (Water & Drainage), GOS	1/9/2024	Tando Muhammad Khan, Sujawal	679.9
2022-23 1434	Renovation / Re-Construction of road Bridge over Mirwah Canal at RD-33 near Railway Station Begmangi, Installation of Steel grill over Retaining Wall along Mirwah Canal B/S RD-69 to 79, 70+200, 72+180, 73+450, 74+200, 75+150, 76+200, 77+15 & 78+570 Both	Satisfactory	4/7/2023	Irrigation (Water & Drainage), GOS	10/18/2023	Khairpur	450.271
2019-20 939	Rehabilitation of Sub Drain M.II & Resectioning of Mirpurkhas Main Drain	Satisfactory	1/23/2024	Irrigation (Water & Drainage), GOS	6/7/2024	Mirpurkhas	83.377
2023-24 1857	Revamping & Rehabilitation of Occupational Safety & Health Centre at Karachi	Satisfactory	12/19/2023	Labour Dept, GOS	3/27/2024	Karachi	22.302
2022-23 1591	Construction of Record Room alongwith Store Room & Provision of Elevator / Lift Facilities and Construction of Cafeteria at High Court Circuit, Larkana (Cap: 57.00 + Rev: 2.100)	Satisfactory	3/13/2023	Law P.A. & Prosecution	7/13/2023	Larkana	59.1
2022-23 1592	Construction of Bar Room, Bar Library and Additional ten (10) No. Courts at District Court Building, Malir (Cap: 241.368 + Rev: 39.373)	Satisfactory	3/21/2023	Law P.A. & Prosecution	10/5/2023	Karachi Malir	280.741
2023-24 1924	C.C Lining of Jiskani Distry-I from RD- 000 to 46+500 RDs (SDG # 6)	Satisfactory	9/29/2023	Lining of Main Canals	5/10/2024	Shaheed Benazirabad	349.524
2023-24 1926	C.C Lining of Lundki from RD-00 to Tail and Gachero Minor from RD-00 to 14+500 (SDG # 6)	Satisfactory	11/30/2023	Lining of Main Canals	5/13/2024	Shaheed Benazirabad, Naushero Feroz	841.094
2023-24 1930	Cement Concrete Lining of Kunner-II Distry from RD-0+000 to RD-21+000 (SDG # 6) (Revised on 10.05.23)	Satisfactory	4/22/2024	Lining of Main Canals	6/28/2024	Hyderabad	517.143

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 1936	Cement Concrete Lining from Head to Tail of Karampur Distry and Ghar Marho Distry (SDG # 6)	Un-Satisfactory	11/27/2023	Lining of Main Canals	3/20/2024	Thatta	376.338
2023-24 1939	Cement Concrete Lining from Head to Tail of Ghar Machi Minor, Hala Minor, Sonada Distry	Satisfactory	5/13/2024	Lining of Main Canals	5/23/2024	Thatta	414.892
2023-24 1947	C.C Lining Along Faiz Ganj Wah 80 to 163+ / CC Lining of Halepota Minor from RD-0+00 to 9+400 & CC Lining of AliNawaz Wah from RD.64+ to 139+200 (SDG # 6)	Satisfactory	9/11/2023	Lining of Main Canals	3/6/2024	Khairpur	1177.139
2023-24 1960	C.C Lining Khairpur Feeder East Canal RD-12.8 to 42.8 (SDG # 6)	Satisfactory	12/12/2023	Lining of Main Canals	5/14/2024	Khairpur	1200
2023-24 1964	Construction of C.C. Lining of Let Minor from RD-0+00 to 59+00 and Poran Minor RD - 0+00 to 13+800	Satisfactory	12/22/2023	Lining of Main Canals	5/14/2024	Naushero Feroz	475
2022-23 1609	C.C Lining of Menglo Minor from RD- 0.000 to 38+200 (SDG # 6)	Satisfactory	7/25/2023	Lining of Main Canals	11/23/2023	Naushero Feroz	227.702
2022-23 1612	Cement Concrete Lining along Dalipota-Minor from RD-0+000 to 45+100 (SDG # 6)	Satisfactory	7/24/2023	Lining of Main Canals	2/21/2024	Naushero Feroz	265.5
2022-23 1625	Cement Concrete Lining along Padhar Minor from RD-0+00 to 43+350 (SDG # 6)	Satisfactory	11/25/2022	Lining of Main Canals	11/23/2023	Badin	278.787
2023-24 1979	Establishment of Veterinary Centres in Sindh - Phase-II (SBA,Shikarpur, Tharparkar, T.M.Khan, Larkano, Ghotki, Dadu & Khairpur) (C:69.614 + R:30.250) (SDG # 2)	Satisfactory	10/19/2023	Livestock and Fisheries, GOS	4/30/2024	Larkana, Dadu	99.864
2023-24 1982	Save Buffalo Calves (Karachi, Badin, Hyderabad, Dadu,Sukkur, Khairpur, Ghotki, Larkano, Kamber at S. Kot, Kashmore at K. Kot, Shikarpur & Jacobabad) (R:407.878) (SDG #7)..	Un-Satisfactory	1/5/2024	Livestock and Fisheries, GOS	4/16/2024	Shikarpur, Jacobabad	407.878
2023-24 1982	Save Buffalo Calves (Karachi, Badin, Hyderabad, Dadu,Sukkur, Khairpur, Ghotki, Larkano, Kamber at S. Kot, Kashmore at K. Kot, Shikarpur & Jacobabad) (R:407.878) (SDG #7)	Un-Satisfactory	12/5/2023	Livestock and Fisheries, GOS	5/17/2024	Qambar Shahdadkot, Larkana	407.878
2023-24 1983	Fattening of Calves (Jamshoro, SBA, Dadu, Sukkur, Khairpur,Ghotki, Larkano, Kamber at S.Kot, Kashmore at K.Kot, Shikarpur & Jacobabad) (R:222.110) (SDG #2)	Satisfactory	10/24/2023	Livestock and Fisheries, GOS	4/2/2024	Jamshoro	222.11
2023-24 1998	Rehabilitation & Renovation of Karachi Fish Harbour - External Services(2nd revised on 21.03.18) (C: 1374.147 +R: 242.237)(SDG #14)	Un-Satisfactory	1/4/2024	Livestock and Fisheries, GOS	1/17/2024	Karachi	1616.384
2022-23 1658	Establishment of Sindh Institute of Animal Health at Karachi(C:176.199 + R.40.780) (SDG #13)	Satisfactory	7/11/2023	Livestock and Fisheries, GOS	3/27/2024	Karachi	631.798
2022-23 1660	Switching Traditional / Conventional Livestock Farming to Contemporary (R:131.970) (SDG #2)	Satisfactory	7/20/2023	Livestock and Fisheries, GOS	11/8/2023	Dadu	131.97
2022-23 1660	Switching Traditional / Conventional Livestock Farming to Contemporary (R:131.970) (SDG #2))	Satisfactory	7/13/2023	Livestock and Fisheries, GOS	11/29/2023	Ghotki	131.97
2022-23 1660	Switching Traditional / Conventional Livestock Farming to Contemporary (R:131.970) (SDG #2)	Satisfactory	4/5/2023	Livestock and Fisheries, GOS	9/12/2023	Larkana	131.97
2022-23 1661	Establishment of Rural / Backyard Poultry farming in District Ghotki & Larkano (R: 99.995) (SDG #2)	Satisfactory	7/21/2023	Livestock and Fisheries, GOS	4/17/2024	Larkana	99.995
2022-23 1687	Introduction of Bio-Floc Aquaculture in Sindh (Jamshoro, Thatta,Badin, Sujawal, TM Khan, Ghotki & Larkana) (R: 100.000) (SDG #2)..	Satisfactory	10/20/2023	Livestock and Fisheries, GOS	4/17/2024	Larkana	100
2023-24 2065	Improvement of Water supply line and Installation of Sewerage line and Paver Block, Road Carpeting in UC-38	Un-Satisfactory	2/12/2024	Local Government, GOS	6/4/2024	Karachi West	170.26

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 2066	Improvement of Water supply line and Installation of Sewerage line and Paver Block, Road Carpeting in UC-39.	Un-Satisfactory	11/13/2023	Local Government, GOS	1/3/2024	Karachi West	173.518
2023-24 2078	Rehabilitation / Improvement of Road / Sewerage Line & Water System	Un-Satisfactory	12/12/2023	Local Government, GOS	3/20/2024	Karachi Korangi	96.805
2023-24 2091	Rehabilitation of Drainage Works & Construction of New C.C.Flooding in Village Ber Sharif, Taluka Kamber (Revised) (SDG#6)	Satisfactory	1/15/2024	Local Government, GOS	6/5/2024	Qambar Shahdadkot	99.682
2023-24 2094	Widening/Reconditioning of asphalt Concrete Road from Main City gatge Chuhar Jamali Road to by-pass Chowk shah Aqeeq Road Via Main City Road including RCC Drain Nala/C.C PaverBlock Taluka Chuhar Jamali District Sujawal	Un-Satisfactory	2/28/2024	Local Government, GOS	5/10/2024	Sujawal	424.447
2023-24 2104	Providing & Laying of C.C Paver & Drainage at Village Retti/New Retti, Taluka Ubauro, District Ghotki @ Mirpur Mathelo	Satisfactory	3/13/2024	Local Government, GOS	6/4/2024	Ghotki	94.103
2023-24 2457	Construction of Civic Centre at Mula Fazal Auditorium Hall Chawkiwara Road Lyari	Satisfactory	1/11/2024	Local Government, GOS	6/28/2024	Karachi	434.627
2023-24 2484	Construction of Dumlottee Road from Dumlottee Well to M-9 & M-5 Link Road (12.3 Km)	Satisfactory	1/16/2024	Local Government, GOS	3/28/2024	Karachi	798.323
2023-24 2486	Reconditioning of road from Majeed Kerio-Mehrabpur road to Vill Dado Gohram Faqeer Zardari, UC Marvi, Taluka Sakrand Mile0/0-3/5 (5.80 Km) (Revised on 03.01.23)	Satisfactory	11/27/2023	Local Government, GOS	5/2/2024	Shaheed Benazirabad	167.79
2023-24 2505	Construction of roads alongwith drainage, Sewerage,Pipes and paving blocks in UC-2 Muslimabad, Malir Karachi	Un-Satisfactory	3/4/2024	Local Government, GOS	6/4/2024	Karachi Malir	118.3
2023-24 2506	Improvement & Reconstruction of Roads in UC-36, 35,30 Fishermen Chowrangi to Nasir Colony	Un-Satisfactory	2/13/2024	Local Government, GOS	6/4/2024	Karachi Korangi	157
2023-24 2517	Construction of road village Abdul Kareem Lashari, Construction of road village Mubarak Lashari, Construction of road village Muhammad Khan Katiyar, Construction of road village Mitho Lashari to Ragwah Mori, Construction of main road Ghulamullahto Dargah	Worst	10/10/2023	Local Government, GOS	11/24/2023	Thatta	63.5
2023-24 2520	Construction of Bridge Over Malir Nadi near Goth Siddique Jokhio, UC Choohar, District Malir Karachi	Un-Satisfactory	12/15/2023	Local Government, GOS	5/17/2024	Karachi Malir	175
2023-24 2523	Rehabilitation and Reconstruction of Roads & Laying of CC flooring / Paver Block at different areas of PS-97	Satisfactory	11/14/2023	Local Government, GOS	3/28/2024	Karachi Korangi	147.75
2023-24 2524	Improvement & Reconstruction of Roads in UC-37 Ward 1	Un-Satisfactory	11/3/2023	Local Government, GOS	12/19/2023	Karachi Korangi	81.007
2023-24 2530	Rehabilitation of road Mewa Shah Graveyard & surrounding area of District West	Satisfactory	2/15/2024	Local Government, GOS	2/28/2024	Karachi West	200.92
2023-24 2621	Construction of internal road of Shah Inayat Village Kiran Hospital Road PS100	Un-Satisfactory	3/12/2024	Local Government, GOS	5/17/2024	Karachi East	29.895
2023-24 2624	Dualization of road 15 Check post G.T. Road to War Mubarak Taluka Rohri	Un-Satisfactory	11/14/2023	Local Government, GOS	2/23/2024	Sukkur	80
2023-24 2625	Widening / Reconditioning of Road from Sukkur Barrage to Rohri City (Dual carriageway)	Satisfactory	5/10/2024	Local Government, GOS	5/27/2024	Sukkur	495
2023-24 2791	Constt: of 05 Nos. Union Council Offices in PS-73 (C:40.000+R:5.000) (SDG # 11)	Un-Satisfactory	11/15/2023	Local Government, GOS	4/26/2024	Jamshoro	45
2023-24 2792	Establishment of Theme Park at Khairpur City (Revised on 12.08.21)	Un-Satisfactory	11/17/2023	Local Government, GOS	5/29/2024	Khairpur	198.195
2023-24 2797	Development of Ghazi Abdul Rasheed Park Sukkur	Satisfactory	10/12/2023	Local Government, GOS	4/24/2024	Sukkur	199.998

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 2799	Rehabilitation of Grounds & Parks, Eid Gah Ground Ward-2, Railway Ground Ward-3, Qalandari Ground Ward-7, Park in Railway Colony Bulbul Barrick Ward-3 Park in Chandio village Adjouned to Dada Bhai village, Park in Kaleem Qazi Ground Ward-7	Un-Satisfactory	10/20/2023	Local Government, GOS	12/20/2023	Karachi South	132.477
2023-24 2800	Rehabilitation of Public Parks and Public Grounds, UC-16, 19, 24 & UC-26, District West Karachi	Un-Satisfactory	12/18/2023	Local Government, GOS	3/20/2024	Karachi West	80
2023-24 2803	Rehabilitation & Beautification of Different Areas of Rohri City District Sukkur	Satisfactory	2/12/2024	Local Government, GOS	5/20/2024	Sukkur	99.81
2023-24 2823	Installation, Upgradation & Automation of existing Traffic Signals in Karachi and Beautification of Shakra-e-Faisal and Adjacent areas of Karachi	Satisfactory	1/15/2024	Local Government, GOS	5/13/2024	Karachi	198.7
2023-24 2824	Establishment of Zoological Park at Khairpur (Ph-II) (SDG#8) (ADP # 1419 of 2020-21)	Un-Satisfactory	11/10/2023	Local Government, GOS	2/13/2024	Khairpur	54.827
2022-23 1713	Rehabilitaioin of the existing distribution system in Hyderabad (Providing Lyaing Jointing & Testing 4	Satisfactory	7/5/2023	Local Government, GOS	11/23/2023	Hyderabad	399.747
2022-23 1715	CC Block Roads in Various Villages of Qasimabad PS-47 (SDG # 9)	Satisfactory	11/11/2022	Local Government, GOS	11/2/2023	Hyderabad	299
2022-23 1717	Improvement & Enhancement of Sewerage System in Taluka City Area District Hyderabad	Satisfactory	7/6/2023	Local Government, GOS	11/23/2023	Hyderabad	414.135
2022-23 1729	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage System including Pumping Stations in District Central, Karachi	Satisfactory	10/3/2023	Local Government, GOS	11/10/2023	Karachi	149.978
2022-23 1730	Rehabilitation / Replacement / Improvement of Water Supply and Sewerage system including Pumping Stations in District South, Karachi	Satisfactory	6/19/2023	Local Government, GOS	10/6/2023	Karachi	133.771
2022-23 1735	Construction of Cover Drain/Repair of exisitbg Drain Ward No. 1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur	Satisfactory	5/2/2024	Local Government, GOS	5/27/2024	Sukkur	82.797
2022-23 1748	Construction / Rehabilitation of Main / Internal Roads, providing, sewerage line of 12 dia PE Pipe and installation of Paver blocks/ CC flooring & Street Lights in Jannat Gul Town, Al-Azam Town, Qayyum Abad, Hasan Noman Colony, Machar Colony, AllahBux G	Satisfactory	11/9/2022	Local Government, GOS	10/13/2023	Karachi East	96.466
2022-23 1755	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12	Satisfactory	11/11/2022	Local Government, GOS	7/17/2023	Karachi East	96.17
2022-23 1757	Construction / Rehabilitation of Main Roads / Internal Roads, Providing Sewerage line of 12	Satisfactory	11/14/2022	Local Government, GOS	7/17/2023	Karachi East	100
2022-23 1761	Construction of Double Road from Pehlwan Goth to Johar Police Station Gulistan-e-Johar including street lights, footpath with paving blocks, Cat eyes road markings including Sewerage line of 12\	Un-Satisfactory	4/3/2023	Local Government, GOS	1/8/2024	Karachi East	98.881
2022-23 1762	Construction of Road & Installation of Paver Blocks, Sewerage & Water Supply Line, Akhtar Colony & Kashmir Colony (UC-01)	Un-Satisfactory	1/8/2024	Local Government, GOS	5/13/2024	Karachi East	98.608
2022-23 1764	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	Satisfactory	5/26/2023	Local Government, GOS	10/10/2023	Karachi East	84.749
2022-23 1767	Providing and laying of Water Supply 4	Satisfactory	4/5/2023	Local Government, GOS	10/10/2023	Karachi East	89.893
2022-23 1783	CC Flooring, Sewerage Line, Water Supply Line & Establishment of Basic Health Center (Dispensary) in UC-11 Baloch Goth.	Satisfactory	3/20/2023	Local Government, GOS	7/18/2023	Karachi West	122.284
2022-23 1787	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-17, UC-27 & UC-28	Satisfactory	6/13/2023	Local Government, GOS	7/6/2023	Karachi West	117.577

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1789	Improvement of Water Supply line, installation of Sewerage line, CC Flooring, Ground and Road Carpeting in UC-20, UC-21 & UC-22.	Satisfactory	4/10/2023	Local Government, GOS	7/17/2023	Karachi West	86.039
2022-23 1791	Construction of Roads, laying of Paver Blocks, Installation of Sewerage System in UC-16, Ghaziabad	Un-Satisfactory	12/19/2022	Local Government, GOS	1/2/2024	Karachi West	46.91
2022-23 1796	Improvement of Sewerage line Boosting Pump, Drainage line and Carpeting of Road in UC-2 Labour Square	Satisfactory	4/12/2023	Local Government, GOS	10/13/2023	Karachi West	81.093
2022-23 1798	Improvement of Water Supply, Sewerage line and Road carpeting in UC-5 Pak Colony	Satisfactory	3/21/2023	Local Government, GOS	7/6/2023	Karachi West	56.222
2022-23 1826	Providing & Laying of Paver Block in Different Streets of UC-41, UC-42, UC-43, UC-44, UC-45 and UC-46 in DMC Keamari	Satisfactory	5/26/2023	Local Government, GOS	7/6/2023	Karachi Keamari	95.99
2022-23 1830	Paver Block and Carpeting of Road in different areas of UC-2 Mowach Goth.	Un-Satisfactory	10/6/2022	Local Government, GOS	4/18/2024	Karachi Keamari	96.326
2022-23 1832	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-3 Keamari Town.	Un-Satisfactory	6/14/2023	Local Government, GOS	11/24/2023	Karachi Keamari	106.576
2022-23 1834	Providing / Laying Paver R.C.C Sewerage Pipe Line and C.C Flooring I/C Cleaning of Nallahs at different places of UC-41, UC-42, UC-43, UC-44, UC-45 & UC-46 in DMC Keamari	Un-Satisfactory	5/30/2023	Local Government, GOS	8/16/2023	Karachi Keamari	92.88
2022-23 1837	Improvement of Water Supply and installation of Sewerage line and Carpeting of Road in UC-30 & 31 Baldia Town.	Satisfactory	5/29/2023	Local Government, GOS	9/12/2023	Karachi Keamari	146.796
2022-23 1846	Providing / Laying & Replacement of Damaged & Unserviceable Sewerage lines in different areas of PS-97	Satisfactory	3/27/2023	Local Government, GOS	10/13/2023	Karachi Korangi	75.857
2022-23 1857	Rehabilitation / Improvement of Road / Sewerage Line & Water System in the area of PS-123, 124	Un-Satisfactory	3/5/2024	Local Government, GOS	5/17/2024	Karachi Central	96.9
2022-23 1866	Providing & Laying of Paver Block at Various Streets / Roads of UC-1, UC-2, UC-22 to UC-39 and UC-45 to UC-50 and Ward Ito 9 Cantt: Taluka City Hyderabad	Satisfactory	7/10/2023	Local Government, GOS	5/17/2024	Hyderabad	292.952
2022-23 1870	Providing & Laying of Paver Block in Hingorno Town Taluka Sindhri 8000 RFT	Satisfactory	7/11/2023	Local Government, GOS	11/22/2023	Mirpurkhas	44.477
2022-23 1872	Providing Sewerage Lines in Various wards / UCs of Taluka Nawabshah Juma Khan Zardari, Village Ghazi Khan Hoat and village Khairshah, Haqani Colony, Badal Colony, Sumera Colony, Ghulam Hyder Shah Colony, Bhattai Colony, Housing Society, Society & Hanif Ka	Satisfactory	9/21/2023	Local Government, GOS	4/24/2024	Shaheed Benazirabad	72.593
2022-23 1874	Improvement of Drainage and Paving Block from Town Committee Via Phulji Station..	Satisfactory	9/12/2023	Local Government, GOS	6/28/2024	Dadu	98.613
2022-23 1875	Improvement of Drainage and Paving Block of Piyaro Station Road...	Satisfactory	9/13/2023	Local Government, GOS	6/28/2024	Dadu	98.826
2022-23 1876	Improvement of Road from Indus Highway Degree College to Theba VIP Road Mehar Link to Dua Hospital i/c Drainage on both sides & Paving Block	Satisfactory	7/7/2023	Local Government, GOS	5/3/2024	Dadu	98.4
2022-23 1898	Construction of Paver Block Road at different streets of Town Khanpur, Village Abdu, Dahar, Mangria Muhalla, Master Bhayo House, Town Committee Chak, Qasim Bhayo & Different Villages of UC Mungrani & UC Ruk	Un-Satisfactory	9/21/2023	Local Government, GOS	4/29/2024	Shikarpur	98.781

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 1900	Providing & Laying of Paver Block in Various Links of Muhallah Osta Gahi, Muhallah Dabar, Muhallah Shaikh and Internal Streets of Muhallah Bhurgari upto Bhurgari Regular Khairpur including Masonery Structure (340426 Sft) Taluka Khairpur	Un-Satisfactory	3/20/2023	Local Government, GOS	2/20/2024	Khairpur	80
2022-23 1904	Providing of Drainage System & Paver Block City Pir Esso U.C Kamal Dero Taluka Gambat,	Un-Satisfactory	4/17/2023	Local Government, GOS	12/11/2023	Khairpur	50
2022-23 1906	Providing & Laying of CC Paver from Civil Hospital to Mangrio Petrol Pump Daharki City	Satisfactory	7/14/2023	Local Government, GOS	11/14/2023	Ghotki	106.34
2022-23 1907	Providing & Laying of CC Paver Mirpur Mathelo City	Satisfactory	3/21/2023	Local Government, GOS	4/24/2024	Ghotki	112.605
2022-23 2100	Establishment of City Hall at Khairpur (SDG # 9)	Un-Satisfactory	3/5/2024	Local Government, GOS	6/10/2024	Khairpur	142
2022-23 2146	Improvement / Rehabilitation of Mubarak Shaheed Road from Cantt General Hospital to Shahrah-e-Faisal, Karachi (2.65 Km)(Revised on 04.06.21)	Satisfactory	7/10/2023	Local Government, GOS	10/13/2023	Karachi	224.612
2022-23 2157	Construction/Rehabilitation of Roads , Sewerage and C.C. Flooring in Dumba Goth, District Malir, Karachi (Revised on 19.05.22)	Un-Satisfactory	4/10/2023	Local Government, GOS	1/3/2024	Karachi	311.883
2022-23 2181	Reconstruction / Rehabilitation of roads, Drain work and Paver Blocks C.C flooring at UC45 Gulshan e Sikandarabad District Keamari Karachi	Satisfactory	5/29/2023	Local Government, GOS	7/6/2023	Karachi Keamari	99.493
2022-23 2184	Construction / Rehabilitation of Roads, Drain Work and Paver Blocks C.C flooring at UC 42 Machar Colony District Keamari Karachi	Un-Satisfactory	5/31/2023	Local Government, GOS	11/8/2023	Karachi Keamari	49.809
2022-23 2196	Construction asphalt road (New / Repair) various roads with drainage Municipal Committee Rohri. Repair of Pedestrian path ways. Roads surface and repairing of old Sukkur Channel and lands down bridge, road	Satisfactory	10/26/2022	Local Government, GOS	7/13/2023	Sukkur	99.144
2022-23 2201	Widening & reconditioning of road, paver block streets and drainage at Moro city	Satisfactory	10/18/2023	Local Government, GOS	2/27/2024	Naushero Feroz	160.062
2022-23 2207	Recond: / Imp: of Road Naoukot Fazal Bhambro Road to Nafees Nagar to Ali Hassan Gurgez to Shanker Bheel to Shadman Gurgez.	Satisfactory	7/14/2023	Local Government, GOS	11/22/2023	Mirpurkhas	139.552
2022-23 2214	Construction / Rehabilitation of various Roads in PS-64 Ganjo Takar Phatak to New Ali Asgarabad Phatak, Ganjo Takar Phatak to Allah Dino Khumarn, Village Jani Rind Road to Noonari Goth & UC 86,87,91,92,94 & Other City Areas Taluka Latifabad Hyderabad	Satisfactory	7/17/2023	Local Government, GOS	6/10/2024	Hyderabad	174.332
2022-23 2216	Construction of road from Seerani Kadhan road @ point Ahmed Shah Mori to Lakho Pir along with inspection path of Noor Wah (12.00 Km)	Satisfactory	7/19/2023	Local Government, GOS	11/22/2023	Badin	99.316
2022-23 2217	Construction of road from Iqbal Sarejo Umer Mallah road to Village Mir Hoat Haji Vikio Khaskheli and Bakar Mori upto Arab Mallah i/c link Ramzan Mandhro (11.80 Km)	Satisfactory	7/19/2023	Local Government, GOS	4/2/2024	Badin	99.331
2022-23 2218	Improvement / Construction of road from Badin Seerani road to connect Pathan Parhyar road via Haji Parhyar (Construction 3.40 Km, improvement 9.00 Km)	Un-Satisfactory	7/20/2023	Local Government, GOS	5/3/2024	Badin	99.323
2022-23 2219	Improvement / Construction of road from water supply post office road to abu Shaikha (Allah Dino Soomro) i/c link road from Badin Seerani road Ghulam Rasool Lutter (Construction 6.00 Km, improvement 7.60 Km)	Satisfactory	7/20/2023	Local Government, GOS	2/14/2024	Badin	99.215

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2241	Construction of Roads Paver Block Street and improvement of Sewerage system in UC Khaldabad and UC Cattal Colony(PS-90) District Malir, Karachi	Un-Satisfactory	6/15/2023	Local Government, GOS	10/6/2023	Karachi Malir	92.256
2022-23 2252	Construction / Rehabilitation of Primary & Secondary Roads of Sukkur District	Satisfactory	9/4/2023	Local Government, GOS	4/25/2024	Sukkur	198.95
2022-23 2393	Rehabilitation & Completion of Remaining Civil Works of Cattle Colony at Sukkur (C:179.187 & R:19.767)	Satisfactory	4/20/2023	Local Government, GOS	2/20/2024	Sukkur	198.954
2022-23 2395	Establishment of Cattle Colony at Rohri	Satisfactory	9/5/2023	Local Government, GOS	4/24/2024	Sukkur	399.939
2022-23 2397	Providing and Fixing of Animatronics\` Dinos at Safari Park - Karachi (Revised on 21.01.22)	Satisfactory	7/3/2023	Local Government, GOS	6/28/2024	Karachi	99.956
2022-23 2405	Beautification of M.C Rohri District Sukkur	Satisfactory	12/16/2022	Local Government, GOS	2/20/2024	Sukkur	51.953
2022-23 2412	Construction of Park and Playground in UC-30 & 31	Satisfactory	6/16/2023	Local Government, GOS	7/6/2023	Karachi South	100
2022-23 2448	Development of Township in Major Urban Centers (50,000 120Square Yard Plots with All Civic Services (Chairman sb Directives)	Un-Satisfactory	6/9/2023	Local Government, GOS	12/11/2023	Jamshoro	9420.88
2022-23 2448	Development of Township in Major Urban Centers (50,000 120 Square Yard Plots with All Civic Services,.	Un-Satisfactory	6/7/2023	Local Government, GOS	12/11/2023	Khairpur	9420.88
2021-22 1377	Providing Sewerage lines in PS-24 (SDG # 6.)	Satisfactory	6/22/2023	Local Government, GOS	10/23/2023	Shaheed Benazirabad	60.409
2021-22 1416	Main Water Supply System in Block 13-A to 11-A & Block 11-B to Block-2, 3 & 3-A of Hawksbay Scheme -42 LDA Karachi	Un-Satisfactory	2/21/2022	Local Government, GOS	1/3/2024	Karachi	150.986
2021-22 1421	Rehabilitation/Replacement/Improvement of Water Supply System by P/L 12	Satisfactory	6/20/2023	Local Government, GOS	10/10/2023	Karachi	35.91
2021-22 1423	Rehabilitation / Improvement and replacement of water and sewerage system in UC-29, 30 and 31 Saddar, DMC South	Satisfactory	6/21/2023	Local Government, GOS	10/10/2023	Karachi	29.13
2022-23 2469	Construction of U-Turn at Natha Khan Bridge (SDG # 9)	Un-Satisfactory	6/1/2023	Mega Schemes for Karachi City	1/8/2024	Karachi	214.466
2022-23 2471	Rehabilitation / Reconstruction of Shahrah-e-Noor Jehan from Abdullah College to Qalandaria Chowk	Satisfactory	6/2/2023	Mega Schemes for Karachi City	10/23/2023	Karachi	1303.83
2022-23 2474	Reconstruction of Rafiqi Shaheed Road and Kalapul Road from Shahrah-e-Faisal to Main Korangi Road	Satisfactory	10/6/2022	Mega Schemes for Karachi City	7/17/2023	Karachi	208.473
2022-23 2479	Construction of Flyover and Underpass at Johar Chowrangi Intersection	Un-Satisfactory	6/6/2023	Mega Schemes for Karachi City	1/2/2024	Karachi	2046.301
2022-23 2486	Improvement of roads from MA Jinnah Road to I I Chundrigar Road (Mumtaz Hassan road, Hasrat Mohani road, Paper Marketroad) District South	Satisfactory	7/3/2023	Mega Schemes for Karachi City	6/28/2024	Karachi South	62.797
2023-24 3303	Rehabilitation / Renovation of Temple & Satsang Hall at Village Doonhon Ibrahim Shah Taluka Babarloi District Khairpur	Satisfactory	9/12/2023	Minorities & Affairs, GOS	2/23/2024	Khairpur	19.835
2023-24 3304	Rehabilitation / Renovation of Domes & Finishing Work i/c Floor Tile of Shri Krishana Mandir at Gambat District Khairpur	Satisfactory	11/10/2023	Minorities & Affairs, GOS	1/3/2024	Khairpur	19.812
2023-24 3306	Rehabilitation / Renovation of Jindpir Darbar old Sukkur	Satisfactory	9/8/2023	Minorities & Affairs, GOS	2/21/2024	Sukkur	19.815
2023-24 3310	Rehabilitation of Hindu Massan at Hayat Pitafi Mirpur Mathelo District Ghotki	Satisfactory	12/28/2023	Minorities & Affairs, GOS	5/6/2024	Ghotki	19.8
2023-24 3311	Repair & Renovation of Daharki Darbar District Ghotki	Satisfactory	12/29/2023	Minorities & Affairs, GOS	5/13/2024	Ghotki	20
2022-23 2534	Extension Work of Dharamshala, Larkana City	Satisfactory	7/27/2023	Minorities & Affairs, GOS	5/17/2024	Larkana	19.835

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2021-22 1941	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu,Thatta, Tharparkar, Jamshoro, Hyderabad, Larkano, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar) (Revised)	Satisfactory	8/21/2023	Minorities & Affairs, GOS	3/8/2024	Larkana	75.829
2021-22 1944	Implementation of various Development Schemes of Minorities in Sindh (Jamshoro, Ghotki, Karachi, Khairpur, Jacobabad, Larkano, Kashmore, Sukkur, N.Feroze, Dadu, SBA, Sanghar, Mirpurkhas, Umerkot, Tharparkar, Matiari, Jacobabad, Jamshoro, Thatta, Shikarpur)	Satisfactory	3/22/2024	Minorities & Affairs, GOS	5/31/2024	Ghotki	704.565
2023-24 3421	Reconstruction of District & Sub Divisional Field offices-cumResidences of Sindh Bureau of Statistics at Khairpur, Tharimirwah, Kotdiji	Satisfactory	1/8/2024	Planning & Development, GoS	5/14/2024	Khairpur	82.03
2022-23 2621	Reconstruction, Renovation & Rehabilitation of Divisional/ District & Sub-Divisional Offices-cum- Residences of Bureau of Statistics, Sindh. (Hyderabad, Jamshoro, Dadu, SBA, Badin, T.M.Khan, Sukkur, Ghotki, Larkano, Jacobabad, Shikarpur, Mirpurkhas, Tharparkar)	Un-Satisfactory	3/25/2024	Planning & Development, GoS	5/24/2024	Larkana	302.15
2022-23 2622	ADP No: 3416 2023-24 Construction / Re-Construction of District Office Cum Residence of Sindh Bureau Of Statistics AtKamber	Un-Satisfactory	9/26/2023	Planning & Development, GoS	11/24/2023	Qambar Shahdadkot	21.87
2022-23 2643	Rehabilitation of RTI, Karachi (C:39.77+R:26.149) (SDG # 3,5)	Satisfactory	1/15/2024	Population Welfare, GOS	3/28/2024	Karachi	65.919
2022-23 2645	Remaining works of RHS-A Centre at Dokri (C:2.847) (SDG # 3, 5)	Satisfactory	6/7/2023	Population Welfare, GOS	9/7/2023	Larkana	2.847
2022-23 2657	Construction of Office Building at Thatta (Compliance)	Satisfactory	3/6/2024	Provincial Ombudsman, GOS	5/10/2024	Thatta	53.059
2023-24 3469	Rehabilitation of Urban Water Supply Scheme Chuhar Jamali(SDG # 6)	Satisfactory	2/29/2024	Public Health Engineering, GOS	5/13/2024	Sujawal	100.982
2023-24 3483	Water Supply Scheme Arazi Via Bubuk and adjoining 26 Nos Villages from Indus Source Taluka Sehwan (SDG # 6)	Satisfactory	2/19/2024	Public Health Engineering, GOS	4/30/2024	Jamshoro	491.134
2023-24 3484	Improvement & Extension Water Supply/Sewerage System Bhit shah (SDG#6)	Worst	11/13/2023	Public Health Engineering, GOS	5/24/2024	Matiari	391.1
2023-24 3485	Improvement and Extention of Urban Water Supply Scheme T.M.Khan City (SDG#6)	Un-Satisfactory	1/16/2024	Public Health Engineering, GOS	6/4/2024	Tando Muhammad Khan	197.624
2023-24 3487	Water Supply Scheme of Village and Union Council Khabri Bhatt (Revised on 16.05.23)	Satisfactory	12/5/2023	Public Health Engineering, GOS	6/28/2024	Shikarpur	77.799
2023-24 3490	Construction of 3.0 MGD Filtration Plant i/c distribution network for Water Supply Scheme Rohri Taluka Sukkur (Revised on 19.04.2023)	Un-Satisfactory	12/6/2023	Public Health Engineering, GOS	4/30/2024	Sukkur	641.518
2023-24 3496	Urban Water Supply Scheme Shah Purchakar Phase-II	Satisfactory	10/5/2023	Public Health Engineering, GOS	4/25/2024	Sanghar	306.405
2023-24 3537	Water Supply Scheme (Filtration) Sakrand Town (SDG # 6) ADP No.2068 (2021-22).	Satisfactory	10/27/2023	Public Health Engineering, GOS	4/3/2024	Shaheed Benazirabad	400.473
2023-24 3582	Improvement & Extention of Urban Drainage Scheme Tando	Un-Satisfactory	1/22/2024	Public Health Engineering, GOS	6/6/2024	Hyderabad	100
2023-24 3587	Contruotion of Drainage Scheme Garho City (SDG # 6).	Un-Satisfactory	9/4/2023	Public Health Engineering, GOS	6/28/2024	Thatta	89.647
2023-24 3611	Rural Drainage Scheme Saeed Khan Laghari UC Bhanote Taluka Hala (SDG#6).	Un-Satisfactory	10/6/2023	Public Health Engineering, GOS	4/25/2024	Matiari	38.449
2023-24 3619	Construction of Drainage Scheme at Various areas of Newpindand Micro Tower Sukkur and Qureshi Goth (Revised on 16.05.23)	Un-Satisfactory	11/14/2023	Public Health Engineering, GOS	4/26/2024	Sujawal	176.775
2023-24 3624	Improvement & Extension of Drainage Scheme Khipro. (SDG # 6)	Satisfactory	10/9/2023	Public Health Engineering, GOS	2/21/2024	Sanghar	333.584
2023-24 3625	Improvement & Extension of Urban Drainage Scheme Shahpur Chakkar (SDG#6).	Satisfactory	10/10/2023	Public Health Engineering, GOS	2/20/2024	Sanghar	199.447

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 3627	Construction of Drainage Scheme Fazal Hussain Chakarani & Khair Mohammad Road Taluka Tando Adam (SDG # 6).	Satisfactory	10/13/2023	Public Health Engineering, GOS	2/20/2024	Sanghar	38.922
2023-24 3634	Paver Block and C.C Drain in Various villages of Taluka Mirokhan and Sujawal and Kamber (SDG # 6).	Satisfactory	10/23/2023	Public Health Engineering, GOS	5/20/2024	Qambar Shahdadkot	137.12
2023-24 3641	Improvement & Extension of Drainage Scheme Aadilpur including Shaikh Muhalla Taluka Ghotki (SDG # 6) (Revised)	Satisfactory	2/26/2024	Public Health Engineering, GOS	5/20/2024	Ghotki	97.455
2023-24 3643	Drainage Scheme for Tharu Shah Taluka Bhiria (SDG # 6).	Un-Satisfactory	10/17/2023	Public Health Engineering, GOS	2/27/2024	Naushero Feroz	159
2023-24 3696	Construction of Surface Drains, CC Block and Paver Block at different Mohallas of Town Committee Hingorja, UC Sami, Village Niwaro UC Meerak, Village Razal Memon, UC Madd, Village Haji Abdul Rahim Bhutto UC Rasolabad, Abbasi Mohallaand Mir Mohalla Commi	Satisfactory	2/13/2024	Public Health Engineering, GOS	6/28/2024	Khairpur	62.789
2023-24 3698	Drainage & paver scheme in various villages of Taluka Khairpur, Pipri, village Arbab Shaikh, village Muhammad Saleh Katohar & village Muhammad Murad, drainage, village Bhano Goth, scheme, village Sanjar Katohar, Drainage, village GajjanPahore, Eidal Phul	Un-Satisfactory	1/4/2024	Public Health Engineering, GOS	5/3/2024	Khairpur	150
2023-24 3705	Improvement Extension Drainage Scheme Kazi Ahmed (SDG#6)	Satisfactory	3/18/2024	Public Health Engineering, GOS	6/28/2024	Shaheed Benazirabad	431.378
2023-24 3707	Improvement & Extension of Urban Drainage Scheme Kandiaro, Taluka Kandiaro (SDG#6).	Satisfactory	1/23/2024	Public Health Engineering, GOS	6/28/2024	Naushero Feroz	269.982
2023-24 3741	Rural Drainage Scheme Mashak (old) Mashak (New) & Abdul Hameed para, UC-Gohram Mari, Taluka Sakrand (SDG#6) ADPNo.2175 (2021-22).	Satisfactory	12/15/2023	Public Health Engineering, GOS	3/8/2024	Shaheed Benazirabad	62.209
2023-24 3878	Rehabilitation of Non-functional Water Supply & Drainage Schemes in District Ghotki @ Mirpur Mathelo (Phase-II) (SDG # 6).	Satisfactory	12/8/2023	Public Health Engineering, GOS	2/26/2024	Ghotki	110.958
2022-23 2664	Installation of 10 Reverse Osmosis Plant (RO Plants) in UC Gabo Pat Keamari Town Karachi (SDG # 6).	Satisfactory	5/9/2023	Public Health Engineering, GOS	5/13/2024	Karachi	97.876
2022-23 2674	Construction of RCC Underground Reservoir for R.O Plant, Improvement / Extension of Distribution Network for Mithi and Islamkot (SDG # 6)	Un-Satisfactory	9/5/2023	Public Health Engineering, GOS	4/2/2024	Tharparkar	485.69
2022-23 2675	Water Supply Scheme Sokliyo to Veeranio Sokliyo to Behrao Via Rahirari (SDG # 6)	Satisfactory	9/6/2023	Public Health Engineering, GOS	5/10/2024	Tharparkar	36.9
2022-23 2677	Improvement of Water Supply Scheme in Town Committee Chhachhro & Town Committee Kheme-jo-Par (SDG # 6)	Satisfactory	4/28/2023	Public Health Engineering, GOS	11/2/2023	Tharparkar	65.833
2022-23 2694	Improvement & Extension of Water Supply Scheme for Kotri City (SDG # 6)	Satisfactory	4/7/2023	Public Health Engineering, GOS	11/27/2023	Jamshoro	160.9
2022-23 2710	Improvement & Extension Water Supply Scheme Bhirya City (Revised on 20.04.17) (SDG # 6).	Satisfactory	7/18/2023	Public Health Engineering, GOS	5/6/2024	Naushero Feroz	98.37
2022-23 2716	Water Supply Scheme (Filtration) Dadu (SDG # 6)	Satisfactory	7/5/2023	Public Health Engineering, GOS	2/23/2024	Dadu	754.737
2022-23 2722	Installation of 02 Nos R.O Plant for Village Hashim Chawro UC Ratokot, Jaro Khan Jogi UC Kothi Kandhoru Taluka Larkano 09 Nos. of Colverts for Village Sabzal Mugheri, Taj Muhammad Mugheri (Bado Wah.), Mahi Khan Talo Khan Jagirani (Bdo Wah) Kirrir Khan Mug	Satisfactory	4/12/2023	Public Health Engineering, GOS	1/10/2024	Larkana	35
2022-23 2770	Construction of New Drainage System & CC Blocks at UC Halepoto, UC Seri & UC Almani. (SDG # 6)	Un-Satisfactory	9/12/2023	Public Health Engineering, GOS	3/6/2024	Hyderabad	78.019

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 2782	Improvement & Extension of Urban Drainage Scheme Ver Taluka Ghorabari(SDG # 6).	Satisfactory	12/6/2023	Public Health Engineering, GOS	3/28/2024	Thatta	118.252
2022-23 2805	Rehabilitation of Urban Drainage Scheme Chuhar Jamali District Sujawal (RGC)	Un-Satisfactory	2/29/2024	Public Health Engineering, GOS	5/13/2024	Sujawal	77.143
2022-23 2812	CC Paving Blocks & Drains for Various Villages of UC Loung Bhatti Taluka Rohri (SDG # 6).	Un-Satisfactory	3/17/2023	Public Health Engineering, GOS	2/23/2024	Sukkur	80
2022-23 2818	Construction of Drainage Scheme at Bachal Shah Miani Sukkur (SDG # 6).	Un-Satisfactory	2/26/2024	Public Health Engineering, GOS	4/30/2024	Sukkur	133.3
2022-23 2820	Construction of Drainage Scheme Allahabad Colony Sukkur (SDG # 6).	Satisfactory	3/22/2023	Public Health Engineering, GOS	5/2/2024	Sukkur	90.793
2022-23 2831	Rural Drainage Scheme Khabri Taluka Lakhi (SDG # 6) (Revised on 29.04.22)	Un-Satisfactory	9/22/2023	Public Health Engineering, GOS	4/26/2024	Shikarpur	35.996
2022-23 2844	Improvement & Extension of Drainage Scheme Mehar Taluka Mehar (SDG # 6)	Satisfactory	7/20/2023	Public Health Engineering, GOS	4/2/2024	Dadu	339
2022-23 2846	Rural Drainage Scheme Mubarakpur Taluka Miro Khan (SDG # 6).	Satisfactory	5/26/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shahdadkot	15
2022-23 2848	Construction of C.C Drains and Paver Blocks in UC's (05 Nos.) of Taluka Shahdadkot (SDG # 6).	Satisfactory	7/10/2023	Public Health Engineering, GOS	2/14/2024	Qambar Shahdadkot	100
2022-23 2850	Paver Block and C.C Drains in Various Muhallas of Mirokhan City (SDG # 6).	Un-Satisfactory	9/30/2023	Public Health Engineering, GOS	3/8/2024	Qambar Shahdadkot	52.18
2022-23 2868	Paver Block & CC Drains from Allah Park Tower to Shahdadkot Naka Bab-e-Zulfiqar via Rest House and Kamber Lashari Road (2.0 Kms) at Taluka Ratodero (SDG # 6).	Satisfactory	7/11/2023	Public Health Engineering, GOS	1/9/2024	Larkana	66.508
2022-23 2869	Paver Block & CC Drains from Allah Wali Masjid to AbdulWahid Soomro Gate via New Eid Gah and Massan (1.50 kms) at Taluka Ratodero (SDG # 6).	Un-Satisfactory	9/29/2023	Public Health Engineering, GOS	5/2/2024	Larkana	45.734
2022-23 2877	Drainage Scheme Village Pir Muhammad Bhutto, UC Ranwati, Taluka Ubauro (SDG # 6).	Satisfactory	7/13/2023	Public Health Engineering, GOS	11/29/2023	Ghotki	72.966
2022-23 2880	Drainage Scheme Mirpur Mathelo (SDG # 6)	Un-Satisfactory	9/14/2023	Public Health Engineering, GOS	2/28/2024	Ghotki	380.884
2022-23 2882	Rural Drainage for Village Syed Ibrahim Shah UC-Buchery Taluka Daur (SDG # 6).	Satisfactory	11/17/2022	Public Health Engineering, GOS	10/17/2023	Shaheed Benazirabad	26.15
2022-23 2883	Drainage Scheme for Various Wards of Nawabshah City (SDG#6)	Satisfactory	7/31/2023	Public Health Engineering, GOS	2/15/2024	Shaheed Benazirabad	118.835
2022-23 2885	Improvement & Extension of Urban Drainage Scheme Sakrand Town (Phase-III) (SDG # 6.)	Satisfactory	1/30/2024	Public Health Engineering, GOS	4/24/2024	Shaheed Benazirabad	196.234
2022-23 2890	Paver Block and Drains Town Committees Naushehro Feroze and Mithiani (SDG#6).	Satisfactory	7/21/2023	Public Health Engineering, GOS	11/23/2023	Naushehro Feroz	86.3
2022-23 2894	Construction of Surface Drains, CC Toping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Municipal Committee Moro Taluka Moro (SDG # 6).	Satisfactory	7/19/2023	Public Health Engineering, GOS	11/29/2023	Naushehro Feroz	142.255
2022-23 2914	Drainage and Paver Schemes in Various Villages of Khairpur and Kotdiji (SDG # 6)	Un-Satisfactory	4/4/2023	Public Health Engineering, GOS	2/15/2024	Khairpur	94.02
2022-23 2991	Providing and Installation of Solar System for Rurul Water Supply and Drainage Schemes in Sindh Phase II (SDG # 6)	Un-Satisfactory	11/14/2022	Public Health Engineering, GOS	2/13/2024	Badin	1575.944
2022-23 3040	Construction of Road from Main Shaikh Bhirkioy Road to Mukhan Morri via Buksho Leghari to Link Road Village Urs Talpur via Gothana Minor side UC Tando Mari.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	6/28/2024	Hyderabad	20
2022-23 3044	Construction of Road from Link Road Muhammad Thebo to Khari Mir Khadim Hussain via Haji Bux Ali Tangri.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	6/28/2024	Hyderabad	20

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3047	Reconditioning of Road and Retaining Wall from Indus Highway to Watio Khoso Road and Improvement of Road from Indus Highway to Village Khudad Pathan.	Un-Satisfactory	4/7/2023	Public Health Engineering, GOS	12/1/2023	Dadu	20
2022-23 3057	Reconditioning of Road from Village Khairo Dhero to Village Allah Bux Hakro via Lashari Bridge including Paver Block and CC Drain, Taluka Ratodero.	Un-Satisfactory	7/6/2023	Public Health Engineering, GOS	4/25/2024	Larkana	110
2022-23 3058	Reconditioning of Road from Wasayo Bhutto Road to Village Jan Muhammad Arbani Taluka Ratodero.	Satisfactory	4/12/2023	Public Health Engineering, GOS	10/17/2023	Larkana	10
2022-23 3066	Electrification of Off Grid areas through Solar Technology, Schools & Villages (R:2000.000) (SDG # 7)	Un-Satisfactory	4/10/2023	Public Health Engineering, GOS	12/19/2023	Matari	2000
Non-ADP	Replacement Of Damaged Outdated Rising Main for Saleemabad Disposal Work Khairpur	Satisfactory	7/22/2022	Public Health Engineering, GOS	7/13/2023	Khairpur	30.479
2021-22 2071	Water Supply Scheme Mir Mushtaque Ahmed Bijarani UC Karampur Taluka Tangwani	Satisfactory	3/22/2023	Public Health Engineering, GOS	9/7/2023	Kashmore	10
2021-22 2077	Water Supply Scheme Village Kot Ghulam Shah UC Rowanti Taluka Kamber (SDG # 6).	Satisfactory	5/31/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shaddadkot	15
2021-22 2161	Rural Drainage Scheme Aali Khabhar UC Khabhar Taluka Warah (SDG # 6).	Satisfactory	5/23/2023	Public Health Engineering, GOS	10/16/2023	Qambar Shaddadkot	20
Non-ADP	Rural Drainage Scheme Dodo Khan khaskheli & Mureed Khnan Zardari	Un-Satisfactory	12/14/2023	Public Health Engineering, GOS	5/23/2024	Shaheed Benazirabad	19.71
2020-21 1727	Construction of Drainage Scheme Bughan City UC Ketu Bander Thatta (ADP No.2081 2017-18)	Worst	2/19/2024	Public Health Engineering, GOS	5/17/2024	Thatta	34.145
2019-20 2069	Rehabilitation of Water Supply Scheme Saban Balhoro. (ADP No.2036 2017-18)	Un-Satisfactory	3/8/2023	Public Health Engineering, GOS	10/23/2023	Dadu	7.956
2018-19 1653	Construction of RCC covered Nala from Railway Phatak to Taj Colony disposal work Nawabshah (SDG # 6)	Satisfactory	12/15/2023	Public Health Engineering, GOS	6/28/2024	Shaheed Benazirabad	22.113
2017-18 2145	Construction of CC Drains and CC Block at various UCs of Larkana (20 Villages) (SDG # 6)	Un-Satisfactory	4/28/2023	Public Health Engineering, GOS	4/30/2024	Larkana	40
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515)	Satisfactory	3/26/2024	Rehabilitation (PDMA), GOS	5/13/2024	Shaheed Benazirabad	891.853
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515) (as per directives of Chairman sb)	Satisfactory	3/18/2024	Rehabilitation (PDMA), GOS	5/13/2024	Larkana	891.853
2023-24 4011	Establishment of Regional Offices of PDMA (SDG # 13) (C:861.338+R:30.515)	Satisfactory	3/13/2024	Rehabilitation (PDMA), GOS	5/13/2024	Mirpurkhas	891.853
2023-24 4024	Maintenance & Repair of 333 Flats at Railway Station and PBC Landhi Karachi (SDG # 9)	Un-Satisfactory	2/1/2024	S.G.A and Coordination, GOS	2/20/2024	Karachi	358.542
2023-24 4049	Establishment of Central Record Room (CRR) in SGA&CD (Revised on 06.05.21) (SDG # 9)	Un-Satisfactory	11/8/2023	S.G.A and Coordination, GOS	1/3/2024	Karachi	185.395
2023-24 4065	Establishment of Rehabilitation Center for Drug Addicts at Karachi (C:63.238 + R:10.690) (SDG # 3)	Satisfactory	11/7/2023	Social Welfare, GOS	1/2/2024	Karachi Central	73.928
2023-24 4069	Establishment of Rehabilitation Center for Senior Citizens in District Thatta (C:61.220 + R:17.086) (SDG # 5 & 10)	Satisfactory	9/5/2023	Social Welfare, GOS	11/24/2023	Thatta	78.306
2023-24 996	Establishment of Autism Rehabilitation & Training Centre at Sukkur C: 79.976 + R:10.024) (SDG#4)	Satisfactory	11/3/2023	Special Education	2/20/2024	Sukkur	90
2023-24 4083	Construction of Athletic Track and Football Ground at Karachi, Sukkur & Larkano	Un-Satisfactory	9/7/2023	Sports & Youth Affairs, GOS	4/26/2024	Sukkur	579.874
2023-24 4092	Construction of Grassy Cricket Ground with Pavilion at Adilpur.	Satisfactory	2/29/2024	Sports & Youth Affairs, GOS	5/15/2024	Ghotki	43.997

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4104	Construction of Multipurpose Sports Hall i/c Walking Track Makhdoom Bilawal Cooperative Housing Society (Revised on 14.04.23)	Satisfactory	1/22/2024	Sports & Youth Affairs, GOS	3/27/2024	Karachi Korangi	153,996
2023-24 4107	Construction of Mini Stadium Bhambha Remaining Work i/c External Electrification at village Bhambha, Taluka Sehwan (Revised on 22.03.22)	Satisfactory	11/2/2023	Sports & Youth Affairs, GOS	5/10/2024	Jamshoro	100
2023-24 4110	Establishment of Indoor Sports Complex at Pakistan Steel Cadet College	Satisfactory	10/25/2023	Sports & Youth Affairs, GOS	4/18/2024	Karachi Malir	55
2023-24 4111	Construction of Futsal Ground for Ladies at Government Girls College..	Satisfactory	1/24/2024	Sports & Youth Affairs, GOS	6/28/2024	Jacobabad	44
2023-24 4116	Construction of Grassy Cricket Ground at Sahib Khan Lund.	Satisfactory	1/19/2024	Sports & Youth Affairs, GOS	5/10/2024	Ghotki	49,499
2023-24 4202	Construction of Youth Development Centre at District Matiari	Satisfactory	9/18/2023	Sports & Youth Affairs, GOS	4/26/2024	Kashmore	85.23
2023-24 4203	Construction of Youth Development Centre at District N. Feroze	Satisfactory	11/20/2023	Sports & Youth Affairs, GOS	1/8/2024	Naushero Feroz	85.23
2023-24 4206	Construction of Youth Development Centre at District Sukkur	Satisfactory	11/14/2023	Sports & Youth Affairs, GOS	5/2/2024	Sukkur	85.23
2023-24 4209	Construction of Youth Development Centre at District Tharparkar	Satisfactory	9/21/2023	Sports & Youth Affairs, GOS	4/29/2024	Tharparkar	85.23
2023-24 4216	Construction of Youth Development Centre at District Malir	Satisfactory	1/10/2024	Sports & Youth Affairs, GOS	6/28/2024	Karachi Malir	85.23
2022-23 3167	Construction of Sports Ground at Dahrki District Ghotki (C:36.575)	Satisfactory	4/11/2023	Sports & Youth Affairs, GOS	1/5/2024	Ghotki	36.575
2022-23 3176	Missing Facilities Gulistan-e-Scouts Training Centre Abul Hasan Asfahani Road Gulshan-e-Iqbal	Satisfactory	5/15/2023	Sports & Youth Affairs, GOS	10/10/2023	Karachi	55
2022-23 3180	Construction of Players Hostel at KHA Ground NIPA	Satisfactory	7/5/2023	Sports & Youth Affairs, GOS	11/10/2023	Karachi East	200
2022-23 3183	Construction & Rehabilitation of Cricket Ground at Jinnah Government College and Installation of Net around the Boundary Wall of Annu Bhai Cricket Ground Nazimabad.	Satisfactory	3/27/2023	Sports & Youth Affairs, GOS	7/17/2023	Karachi Central	65,995
2022-23 3187	Construction of Ladies Gym & Indoor Hall at Ghotki	Satisfactory	3/21/2024	Sports & Youth Affairs, GOS	6/28/2024	Ghotki	55
2022-23 3191	Laying of Football Turf and Allied Works at Lyari International Ground, Phase -1	Satisfactory	10/4/2023	Sports & Youth Affairs, GOS	11/22/2023	Karachi South	99.8
2022-23 3196	Rehabilitation and Up-gradation of Sports Ground at Karsaz	Satisfactory	3/28/2023	Sports & Youth Affairs, GOS	7/18/2023	Karachi East	44
2021-22 2569	Construction of Youth Development Center at Kambar (C:54.978•R:5.022)	Satisfactory	3/9/2023	Sports & Youth Affairs, GOS	10/18/2023	Qambar Shahdadkot	60
2023-24 1067	Establishment of Vocational Centres for girls (04 Units), (i) Village Punhal Khan Chandio Taluka Sakrand District S.B.A	Satisfactory	5/17/2024	STEVTA, GOS	6/3/2024	Shaheed Benazirabad	90.363
2020-21 1891	Boring & Installation of 150 Nos Tube wells on Solar Energy for Assured Supply of 100 cusecs for Thar Coal from LBOD Spinal Drain RD-362 (Revised)	Un-Satisfactory	10/5/2023	Thar Coal Infrastructure Development	10/19/2023	Umerkot, Sanghar, Badin	1936.266
2018-19 1858	Construction of Pre-Treatment System for RO Plant LBOD Water Supply Scheme at Nabisar for Thar Coal Power Project	Un-Satisfactory	10/3/2023	Thar Coal Infrastructure Development	10/19/2023	Tharparkar	3250.15
2016-17 2214	Water Carrier from Nabisar Reservoir to Thar Coal Field-II (Revised)	Un-Satisfactory	10/4/2023	Thar Coal Infrastructure Development	11/16/2023	Tharparkar	15652.69
2023-24 1112	Establishment of Khairpur College of Agriculture and Management Sciences Khairpur Mir	Satisfactory	5/20/2024	Universities and Boards	6/3/2024	Khairpur	1392.513

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4287	Establishment of Women Development Complex at SBA (Revised on 29.09.20) (R: 44.767) (SDG # 1, 4, 5, 8 & 9)	Un-Satisfactory	2/20/2024	Women Development, GOS	6/28/2024	Shaheed Benazirabad	44.767
2022-23 3315	Repair / Renovation and Improvement of Services of Darul Aman Sukkur (C:14.160 + R:15.840) (SDG # .2)	Un-Satisfactory	4/6/2023	Women Development, GOS	1/5/2024	Sukkur	30
2018-19 1869	Implementation of Gender Reforms Action Plan (GRAP) Sindh (Revised) (R:544.770) (Karachi, SBA, Shikarpur, Sukkur, Larkana, Mirpurkhas, Jamshoro & Hyderabad)	Un-Satisfactory	3/29/2023	Women Development, GOS	11/8/2023	Hyderabad	544.77
2018-19 1872	Advocacy for Women Empowerment in Sindh (All Districts).	Satisfactory	3/30/2023	Women Development, GOS	11/1/2023	Mirpurkhas, Jamshoro, Hyderabad	49.346
Non-ADP	Rehabilitation of Road from Ghulam Nabi Chhutto to Village Hadi Bux Chutto 3.2km in District Jamshoro (Sujawal)	Satisfactory	11/22/2023	Work and Service, GOS	4/25/2024	Jamshoro	149.331
2023-24 4307	W/R of road National Highway to Tando Adam via Bhit Shah mile 0/0-17/0 (27.20 Kms)	Satisfactory	11/24/2023	Work and Service, GOS	6/11/2024	Matiari	747.346
2023-24 4310	W/R of road from Arrore Bachal Shah to Choundko (32.18 Kms)	Satisfactory	8/7/2023	Work and Service, GOS	9/6/2023	Sukkur	540.878
2023-24 4319	(i).Reconstruction of Pre-stressed Bridge 400 RFT (121.91 Meter) on Nae Sukhan @ mile 6/5. (ii). Reconstruction of pre-stressed Bridge 50 RFT (15.24 meter) on Rain Nala @ mile 2/0 @ link road connecting National Highway N-5 to Motorway M-9 @ Kat	Satisfactory	5/2/2024	Work and Service, GOS	5/13/2024	Karachi	149.429
2023-24 4343	Rehabilitation / Widening and Reconditioning of road Rohri Interchange M-5 to Salehpat City Dual Carriageway (Due to Heavy Traffic existing 24 proposed 50) (0.80 Kms) (Revised on 25.01.23)	Un-Satisfactory	10/9/2023	Work and Service, GOS	5/30/2024	Sukkur	456.195
2023-24 4344	Rehabilitation / Reconditioning of road from Ghulam Bund to Dhandi via Faqirabad (11.00 Kms) (Revised on 08.05.23)	Satisfactory	9/6/2023	Work and Service, GOS	5/3/2024	Sukkur	159.371
2023-24 4347	Rehabilitation of various roads at village Serai Piyaro Khan, Nazar Mohammad Gaho, Imam Bux Palh, sahib Khan Chakrani, Shadi Shaheed road, Rattal Bhambhro and Babar Wada Jhangoroad to Ahdi Rajper (15.00 Kms) (Revised on 08.05.23)	Satisfactory	11/8/2023	Work and Service, GOS	4/2/2024	Khairpur	196.88
2023-24 4349	Reconditioning of road from Jalal Jee Stop Mehran N/Highway to village Pholirhi via Bhangro Behan, UC Bhangro (11.60 Kms) (Revised on 08.05.23)	Un-Satisfactory	11/9/2023	Work and Service, GOS	4/3/2024	Khairpur	148.922
2023-24 4351	Rehabilitation / Construction of road from Odha More to Ali Murad Jamali via Amanullah Odho, Paraocha Ulro, G. Nibo Ulro, Muhammad Hayat Ulro, Shaman Ulra, Mehmood Odho mile 0/0-7/4, (12.06 Kms) (Revised on 22.05.23)	Un-Satisfactory	11/16/2023	Work and Service, GOS	5/2/2024	Khairpur	202.457
2023-24 4355	Improvement of road from Fakirabad to Jan Muhammad Gopang to Old N.H Way road mile 0/0-2/4 (4.00 Kms) Rehabilitation of road from Jhanda Shakh to Fakirabad upto GIMS road mile 0/0-5/0 (8.00 Kms) (Revised on 22.05.23)	Satisfactory	11/30/2023	Work and Service, GOS	2/27/2024	Khairpur	211.403
2023-24 4372	Widening / Reconditioning of road from Haji Ali Nawaz Deepar to Achhi Masjid approach link village Budak (10.00 Kms) (Revised on 14.04.23)	Satisfactory	9/20/2023	Work and Service, GOS	2/21/2024	Naushero Feroz	241.998
2023-24 4380	W/R / Construction of road from N.H.A Sarkari Khooh to connect Aumb Junejo road via Bachalpur, Muhammad Ismail Bhand road (16.00 Kms) (with 5cm thick Asphalt surface) (Revised on 14.04.23)	Satisfactory	9/22/2023	Work and Service, GOS	1/8/2024	Shaheed Benazirabad	388.982
2023-24 4382	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms) (Revised on 14.04.23)	Satisfactory	9/21/2023	Work and Service, GOS	1/3/2024	Shaheed Benazirabad	243.155

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4388	Reconditioning of road from Nawabshah - Kazi Ahmed road to connect Nawabshah - Sakrand road @ Landhi Stop Via Bildo Magsi, Khair Shah & Ghulam Qadir Jatoi 5.00 Kms	Satisfactory	12/20/2023	Work and Service, GOS	5/17/2024	Shaheed Benazirabad	66.183
2023-24 4389	Reconditioning of road from Mehran Highway @ Bhooral Shah Stop to village Abdullah Bughio via Gabol Stop and village Jeeand Khan Gabol mile 0/0-3/6 - 6.03 Kms (With 2	Satisfactory	10/26/2023	Work and Service, GOS	5/2/2024	Shaheed Benazirabad	97.369
2023-24 4393	W/R of road from Dengan Bhurgari to Jhuluri (9.00 Kms) (Revised on 14.04.23)	Satisfactory	9/27/2023	Work and Service, GOS	5/13/2024	Mirpurkhas	234.815
2023-24 4395	Reconditioning of link road from village Bego Kaka Chowk road to Sarhari Raod via village Bhale Dino Kaka road mile 0/0-7/0(11.20 Kms) (Modified)(Revised on 14.04.23)	Satisfactory	1/24/2024	Work and Service, GOS	6/4/2024	Matiari	269.93
2023-24 4413	Reconditioning of Asphalt Concrete road from Hyderabad - Mirpurkhas road at point Rahuki Bus Stop to Hyderabad - Shaikh Bhirkio road via Bhindo Sharif & Reconditioning of Asphalt Concrete road from Mirpurkhas - Hyderabad road to village Wali Muhammad Khask	Satisfactory	9/28/2023	Work and Service, GOS	2/23/2024	Hyderabad	96.501
2023-24 4418	Reconditioning of road from Gharo Mori to Panjtana (6.20 Kms) (Revised on 13.04.23)	Satisfactory	12/4/2023	Work and Service, GOS	4/30/2024	Tando Muhammad Khan	79.318
2023-24 4421	Improvement of road from Dumbalo to Kapri Mori mile 0/0-7/0 (11.263 Kms) (Revised on 14.04.23)	Satisfactory	12/6/2023	Work and Service, GOS	6/10/2024	Badin	240.87
2023-24 4424	Widening / Reconditioning of link road from Chach Jahan Khan - Mian Usman Quba road @ 5.00 Kms to village Haji Ali Muhammad Jat Warri = 0.00-7.30 Kms (Revised on 13.04.23)	Satisfactory	11/22/2023	Work and Service, GOS	6/12/2024	Sujawal	201.908
2023-24 4439	W/R of road from Indus Highway to Choukhandi via Ali Bux Junejo village Towards Boriri village, i/c Paver Block & Drain mile 0/0-3/0 (4.83 Kms) (Revised on 18.04.23)	Un-Satisfactory	11/10/2023	Work and Service, GOS	5/29/2024	Dadu	137.49
2023-24 4443	Widening & Reconditioning of road from Walwani Chodagi to Tharri Jado Shaheed via Phulji village (8.50 Kms) (Revised on 18.04.23)	Satisfactory	2/27/2024	Work and Service, GOS	6/28/2024	Dadu	172.443
2023-24 4454	Reconditioning of road from Dasori link road to Tayyab Thebo Hazoor Bux Thebo via Habib House, Soothar House mile 0/0-1/2 (2.00 Kms) (1	Satisfactory	11/14/2023	Work and Service, GOS	5/17/2024	Tando Allahyar	20.035
2023-24 4457	W/R of road from Tando Allahyar to Mirwah road at Belaro Shakh Stop mile 0/0-20/4 (33.00 Kms) (18 to 24 with 2	Satisfactory	11/7/2023	Work and Service, GOS	5/17/2024	Tando Allahyar	1342.916
2023-24 4459	W/R of road from Tando Allahyar Mirwah road to Qazi Noor Muhammad 0/0-1/4 (2.40 Kms)	Satisfactory	11/8/2023	Work and Service, GOS	2/26/2024	Tando Allahyar	53.335
2023-24 4460	W/R of road Nawabshah - Sanghar road @ 3 Water Stop to Jam Sahib 0.00 - 19.00 Kms (Revised on 24.05.23)	Satisfactory	12/21/2023	Work and Service, GOS	6/6/2024	Shaheed Benazirabad	970.956
2023-24 4463	Rehabilitation of Inter City road / Paving Block various streets of Thatta City i/c Drain Nali	Satisfactory	3/7/2024	Work and Service, GOS	5/10/2024	Thatta	440.519
2023-24 4484	Reconditioning of road from Perumal Tando Mitha Khan via 18 Mile to village Tharoo Khaskheli road. 0.00-10.00 Kms (With 1-1/2	Satisfactory	9/20/2023	Work and Service, GOS	3/11/2024	Sanghar	163.194
2023-24 4516	Construction / Improvement of road from Marowala to Gulab Chowk (Taken up length upto Ayoub Shar) (3.50 Kms)	Satisfactory	3/28/2024	Work and Service, GOS	6/5/2024	Ghotki	70.498
2023-24 4560	Reconditioning of road from Tando Adam Bhit Shah road to Hala Shahdadpur road via Kunb Darhoon, Giddar Ahpan, Baran Hazari. Malook Ahpan and Makhan Ahpan road Mile 0/0-7/5(12.20 Kms) with 1-1/2	Satisfactory	3/11/2024	Work and Service, GOS	5/17/2024	Sanghar	155.962
2023-24 4566	Reconditioning of road from Shahpur Chakar - Chowdagi road mile 2/4-5/5 (5.00 Kms) (18 width 1-1/2	Satisfactory	3/6/2024	Work and Service, GOS	6/7/2024	Sanghar	114.701

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2023-24 4715	Reconditioning of Road from Phull to Bodlo Dahri Rode Mile 0/0-7/4	Satisfactory	2/23/2024	Work and Service, GOS	6/6/2024	Naushero Feroz	180
2023-24 4783	Widening & Recondition of Road from Thatta to Jhampir Via Satyoon Baradabad road. KM=0.00-40.00=40.00 KMs	Satisfactory	3/8/2024	Work and Service, GOS	6/28/2024	Thatta	2052.536
2023-24 4807	Reconditioning / Construction of road from Main National Highway to Kameja Shakh via Goth Hamzo Babbar, Azam Shah, Goth Khad Hajano & Reconditioning of Road from Dargah Bilawal to Bhanoth Road Mile 0/0-7/4	Satisfactory	11/23/2023	Work and Service, GOS	6/3/2024	Matari	299.383
2023-24 4829	Construction of various roads in UCs of Taluka Naseerabad Kamber Warah & Miro Khan (5.00 Kms) (Phase-1)	Un-Satisfactory	11/16/2023	Work and Service, GOS	4/30/2024	Qambar Shahdadkot	808.704
2023-24 4868	Construction of various roads in Taluka Warah (19.95 Kms)	Satisfactory	4/26/2024	Work and Service, GOS	6/3/2024	Qambar Shahdadkot	216.783
2023-24 4876	Construction / Reconditioning of road from Mehran Highway @ Mungla Naako to connect Malhar mangrio, road via village Shaman Lashari & village Muhammad Bux Mojai (9.00 KM)(Revised on 08.05.23)	Satisfactory	1/24/2024	Work and Service, GOS	5/31/2024	Khairpur	183.185
2023-24 4888	Construction of road from Mirpurkhas-Sindhri to Patoyoon road to link various villages Union Council Old Mirpur & Ahmed Bux Narejo (Length - 8.30 Kms) (Revised on 08.05.23)	Satisfactory	1/15/2024	Work and Service, GOS	6/3/2024	Mirpurkhas	137.1
2023-24 4892	Construction of road from Mureed Khaskhally to Sonharo Dal via Hassan Shah Baghban (4.00 km) (Revised on 11.04.23)	Satisfactory	12/26/2023	Work and Service, GOS	5/20/2024	Umerkot	81.254
2023-24 4910	Construction of road from Tando Muhammad Khan Badin road @ mile 42/2 to village Suwali Dangno along Dokia Wah mile 0/0-6/2 (10.00 Kms) (Revised on 13.04.23)	Satisfactory	1/17/2024	Work and Service, GOS	6/10/2024	Tando Muhammad Khan	186.049
2023-24 4921	Construction / Rehabilitation of various roads of UC-11, UC-12, Taluka Thatta, District Thatta (Revised on 13.04.23)	Satisfactory	3/11/2024	Work and Service, GOS	6/3/2024	Thatta	126.759
2023-24 4928	Construction of road Network upgradation of 17 existing roads, connecting to Chuhar Jamali (203 Kms) (RGC)	Un-Satisfactory	2/27/2024	Work and Service, GOS	5/17/2024	Sujawal	3905.919
2023-24 4937	Construction of different roads / streets of Taluka Qasimabad and Union Councils Hatari, Barchani, Bahram & Masu (19.70Kms)	Satisfactory	12/25/2023	Work and Service, GOS	5/30/2024	Hyderabad	311.858
2023-24 4940	Construction of road from Oon Jo Wandhio to village Bhako via Kharoro (8.00 Kms)	Satisfactory	3/5/2024	Work and Service, GOS	6/28/2024	Tharparkar	236.363
2023-24 4942	Construction of road from Jhangal Malik to village Baloch Khan Chang (3.00 Kms)	Un-Satisfactory	1/16/2024	Work and Service, GOS	5/2/2024	Ghotki	44.513
2023-24 5066	Construction of road from Bharchondi to Sui Sharif (Taken up length upto Koro Chachar) (7.20 Kms)	Satisfactory	3/25/2024	Work and Service, GOS	6/28/2024	Ghotki	131.586
2022-23 3326	Improvement / Construction of Road from National Highway Bogo Wah on Both site (10.00 Kms) (SDG # 9)	Un-Satisfactory	11/23/2022	Work and Service, GOS	5/13/2024	Ghotki	260.815
2022-23 3354	W/R of road from N-55 Jail Chowrangi to Mari Chowk via ShahiBagh and approach to Court Complex at City Shikarpur (7.0 Kms) (SDG # 9)	Un-Satisfactory	11/29/2022	Work and Service, GOS	12/1/2023	Shikarpur	165.277
2022-23 3364	Rehabilitation of Station road Madeji City Portion upto Rice Canal (Carpeting & Paver Block) (5.00 Kms)	Un-Satisfactory	4/10/2023	Work and Service, GOS	6/6/2024	Shikarpur	76.285
2022-23 3375	Improvement of road from Shahdadkot Motorway Bypass (M-8) road @ Point Police Chowki to village Meenhoon Khan Leghari (Old Railway Track) via Juneja and Brohi (11.00 Kms)	Satisfactory	9/19/2023	Work and Service, GOS	1/8/2024	Qambar Shahdadkot	109.939
2022-23 3396	Reconditioning / Construction of road from Khanpur Thikratho road to Ibrahim Mahtam via Khameso Bhatti, Ali Madad Mahtam, Ucheer enclosed various links and Kabil Mahtam (9.00Kms)	Satisfactory	10/27/2022	Work and Service, GOS	7/14/2023	Sukkur	96.134

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3413	Reconditioning of road from Pacca Chang to Karoondi via Hussain Shah & via Sijawal Khaskheli (5.20 Kms)	Satisfactory	11/29/2022	Work and Service, GOS	7/14/2023	Khairpur	48.969
2022-23 3429	Reconditioning of road from Kandiaro Bus Stop to Saeed Khan Lakho via Siddique Lakho (10.00 Kms)	Satisfactory	7/20/2023	Work and Service, GOS	2/27/2024	Naushero Feroz	114.911
2022-23 3437	W/R of road from Dejarja to Chowdagi (with Asphalt) (11.50 Kms)	Satisfactory	9/19/2023	Work and Service, GOS	1/8/2024	Naushero Feroz	204.421
2022-23 3450	Reconditioning of road from Nawabshah - Sanghar road to village Ali Jan Brohi road (3.40 Kms)	Satisfactory	11/16/2022	Work and Service, GOS	10/20/2023	Shaheed Benazirabad	45.519
2022-23 3451	Widening / Reconditioning / Construction of road from Varr Stop to Connect Nawabshah - Ghupchani Shakal Jamali road via Khando Stop, Dost Pir, Hassan Jamali & Baksho Jamali (15.00Kms) (with 5 cm Thick Asphalt Surface)	Satisfactory	11/17/2022	Work and Service, GOS	9/18/2023	Shaheed Benazirabad	239.6
2022-23 3487	Construction / Improvement of road from Umerkot to Kunri via Diggu / Gapno Phase-II (18.40 Kms)	Satisfactory	8/11/2022	Work and Service, GOS	10/23/2023	Umerkot	185.954
2022-23 3518	Widening / Reconditioning of Asphalt Concrete road from Tando Fazal to Seri road mile 0/0-5/4 (8.80 Kms), Taluka RuralHyderabad	Satisfactory	10/17/2022	Work and Service, GOS	1/9/2024	Hyderabad	240.117
2022-23 3565	Improvement / Construction of roads of Taluka Manjhand:(i) Indus Highway to village Tangyani via Shah Awais village Golara, village Qaim Khan Khoso & Mureedani i/c M/S mile 0/0-II/4 (18.507 Kms) (ii) Indus Highway to Qubi via FaqeerBux Fanani Khoso, i/c	Satisfactory	9/26/2023	Work and Service, GOS	4/2/2024	Jamshoro	173.605
2022-23 3613	Improvement of road from Naukot to Nabisar via Noohato mile 0/0-27/4 (44.00 Kms)	Satisfactory	9/25/2023	Work and Service, GOS	3/6/2024	Tharparkar	1076.447
2022-23 3857	Construction of road from New Bypass Larkana Miro Khan to Kamber, Mirokhan road (3.00 Kms)	Satisfactory	9/18/2023	Work and Service, GOS	4/29/2024	Qambar Shahdadkot	179.153
2022-23 3874	Construction of road from Murad Ghoto link road to Bakro Wah, Deh Hussain Beli (2.00 Kms)	Un-Satisfactory	7/17/2023	Work and Service, GOS	12/21/2023	Ghotki	25.137
2022-23 3875	Construction of road from Izzat Wari to village Kaman Mahar via Raza Muhammad Mahar and village Aleem Malik (8.00 Kms)	Un-Satisfactory	7/14/2023	Work and Service, GOS	12/21/2023	Ghotki	111.69
2022-23 3910	Construction of road from Muhammad Hassan Makrani to village Haji Afzal Mehar Taluka Shujabad (5.60 KMS)	Satisfactory	7/25/2023	Work and Service, GOS	5/13/2024	Mirpurkhas	79.555
2022-23 3912	Construction of road from Siloor Mori to Adam Mori via Village Soomar Junejo, Taluka Jhudo (16.00 Kms)	Satisfactory	7/25/2023	Work and Service, GOS	5/10/2024	Mirpurkhas	198.285
2022-23 3927	Construction of road from Dhalo jo Tar to Jetrar road (7.00 Kms)	Satisfactory	4/14/2023	Work and Service, GOS	9/18/2023	Umerkot	154.062
2022-23 3928	Construction of road from Tar Ahmed to Samoon Rind via Umaid Ali Rind Faqir Tar (7.00 Kms)	Satisfactory	4/13/2023	Work and Service, GOS	9/18/2023	Tharparkar	112
2022-23 3963	Reconditioning / Widening of Road from Jarri Mori to Dando to Village Nazar Khoso via Haji Khan Stop (7.10 Kms)	Satisfactory	7/24/2023	Work and Service, GOS	11/29/2023	Tando Muhammad Khan	99.994
2022-23 3964	Reconditioning / Widening of Road from Digh Mori Soomerki Shakh to Village Jan Muhammad Wassan to Peeru Wassan toVillage Bashir Brohi via Nawab Pakko (6.00 Kms)	Satisfactory	7/24/2023	Work and Service, GOS	1/3/2024	Tando Muhammad Khan	127.186
2022-23 3973	Construction of road from Malkani City via Mehrab Regulator toMehrab Shahr i/c link road to Babar Kaloi from Malkani Roopo Rebari road (3.42 Kms)	Satisfactory	7/21/2023	Work and Service, GOS	6/5/2024	Badin	99.997
2022-23 3974	Construction of road from Badin Nindo road to Talho Khan Bhurgri, Otiya Rai Singh, Saeed Khan Bhurgri, Haji Abdul Karim Bhurgri i/c Mir Muhammad Rind, Zubair Rind, via Karo Wahconnect Tando Bago Nindo road 6.15 Kms	Satisfactory	7/21/2023	Work and Service, GOS	1/3/2024	Badin	99.856

ADP#	Name of Project	Report Type	Visit Date	Department	Published Date	Location	Cost
2022-23 3994	Construction / Reconditioning of road from Salhani City Check Post Pano Akil Cantt to Sultanpur road at Bridge Check post Pano Akil Cantt (Strategic Road) (4.00 Kms)	Satisfactory	7/10/2023	Work and Service, GOS	2/26/2024	Sukkur	165.221
2022-23 4145	Construction of Overhead Bridge on Railway Line between Kotri City and the Industrial Area Kotri (SDG # 9)	Un-Satisfactory	6/7/2023	Work and Service, GOS	7/6/2023	Hyderabad	1274.449
2022-23 4146	Construction of Pre-stressed Bridge Karachi 262.50 (80 m) on Sukhan Nadi near Haji Sheedi Goth to Pir Sarhandi Goth road	Satisfactory	5/31/2023	Work and Service, GOS	11/22/2023	Karachi	89.03
2022-23 4157	Repair and Renovation of Residential Colony and office Building of Camp Office, Sindh Coal Authority at Mithi.	Satisfactory	4/13/2023	Work and Service, GOS	3/6/2024	Tharparkar	335.996
2022-23 4775	W/R of road from Thariri Jado Shaheed Road to New Gaj (4/0-18/0=26.00 Kms)	Satisfactory	1/16/2023	Work and Service, GOS	4/29/2024	Dadu	653.892
2022-23 4844	Construction of road from Garhi Khuda Bux Bhutto Ratodero road to Bahman Plot along with Sim Drain (8.00 Kms) 24' wide 2	Satisfactory	1/15/2023	Work and Service, GOS	1/31/2024	Larkana	527.76
Non-ADP	CONSTRUCTION OF ROAD FROM NAWAB BHAWAL ROAD TO VILLAGE GULAB KHAN KHASKHELI TO VILLAGE HAJIALLAH DINO KHASKHELI 0/0 TO 1	Satisfactory	3/15/2023	Work and Service, GOS	2/27/2024	Shaheed Benazirabad	19.964
Non-ADP	Construction of Rooms and Maintenance of Community Center Mehar.	Satisfactory	3/15/2023	Work and Service, GOS	7/4/2023	Dadu	19.02
Non-ADP	Remaining work / Missing facilities in Gym Khana Dadu	Satisfactory	3/16/2023	Work and Service, GOS	7/4/2023	Dadu	30
Non-ADP	Construction of Road From Mahar Road to Muhammad Usman Mahar	Satisfactory	5/18/2023	Work and Service, GOS	7/20/2023	Sukkur	19.77
2021-22 2652	W/R Sanghar to Khipro via Chotiariyon Tando Mitha Khan & Loon Khan Road (53.10 Kms) (With Asphalt Surface)	Satisfactory	5/9/2023	Work and Service, GOS	10/19/2023	Sanghar	1479
2021-22 2653	W/R / Construction of road from Kumb to Malheer Patto via Bkahu Khan Lashari Rais Bangal Khan Chandio upto Old N.H Way Kotdiji road mile 0/0-12/6 (20.50 kms)	Satisfactory	5/4/2023	Work and Service, GOS	10/19/2023	Khairpur	301.255
2021-22 2767	Rehabilitation / Reconditioning of road from Water Works (Bunder road to Bhosa Line via Tanga Stand, Royal road, Nawab Tikka Shop, Qureshi road, Numaish Police Station Chowk i/c link road NADRA Office Local Board (2	Satisfactory	9/29/2022	Work and Service, GOS	10/18/2023	Sukkur	116.352
2021-22 3081	Construction of link road from main Piromal road to village Turk Bhugti link road to village Karim Bhugti (6.00 Kms) (SDG # 9).	Satisfactory	5/10/2023	Work and Service, GOS	11/27/2023	Sanghar	59.5
2021-22 3100	Construction / Rehabilitation of road from Shahpur to Sardar Garh road (17.00 Kms) (SDG # 9)	Un-Satisfactory	11/17/2023	Work and Service, GOS	12/4/2023	Ghotki	189.864
2021-22 3110	Construction of road from link road village Abdul Rasheed to village Ghulam Muhammad village Muhammad Sharif village Juma Khan Jagirani (4.82 Kms) ((SDG # 9)	Un-Satisfactory	2/24/2023	Work and Service, GOS	12/21/2023	Khairpur	59.046
Non-ADP	Remaining work at Irrigation Public Park Dadu	Satisfactory	3/14/2023	Work and Service, GOS	7/4/2023	Dadu	10

Annexure (C)

COMPLETED SCHEMES IN FY 2023-24

ADP	Name of Scheme	Sector	Estimated Cost
6	Establishment of Agro-Export Processing Zone for Export of Fruits, Vegetables, Flowers & Allied Processing Products from Local Farms / Processing Units to Overseas Markets (Revised 09.03.06) (Re-revised 25.02.10)	Agriculture, Supply & Prices	490.513
14	Establishment of Demonstration Plots of Fruit Crops Ber (Jujube) at Farmer's Field in District Tharparkar (R:15.000)	Agriculture, Supply & Prices	15.000
34	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-1 Project (World Bank Assisted) (Total:30139.75 including IDA Share:18686.64, GoS' Share:6120.00 & Farmers' Share:5333.11)	Agriculture, Supply & Prices	6120.000
44	Integrated Water Resource Management in Sindh (Total:2393.495 including GoS' Share:1932.447 & Farmers' Share:461.048)	Agriculture, Supply & Prices	1932.447
59	Construction / Repair / Renovation of Janaza Gha Bakara Peeri Singo Lane.	Auqaf, Zakat, Ushr & RA	25.000
61	Construction & Provision of Allied Facilities at Dargah Sain Mehboob Shah village & UC Mad Bhu.	Auqaf, Zakat, Ushr & RA	15.000
62	Construction & Provision of Allied Facilities at Dargah Shaeed Badshah village Haji Ghulam Shah UC Puranoabad.	Auqaf, Zakat, Ushr & RA	15.000
65	Construction & Provision of Allied Facilities at Dargah Makhdoom Sakhi Shah Jamal Village Balhreji UC Maenjodaro Taluka Dokri.	Auqaf, Zakat, Ushr & RA	14.000
79	Construction of New Compound Wall and Allied Facilities at Dargah Shah Yaqeeq, District Sujawal	Auqaf, Zakat, Ushr & RA	24.000
98	Automation of Stamps & Registration, 21 districts (Revised on 26-12-14, Re-revised on 08-02-22, 3rd revised on 19-04-23) (SDG #9)	Board of Revenue	2128.101
104	Acceleration of Additional Facilities at Culture Center Kamal Dero. (Revised on 17.09.20) (C:82.769+R:14.914)	Culture, Tourism, Antiquities & Archives	97.684
108	Provision of Additional Allied Facilities & External Development at Sindh Institute for Music & Performing Arts & DR. N.A Balouch Institute at Jamshoro. (Revised on 16.05.23) (C:186.904+R:8.408)	Culture, Tourism, Antiquities & Archives	195.312
113	Provision of Allied Facilities at Cultural Complex Tando Allah Yar. (Revised on 16.05.23) (C:166.147+R:26.936)	Culture, Tourism, Antiquities & Archives	193.083
116	Provision of Allied Facilities at Culture Center Thano Bula Khan. (Revised on 16.05.23) (C:178.98+R:11.020)	Culture, Tourism, Antiquities & Archives	190.000
140	Provision of Missing Allied Facilities and Up-liftment of Old Bungalows at Keenjhar Lake, Thatta. (C:31.002+R:8.998)	Culture, Tourism, Antiquities & Archives	40.000
153	Conservation & Restoration of Khudabad Masjid at District Dadu. (Revised on 15.02.23) (C:539.407)	Culture, Tourism, Antiquities & Archives	539.407
165	Establishment of Sindh Cultural Mart at Sindh Archives Karachi (Revised on 23-05.23) (C:71.662+R:6.338)	Culture, Tourism, Antiquities & Archives	78.000
174	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (147 Units) (C:713.202+R:176.794) (SDG#4)	Education (School)	889.996
176	Rehabilitation/ Expansion/ Improvement of High Priority 4560 Schools (Primary / Elementary Schools) (182 Units) (SDG#4)	Education (School)	1185.040
178	Construction of Six Room Buildings for Shelterless Primary Schools (01 Unit) (Revised on 19.05.2023)(C: 23.941 + R: 1.210) (SDG#4)	Education (School)	25.151
182	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (Revised on 20.05.2023)(SDG#4)	Education (School)	29.243
183	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (04 Units) (SDG#4)	Education (School)	24.879
184	Rehabilitation of High Enrollment Dangerous Primary Schools with Additional Class Rooms and Provision of Missing Facilities (05 Units) (SDG#4)	Education (School)	24.017
186	Construction of Building for Shelterless Primary School (01 Unit) (Revised on 19.05.2023) (C: 22.392, R: 2.012) (SDG#4)	Education (School)	24.404
187	Construction of Buildings for Shelterless Primary Schools (02 Units) (Revised on 19.05.2023)(C: 44.724 + R: 2.758) (SDG#4))	Education (School)	47.482
188	Construction of Building for Shelterless Primary School (01 Unit) (C: 18.492, R: 1.379) (Revised on 19.05.2023) (SDG#4)	Education (School)	19.871
189	Construction of Building for Shelterless Primary School (01 Unit) (C:34.245 + R:1.379) (SDG#4) (Revised on 04.01.23)	Education (School)	35.624

ADP	Name of Scheme	Sector	Estimated Cost
190	Construction of Building for Shelterless Primary School (01 Unit) (C:21.083 + R:1.379) (Revised on 20.05.2023) (SDG#4)	Education (School)	22.462
193	Construction of Buildings for Shelterless Primary Schools 02 Units) (C:35.838 + R:2.758) (Revised on 20.05.2023)(SDG#4)	Education (School)	38.596
195	Construction of Buildings for Shelterless Primary Schools (04 Units) (Revised on 23.05.2023) (67.516 + R:5.516) (SDG#4)	Education (School)	73.487
196	Construction of Buildings for Shelterless Primary Schools (04 Units) (C:75.344 + R:5.516) (Revised on 20.05.2023) (SDG#4)	Education (School)	80.860
197	Construction of Buildings for Shelterless Primary Schools (04 Units) (Revised on 19.05.2023) (C:75.602 + R:5.516) (SDG#4)	Education (School)	81.118
204	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities (SDG#4) (Revised on 20.05.2023)	Education (School)	65.115
205	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities (SDG#4)	Education (School)	64.304
206	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities (SDG#4) (Revised on 20.05.2023)	Education (School)	65.821
210	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities (C:68.663 + R:3.910) (SDG#4)	Education (School)	72.573
218	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities (SDG#4)	Education (School)	62.965
223	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities. (Revised on 18.05.2023) (SDG#4)	Education (School)	78.947
226	Rehabilitation / Reconstruction of High Enrollment Dangerous Primary / Elementary Schools and Provision of Missing Facilities. (Revised on 18.05.2023)(SDG#4)	Education (School)	44.587
232	Up-gradation of Primary Schools to Elementary Schools (04 Units) (C:64.862 + R:10.128) (Revised on 22.05.2023) (SDG#4)	Education (School)	74.990
237	Up-gradation of Primary Schools to Elementary Schools (03 Units) (C:75.305 + R: 2.984) (Revised on 18.05.2023)(SDG#4)	Education (School)	78.289
244	Construction of Building of Government Boys Lower Secondary School at Muhammad Bux Narejo Taluka Hussain Bux Mari (Revised on 23.05.2023)(SDG#4) (C:17.813 + R:2.532)	Education (School)	20.345
246	Up-gradation of Primary School to Elementary School at GBPS Mitho Khan Narejo UC Madd Taluka Sobhodero & GBPS Haji Ismail UC Jado Wahan Taluka Gambat (02 Units) (revised on 14.02.2023) (C:45.788 + R:5.064) (SDG#4)	Education (School)	50.852
248	Up-gradation of Girls Primary Schools to Elementary Schools at Saeed Khan Laghari & Construction of Additional Class Rooms at GBPS Saeed Khan Laghari Taluka Hala (02 Units) (C:48.363 + R:3.448) (SDG#4) (Revised on 04.01.23)	Education (School)	51.811
252	Construction of Buildings for Shelterless Primary Schools (02 Units) (SDG#4) (C:23.366 + R:2.012)	Education (School)	25.378
253	Construction of Building for Shelterless Primary School (01 Unit) (SDG#4) (C:17.394 + R:2.012).	Education (School)	19.406
254	Construction of Building for Shelterless Primary School (02 Units) (SDG#4) (27.898 + R:2.072)	Education (School)	29.970
418	Sindh Basic Education Program (SBEP) (Approved Cost: Rs.14355 M USAID Grant: Rs.13485 M & G.O.S. Share: Rs.870 M) (C: 651.147 + R: 218.853) (SDG#4)	Education (School)	870.000
432	Provision of Missing / Additional Facilities and Renovation of Existing High Schools along with Feeder Primary School at distance of 1.5 K.M Radius (01 Unit) (C: Rs. 40.000 + R: 2.923) (SDG#4)	Education (School)	53.764
444	Up-gradation of Middle School to High School (01 Unit)(Revised on 18.05.2023) (C:42.703 + R: 4.555) (SDG#4)	Education (School)	47.258
445	Up-gradation of Middle School to High School (01 Unit) (Revised on 22.05.2023) (C:38.261 + R:4.091) (SDG#4)	Education (School)	42.352
446	Up-gradation of Middle School to High School (01 Unit) (C: 25.640 + R: 4.091) (SDG#4)	Education (School)	29.731
447	Up-gradation of Middle School to High School (01 Unit) (Revised on 23.05.2023) (C:34.171 + R:5.357) (SDG#4)	Education (School)	39.528
452	Up-gradation of Middle School to High School (01 Unit) (Revised on 18.05.2023)(C:37.302 + R:4.091) (SDG#4)	Education (School)	41.393
454	Up-gradation of Middle School to High School (01 Unit) (Revised on 18.05.2023) (C:41.379 + R:4.091) (SDG#4)	Education (School)	45.470
455	Up-gradation of Middle School to High School (01 Unit) (Revised on 19.05.2023)(C: 36.829 + R: 4.091) (SDG#4)	Education (School)	40.920
458	Up-gradation of Middle School to High School (01 Unit) (Revised on 18.05.2023)(C:34.494 + R:4.091) (SDG#4)	Education (School)	38.585
467	Provision of Missing / Additional Facilities and Renovation of Existing High / Higher Secondary Schools (Revised on 22.05.2023) (04 Units) (C:75.529 + R:1.828) (SDG#4)	Education (School)	77.357
470	Provision of Missing / Additional Facilities and Renovation of Existing High / Higher Secondary Schools (Revised on 23.05.2023) (05 Units) (SDG#4)	Education (School)	84.909
472	Provision of Missing / Additional Facilities and Renovation of Existing High / Higher Secondary Schools (06 Units) (Revised on 23.05.2023) (SDG#4)	Education (School)	65.839
476	Provision of Missing / Additional Facilities and Renovation of Existing High / Higher Secondary Schools (06 Units) (SDG#4)	Education (School)	53.974

ADP	Name of Scheme	Sector	Estimated Cost
486	Re-construction of Compound Wall and other missing facilities at Bahria Public School Naushahro Feroze (01 Unit) (Revised on 23.05.2023) (SDG#4)	Education (School)	52.171
488	Construction of Govt. Boys High School Makhdoom Ghulam Hyder Taluka Hala (01 Unit) (SDG#4)	Education (School)	78.802
489	Up-gradation of Middle School to High School & Reconstruction of Existing Middle School Barachani Taluka Bulri Shah Karim (01 Unit) (Revised on 19.05.2023) (C:58.465 + R:4.091) (SDG#4)	Education (School)	62.556
491	Repair / Rehabilitation of School Building & Re-construction of Compound Wall of Govt. Naz Pilot Secondary School (SDG#4) (Revised on 19.05.2023)	Education (School)	72.196
498	Construction / Reconstruction of Govt. Boys High School Jhuddo. (Revised on 18.05.2023)(SDG#4)	Education (School)	75.012
501	Provision of Missing Facilities at Government High School Trimor Taluka Nawabshah (SDG#4) (revised on 22.05.2023)	Education (School)	14.109
502	Construction of Compound Wall and Earth Filling of Government Higher Secondary School Ber Sharif Taluka Kamber (SDG#4)	Education (School)	30.300
598	Provision of Additional Facilities at Government High School Haji Junejo	Education (School)	40.000
678	Introduction of Life Skill Based Education Training for ES&HS School Teachers in Sindh (SDG#4)	Education (School)	85.565
693	Repair / Rehabilitation/ Reconstruction of field offices of Education & Literacy (SDG#4) (Revised on 22.05.2023)	Education (School)	35.472
694	Repair / Rehabilitation/ Reconstruction of field offices of Education & Literacy (SDG#4) (Revised on 22.05.2023)	Education (School)	46.172
713	Construction of ECE Class Rooms / Rehabilitation / Up-gradation of Various Schools of UC 1 to 19 (SDG#4) (Revised on 18.05.2023)	Education (School)	118.827
714	Construction of (Govt. Boys / Girls Secondary Schools) in Shirin Jinnah Colony Karachi (02 Units) (Revised on 18.05.2023)(C:77.902 + R:2.00) (SDG#4)	Education (School)	79.902
715	Rehabilitation / Re-construction & Provision of Missing Facilities in GHS G. Jaffar (01 Unit) (Revised on 22.05.2023) (SDG#4)	Education (School)	43.403
716	Rehabilitation of Government Schools of Taluka Kamber, Warah & Naseerabad (07 Units) (SDG#4)	Education (School)	19.354
718	Rehabilitation & Provision of Missing Facilities in Existing GBHS Baberlo, GGHS Luqman, GBHSS Talpur Wada & GHSS Faiz Kotdiji (04 Units) (Revised on 22.05.2023) (SDG#4)	Education (School)	80.870
721	Construction of Building for Shelterless Primary schools Hazoor Jami Rind UC- Hoat Faqeer, Abdul Ghani Brohi (Chakar Brohi Deh -54 Nusrat), Muhammad Uris Sehto UC- Obhari Sewari and Muhammad Ramzan Chandio UC -Jhuro Shar (04 Units) (Revised on 22.05.2023) (C:17.268 + R:2.000) (SDG#4)	Education (School)	19.268
724	Repair, Rehabilitation and Provision of Missing Facilities in various Government Schools of UC-3,4,5,6, 11,12,13,14,15,16,17,18 & 44 of District Hyderabad (07 Units) (Revised on 23.05.2023) (SDG#4)	Education (School)	46.130
761	Rehabilitation / Reconstruction & Provision of Additional Facilities in Existing Primary / Middle / High Schools Taluka Shahdadpur (SDG#4)	Education (School)	29.965
768	Strengthening of Office of the Chief Engineer Education Works Sukkur (C:19.104 + R:0.849)	Education (School)	19.953
838	Establishment of Degree College in existing Dhoro Naro Higher Secondary School District Umerkot (C:25.905 + R:1.851) (SDG#4)	Education (College)	27.500
840	Rehabilitation & Provision of Missing Facilities in C&S Govt. Boys College Shikarpur (C:82.87 + R:6.320) (Revised on 09.09.2021)(SDG#4)	Education (College)	89.190
842	Improvement / Renovation of Govt.Boys Degree College Gulzar-e-Hijri East Karachi (SDG#4) (Revised on 23.12.2021)	Education (College)	96.999
843	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Hyderabad (SDG#4)	Education (College)	52.809
844	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District T.Allah Yar (SDG#4) (C:19.389, R: 1.192)	Education (College)	20.581
847	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Dadu (SDG#4)	Education (College)	31.750
848	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District T.M.Khan (SDG#4)	Education (College)	20.495
849	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Badin (SDG#4)	Education (College)	38.321
850	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Thatta (SDG#4)	Education (College)	52.080
853	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Umerkot (SDG#4) (C: 29.769 + R: 8.500)	Education (College)	38.269
855	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Shaheed Benazirabad (SDG#4)	Education (College)	45.534
856	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District N. Feroze (SDG#4)	Education (College)	31.880
857	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Sanghar (SDG#4)	Education (College)	54.991
859	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Khairpur Mir's (SDG#4)	Education (College)	54.833

ADP	Name of Scheme	Sector	Estimated Cost
860	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Ghotki (SDG#4)	Education (College)	26.693
861	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Larkano (SDG#4)	Education (College)	26.908
862	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Kamber-Shahdadkot (SDG#4)	Education (College)	20.728
863	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Shikarpur (SDG#4)	Education (College)	27.460
864	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Jacobabad (SDG#4)	Education (College)	20.924
871	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Karachi Korangi (SDG#4)	Education (College)	41.433
872	Rehabilitation & Provision of Missing Facilities in Existing Colleges in District Keamari Karachi (SDG#4)	Education (College)	19.989
879	Re-construction of Building for Existing Government Intermediate College @ Garho Taluka Ghora Bari District Thatta Renamed As Construction of Building for Existing Govt. Degree College @ Garho Taluka Ghora Bari District Thatta (SDG#4)	Education (College)	99.978
880	Conversion of Higher Secondary School Kaloi to Degree Level District Tharparkar (SDG#4) (C: 34.073 + R: 3.000)	Education (College)	42.298
886	Re-Construction of Building Govt. Boys Degree College Miro Khan District Kamber-Shahdadkot (SDG#4) (Revised on 19.05.2023)	Education (College)	157.803
887	Rehabilitation & Provision of Missing Facilities in Existing GBDC / GGDC Naudero District Larkano (Revised on 08.03.2023)	Education (College)	113.770
889	Conversion of Higher Secondary School to Degree College at Hingorja District Khairpur (SDG#4) (C: 38.457 + R: 2.100)	Education (College)	40.557
893	Provision of Furniture in existing Degree Colleges in Sindh (SDG#4)	Education (College)	80.000
897	Establishment Girls Degree College Murad Memon Goth District Malir (SDG#4) (C: 87.12, R:8.463)	Education (College)	95.583
912	Establishment of Degree College at Khipro District Sanghar (C:88.480 + R:9.000) (SDG#4) (ADP 2021-22 S. No.473)	Education (College)	97.480
914	Establishment of Degree College at Nagar Parkar District Tharparkar (C:90.978 + R:7.901) (SDG#4) (ADP 2021-22 S. No.476)	Education (College)	98.879
915	Establishment of Girls Degree College at Jamesabad Kot Ghulam Muhammad District Mirpurkhas (C:90.978 + R:7.901) (SDG#4) (ADP 2021-22 S. No.477)	Education (College)	98.879
916	Establishment of Degree College at Garhi Khairo District Jacobabad (C:89.089 + R:7.963) (SDG#4) (ADP 2021-22 S. No.478)	Education (College)	97.052
917	Establishment of Girls Degree College at Tando Jam District Hyderabad (C:92.789 + R:6.21) (SDG#4) (ADP 2021-22 S. No.479)	Education (College)	99.000
918	Establishment of Degree College in existing Nasarpur Higher Secondary School Tando Allah Yar (C:25.000 + R:2.500) (SDG#4) (ADP 2021-22 S. No.481)	Education (College)	27.500
919	Establishment of Degree College in existing Chachro Higher Secondary School Tharparkar (C:24.989 + R:2.500) (SDG#4) (ADP 2021-22 S. No.483)	Education (College)	27.489
921	Establishment of Degree College in existing Warha Higher Secondary School District Kamber Shahdad Kot (C:25.905 + R:1.851) (SDG#4) (ADP 2021-22 S. No.485)	Education (College)	27.756
922	Establishment of Degree College in existing Nasirabad Higher Secondary School District Larkano (C:25.838 + R:1.851) (SDG#4) (ADP 2021-22 S. No.486)	Education (College)	27.689
923	Establishment of Degree College in existing Islam Kot Higher Secondary School District Mirpurkhas (C:24.989 + R:2.500) (SDG#4) (ADP 2021-22 S. No.487)	Education (College)	27.489
924	Establishment of Degree College in existing Manjhand Higher Secondary School District Jamshoro (C:25.000 + R:2.500) (SDG#4) (ADP 2021-22 S. No.489)	Education (College)	27.500
925	Construction of Building for existing Degree College Daultapur District Sh.Benazirabad (C:88.480 + R:9.000) (SDG#4) (ADP 2021-22 S. No.492)	Education (College)	97.480
926	Remaining Work of Law College Halla District Matiari (SDG#4) (ADP 2021-22 S. No.497)	Education (College)	20.000
1022	Rehabilitation of Govt. Special Education & Rehabilitation Centre for Physical Handicapped Children Khairpur. (C: 14.094+R: 0.00) (SDG#4)	Education (Emp)	14.924
1070	Re-construction of Vocational Training Center at Diplo (C:36.825 + R:5.407) (SDG # 1,4,9)	Education (STEVTA)	42.232
1136	Installation of 500 KW Solar Photovoltaic System for Solarization of remaining Buildings/Classrooms / Laboratories at QUEST, Nawabshah District Shaheed Benazirabad. (SDG # 4, 7, 9)	Education (U&B)	99.780
1137	Repair and Renovation of 02 Boys Hostel Block C & D and Walk Ways 7' Wide I/C Fiber Glass Shed from Sector-A towards Boys Hostels at QUEST Nawabshah (Phase-I)	Education (U&B)	99.500
1141	Provision of Water Supply at Shaheed Benazir Bhutto University (SBBU), Shaheed Benazir Abad (SDG # 4,6)	Education (U&B)	47.682
1217	Construction of First Floor and Ancillary Facilities District Accounts Officer Kamber	Finance	30.000
1227	Green Pakistan Program-Revival of Forestry and Wildlife Resources in Pakistan (Ten Billion Trees Tsunami Program, Phase-I Up-scaling of GPP) Sindh chapter (Total cost of Rs. 5827.400 million, GoP share of Rs. 2811.050 million and GoS share Rs. 3016.350 million)	Forest & Wildlife	3016.350
1228	Sarsabz Sindh Making Sindh Green and Environment Friendly (SDG # 15)	Forest & Wildlife	599.944

ADP	Name of Scheme	Sector	Estimated Cost
1229	Satellite Based Mapping of Forest Areas and Follow-up Satellite Service for Implementation of Sindh Sustainable Forest Management Policy 2019 (SDG # 15)	Forest & Wildlife	320.000
1240	Re-construction of Underground Tank with Pumping room at NICH, Karachi (C: 44.676) (SDG #3)	Health	44.676
1243	Provision of linear accelerator with integrated high field MRI System at DUHS Karachi (Revised on 29.05.23) (GOS Share Rs. 2847.239 and additional Rs. 200.000 DUHS) (C:83.160+R:2764.079) (ADP # 745 2021-22) SDG # 3	Health	2847.239
1282	Strengthening of health facilities (07 Nos) at Lal Khan Lashari, Yousif Jamali, Nagar Khan Brohi, Manhayoon, Duri Dero, Umeed Ali Katohar & Gaheer, Taluka Sehwan, District Jamshoro.(C:19.137 + R:2.240)(SDG #3)	Health	21.377
1300	Construction of Maternity Home at Mehar, UC Mehar, Taluka Ghorabari, District Thatta. (C: 15.667+R: 4.253) (SDG #3)	Health	19.920
1363	Construction of 150 Bedded Hospital at Larkana (PC-II)	Health	50.000
1364	Re-construction of Sindh Government Anwar Paracha Hospital for Gynecological & Obstetric Services Sukkur (PC-II)	Health	40.000
1365	Sindh Institute of Cardiovascular Diseases Nawabshah (PC-II)	Health	60.000
1366	Sindh Institute of Cardiovascular Diseases Karachi (PC-II)	Health	140.000
1505	Improvement / Strengthening of Security to Police Residential Colony of District Ghotki (Construction of Compound Wall with Watch Towers) (SDG # 16)	Home	53.334
1524	Construction of Affidavit Centre, Pray Area, General Bathroom, Bar Room, Library, Prosecutor Chamber, and Public Cafeteria at ATC Courts, Central Prison, Karachi.	Home	166.350
1572	Rehabilitation / Providing and Laying Sewerage Line, Paver Blocks at Katchi Abadi Noorani Basti, Bilal Colony Korangi	Human Settlement	28.694
1573	Upgradation plan of CC Drain & CC Flooring at Katchi Abadi Chandi Ram Colony, Umerkot	Human Settlement	28.000
1584	Providing & Supplying of Water Supply line and Reconditioning of Road at SIE Extension Hyderabad	Industries & Commerce	83.195
1585	Improvement of Basic Infrastructure of Industrial Park Sehwan Establish year 1974-75 (5 Acre Land)	Industries & Commerce	39.461
1588	Improvement of Basic Infrastructure of SIE Hyderabad. Establish year 1985-86 (50 acre land)	Industries & Commerce	90.866
1594	Infrastructure Rehabilitation and Development at S.I.T.E Ltd. Karachi	Industries & Commerce	242.806
1600	Establishment of Museum of Antique Printing & Allied Machines in Sindh Government Press, Karachi. (Revised on 09.05.23)	Industries & Commerce	149.843
1611	Installation of Security Surveillance Cameras at Worship Places of Minorities (Revised on 17-03-20)	Information S&T	382.698
1612	Up-Gradation of Video Conferencing System in Sindh (Revised on 18-02-21)	Information S&T	189.150
1615	Information & Computing Technology System at Cadet College Sanghar	Information S&T	49.750
1635	Construction of IRE Sub-Drain RD-0 to 35 (Village Abdul Wahab Khoso), Sub-Drain Qubo Saeed Khan, 3LA Sub Drain RD-0 to 37 and Extension of 3R Sub-Drain RD - 18 to 32 of Shahdaddock System in Drainage Division Larkano (Revised on 12.02.16) (SDG # 6)	Irrigation	162.000
1636	Rehabilitation of Existing Tubewells and Small Surface Drainage Scheme Dingro, Jari Agro (SDG#6)	Irrigation	199.823
1637	Construction of Pumping Stations of 80 Cusecs to Control Water Logging Salinity and Drain out monsoon Water at Chamber, Tando Allahyar (SDG # 6)	Irrigation	195.200
1638	Boring & Installation of 250 Nos Tubewells of 2.0 Cusecs on Solar Energy (SDG # 6)	Irrigation	2087.110
1640	Restoration of 200 Nos Existing Tube wells under closed in Major Faults & Re-boring of 50 Nos Bore Failure Tubewells & Pacca Sim Nala from Wali Muhammad Kandhro to Babar Jo Goth P4L Main Nala in Khairpur (SDG # 6)	Irrigation	450.000
1643	Installation of 50 Nos T/Wells Deh Fareedabad Barani District Dadu and Re-boring of 13 Nos Bore Failure T/Wells and Restoration of 70 T/Wells closed due to transformers defect and 48 Nos closed due to 11 KVA Line including Rehabilitation of Ruk Gharhi Yaseen & Masti Pumping Station (SDG # 6)	Irrigation	575.752
1645	Re-boring of 25 Nos Bore failure Tubewells including Restoration of old direct disposal arrangement and Re-furbishment of SCARP Tubewells and Installation of 15 Nos New Tubewells in different Dehs in Tubewell Division No.II Hala & Surface Drainage scheme Gul Muhammad Dero Deh Narli, Taluka Matiari and Deh Rahoki, Deh Pangrio Rahittee and Deh Ujano Taluka Saeeadabad and Deh Khan Muhammad Dero in Deh Kariqadeer, Matiari (SDG # 6)	Irrigation	374.786
1646	Rehabilitation of EKTID Main Drain of 109 RDs and other structural works of Tubewell Division Khairpur and Supplying & Fixing of new Generator sets, Additional Transformers 500, 300, 200 KVA in Pumping Stations F, B, G and Talpur Wada (SDG # 6)	Irrigation	195.000
1649	Installation of 100 New Tubewells (SDG # 15)	Irrigation	560.600
1650	Rehabilitation / Restoration of Drainage Infrastructures and Construction of Retaining Wall around Larkano City on Various Drains including IR, 2R and IR-C Sub Drain of Larkano South System, IR Ghar Sub Drain and Reconstruction of Structures including VRBs, VRCs, Water Course X-ings, Inlets, Junction Culverts etc (SDG # 6)	Irrigation	800.000
1651	Surface Drainage Scheme near Village Alam Khan Odho (left over pocket) (Revised on 09.03.17) (SDG # 6 & 15)	Irrigation	399.872
1652	Installation of 84 Nos. of 2.0 cusecs Tubewells along the Embankment Chotiari Reservoir (Remaining Works) - (Revised on 17.03.20)(SDG # 6)	Irrigation	322.329

ADP	Name of Scheme	Sector	Estimated Cost
1653	Rehabilitation of Branch Drain, Sub Drain, Reconstruction of Water Course Crossing, Village Road Bridges and Construction of Retaining Wall along 3RA Sub-Drain in Shikarpur Drainage Division (SDG # 6)	Irrigation	153.536
1659	Construction of Retaining Wall along 3LB Sub-Drain of Larkano North System from RD-4 to 5 (both side).	Irrigation	16.771
1660	Construction of Retaining Wall along 3LC Sub-Drain of Larkano North System from RD-6 to 8	Irrigation	16.887
1670	Construction of Tubewells & Pumping Stations on Solar Energy System of Drainage Division SBA.	Irrigation	498.228
1676	Installation of New Solar Tube-wells (25 Nos.) in District, Sanghar, SBA & Tando Allahyar	Irrigation	175.050
1686	Installation Tubewells of 06 Villages of U.Cs Soomar Khan, Gupchani, Jhooro Khan Shar and Abdul Hassan: Village Zahid Ali Jamali, Deh 14 Nasrat, UC Soomar Khan, Village Nawab Khan Brohi, Deh 14 Nasrat, U.C Soomar Khan, Village Meer Mahar, U.C Soomar Khan Jamali, Village Nabi Dad Brohi, Deh Pubjo, U.C Gupchani, Deh Akro-II (Sr. No. 1921/1 to 4 1922/1 to 4) village Yaseen Brohi, U.C Abdulk Hassan, Taluka Daur.	Irrigation	51.766
1688	Rehabilitation & Solar System 7 Nos. Pumping Station at Bodlo Behan, Karocho, Mallah Kacho Pako Ilyas Pir	Irrigation	49.996
1727	Sindh Resilience Project (Irrigation Component) for Strengthening Flood Embankments & Constructing Small Dams including Systems for Improving Resilience (World Bank Funded), Total Cost Irrigation Component Rs. 9984.00 Million (WB Share Rs. 8320.000 M) & GoS Share (Rs. 1664.00M) (SDG # 6)	Irrigation	1664.000
1732	Constructing Stone Pitching at RD-9+00 to 15+00 RMC B/S and Downstream Fall Structure 16, 17, 18, 19 & 20 B/Sides (Revised 22-02-22).	Irrigation	378.078
1739	Renovation / Reconstruction of Regulator on Distries and Minors in Sindh.	Irrigation	400.000
1741	Providing Stone Apron, Stone Pitching, Earth Work along L.S Bund Mile 18/0 to 20/0 in Northern Dadu Division Larkano. Total Cost Rs.241.586 Million) (GOP Share 65%) & (GOS Share 35%) - NDRMF	Irrigation	90.230
1744	Removal of Encroachment from Irrigation Department's Property & Securing its possession including Schemes of Rehabilitation (Phase-I).	Irrigation	150.000
1746	Training of Engineers for Employment in Private Sector.	Irrigation	156.886
1748	Rehabilitation of Shah Awais Pumping Scheme in Shahbaz Irrigation Division Sehwan (Revised 21-03-23)	Irrigation	37.665
1749	Construction of 01 No. New Pumping Scheme Near Village Noorpur in Taluka Manjhand (Revised 21-03-23)	Irrigation	55.444
1750	Construction of Stone Pitching and Earth Work along Various Portions along B.S Feeder Main Canal from RD-193 to 269 (Revised 05-08-22)	Irrigation	231.031
1751	Construction of 02 Nos. New Pumping Schemes Near Village Dari Gancha and Village Kalri in Taluka Manjhand (Revised 21-03-23)	Irrigation	111.358
1753	Construction of Culverts (Bridge) on Shahbaz Minor, Taluka Sakrand, Shaheed Benazirabad.	Irrigation	29.008
1762	Construction of C.C. Lining from Head to Tail of Kot Lalu Minor, Magsi Minor, Drakhi Minor & Gabri Minor including allied structures in Nasrat Division.	Irrigation	441.727
1763	Construction of C.C. Lining from Head to Tail of Pubjo Minor & Kazi Ahmed Minor including allied structures in Dad Division.	Irrigation	418.335
1771	Construction of Pre-stressed Bridge over Rohri Canal at RD-288 near village Banho Mangrio & Construction of Bridge on Dad Wah RD-25 Opposite Village Sardar Moola Bux Mubejo and 2 Nos. Bridges on Dalipota Minor Taluka Naushahro Feroze.	Irrigation	201.397
1772	Cement Concrete Lining of Ali Bahar Branch from RD-0+00 to RD-20+900	Irrigation	280.895
1777	C.C. Lining of Nagna Distry from RD-0.00 to 82+500 (Revised 05-08-22)	Irrigation	1021.259
1791	Construction of X-Regulators along Garhi Chand Distry RD-45, Jani Dero Distry RD-24.5, Replacement of Deck Slab and Flaxier Apron Road Bridge over B.S Feeder RD-114 and Construction of Road Bridge RD-37 Qaser Shakh and Hairo Shakh RD-8 & Construction of Stone Pitching from RD-55 to 90 B.S Feeder Guddu Barrage Region (Revised on 29-03-23).	Irrigation	276.898
1803	Construction of Retaining wall along Chota Begari RD-17 to 23 (City Portion) and Repair of Sindh Canal Sub Division and Resident of AXEN.	Irrigation	182.887
1851	Construction of Six (06) Nos Umeed-Jo-Wandio, Ranasar, Gotrawa, Abasar, Khane-Jo-Wandio and Khetlai Dams in Nagarparkar Area (Thar Region) (SDG # 6)	Irrigation	852.000
1872	Construction of One (01) Residence at Tangwani (SDG # 16)	Law, Prosecution & HR	9.787
1891	Construction of Four (04) Court Building at Naushehro Feroze (2 ADJs & 2 JMs) (Revised on 05.01.23)	Law, Prosecution & HR	115.419
1900	Construction of One Court at Nara (SDG # 16)	Law, Prosecution & HR	38.319
1901	Construction of additional Court / Record Room for District West and Extension of Bar Room (Revised on 10.3.20) (C:300.742+R:32.815) (SDG # 16)	Law, Prosecution & HR	333.557
1927	C.C Lining of Landhi-I Minor from RD-0 to 25+400 in Tando Allahyar Sub-Division (SDG # 6)	Lining of Main Canals	216.169
1934	Cement Concrete Lining of Masoodi Distry RD-0.00 to Tail (SDG # 6)	Lining of Main Canals	391.171

ADP	Name of Scheme	Sector	Estimated Cost
1948	Cement Concrete Lining of Husri Distry from RD-18+500 to 37+000 (SDG # 6)	Lining of Main Canals	219.617
1951	C.C Lining of Toori Minor Head to Tail (SDG # 6)	Lining of Main Canals	190.518
1957	C.C Lining Chach Minor RD+00 to 21+200 (SDG # 6)	Lining of Main Canals	133.068
1959	C.C Lining of Chitti Minor RD-0 to 33 (SDG # 6)	Lining of Main Canals	299.741
1966	Lining of Nendhra Minor from Bangli Regulator Jam Branch Tando Adam Sub-Division-I Hala Division Rohri Circle	Lining of Main Canals	100.000
1979	Establishment of Veterinary Centres in Sindh - Phase-II (SBA, Shikarpur, Tharparkar, T.M.Khan, Larkano, Ghotki, Dadu & Khairpur) (C:69.614 + R:30.250) (SDG # 2)	Livestock & Fisheries	99.864
1980	Switching Traditional / Conventional Livestock Farming to Contemporary (Revised on 19.05.2023 (R: 146.870) (SDG#2)	Livestock & Fisheries	146.870
1981	Establishment of Rural / Backyard Poultry Farming in District Ghotki & Larkano Revised on 22.03.2023 (R: 157.240) SDG#2	Livestock & Fisheries	157.240
2013	Construction of (55 Nos) Tough Tiles / Paver roads and drainage schemes in District Kashmore (SDG # 6)	LG (Water Supply)	126.931
2014	Providing Water Supply & Drainage schemes at various places of District SBA (SDG # 6)	LG (Water Supply)	425.000
2019	Providing of 10 Nos. Suction Machines and 10 Nos. High Pressure Jetting Machines including Up-gradation of existing machines for improvement of Sewer work in different Districts of Karachi (SDG # 6)	LG (Water Supply)	899.920
2022	Rehabilitation of Northern Sewage Treatment Plant (SDG#6)	LG (Water Supply)	100.000
2023	P/L/J testing of 60" Dia PE Pipe Water Supply Raising Main From Cananl Intake Pumping Station to Pre-Settlement Lagoons i/c Interconnection and Allied Works, Hyderabad (SDG#6)	LG (Water Supply)	323.945
2024	Improvement of Drainage System of Sukkur City (Revised)	LG (Water Supply)	643.330
2025	Phase-I of 25 years Sewerage/ Drainage Master Plan of Mirpurkhas (Revised on 01.4.21)	LG (Water Supply)	3762.379
2029	Up-gradation of NEK (P&F) K-II & K-III Pumping Station and Filter Plant District Malir	LG (Water Supply)	520.880
2031	Up-gradation of old and new Pumping stations of Ghara, District Thatta	LG (Water Supply)	329.736
2040	Providing & Laying 400 MM, 315 MM, 200 MM, 160 MM & 110 MM P.E line I/C 15" Dia, 12" Dia, 8" Dia, 6" Dia & 4" Dia Sluice Value I/C 02 NSO, DWT Vertical Turbine Pumps in UC-01 & UC-02 Akhtar Colony, Kashmir Colony Defence views Phase-I & II Adjoining Area for Improvement of Water Supply in Jamshed Town (Revised on 29.05.23)	LG (Water Supply)	299.490
2041	Construction of Cover Drain/Repair of exisitbg Drain Ward No. 1,2,3,4,5,6,7,8,9 & 10 MC Rohri District Sukkur (Revised on 25.05.23)	LG (Water Supply)	128.000
2042	Construction of CC Paver, Drain Various Wards of Town Committee Bagrani & CC Paver and Drain Bedil Bekas Tunnel to via Bedil Beks Dargha to Beri Chowk M.C Rohri District (Revised on 18.04.22)	LG (Water Supply)	91.227
2043	Construction of Paving block CC Drain and Water Supply for various Streets and Villages of UC Arrore, District Sukkuar (Revised on 25.05.23)	LG (Water Supply)	181.400
2044	Construction of Paving blocks, CC Drains & Water Supply Scheme for Various Streets & Villages of UC Trimoonh, District Sukkur (Revised on 25.05.23)	LG (Water Supply)	184.000
2045	Construction of Paving Block CC Drains for Various Streets & Villages of UC Kotri, District Sukkur (Revised on 25.05.23)	LG (Water Supply)	120.900
2046	Construction of Water Supply scheme and Under Ground Tanks	LG (Water Supply)	97.967
2047	Construction & Rehabilitation of Main / Internal Roads. Providing Sewerage line of 12' and 18' dia RCC Pipe, Water line of 4' dia PE Pipe and Installation of Paver Blocks / CC flooring & Street lighting in Bukkhar Goth, Sikander Goth, Abbas town, Abdullah Palari Goth and Various Areas of UC-29.	LG (Water Supply)	95.418
2048	Road Carpeting, C.C Flooring Sewerage line, Manzoor Colony-II (UC-06)	LG (Water Supply)	84.749
2060	Improvement of water supply line, Installation of sewerage line, paver block and road carpeting in UC-17, UC-27 & UC-28 (Revised on 14.04.2023)	LG (Water Supply)	178.677
2062	Water supply line, Sewerage line, Paver Block in UC-6 & UC-7 Golimar, Karachi	LG (Water Supply)	187.120
2071	Improvement of water supply and installation of Sewerage line and Paver Block in UC-33 & 34 Baldia Town. (Revised on 17.04.2023)	LG (Water Supply)	177.146
2078	Rehabilitation / Improvement of Road / Sewerage Line & Water System	LG (Water Supply)	96.805
2079	Rehabilitation / Improvement of Road / Sewerage line & Water system in the area of PS-127, 128.	LG (Water Supply)	150.000
2080	Construction of CC Block for Various Streets of Taluka Qasimabad & Taluka Rural Hyderabad (Revised on 13.12.22)	LG (Water Supply)	169.570

ADP	Name of Scheme	Sector	Estimated Cost
2081	P/L/J & Testing of 4", 6", 8" & 12" dia P.E /PVC Water Supply lines at Different Areas of Hyderabad	LG (Water Supply)	48.654
2082	Rehabilitation of Mir Khan Drainage Pumping Station and Providing of Nullah / Sewer Line from SRC to Bostan House Unit No. 12, Taluka Latifabad Hyderabad	LG (Water Supply)	99.948
2084	P/L/J of Paver Block Roads of U-C #04, 05, 06, 08 Mirpurkhas Length. 6.12 KMs (Revised on 25.05.23)	LG (Water Supply)	167.226
2085	Providing & laying of Paver Block Roads in U.C. # 02, 03 (1.54 km) & Construction of Road in U.C. Old Mipur, U.C. Mir Aachan (3.00 km) Taluka H.B Mari (Revised on 25.05.23)	LG (Water Supply)	78.184
2086	Improvement of Link Road with Paver Block from Allah Wala Chowk to Kambeer - Shahdakt road via Sui Gas Office i/c Approaches to Various Streets (2.60 kms) Shahdakt City	LG (Water Supply)	98.174
2087	Providing & Laying of Paver Block in Various Links of Muhallah Osta Gahi, Muhallah Dabar, Muhallah Shaikh and Internal Streets of Muhallah Bhurgari upto Bhurgari Regular Khairpur including Masonery Structure (340426 Sft) Taluka Khairpur (Revised on 03.06.23)	LG (Water Supply)	157.165
2088	Providing & Laying of Paver Block from Ferdous Masjid, Mill Colony, Jinnah Colony, Madina Colony Road to Technical University Road via Food Goodown including Various Streets of Khannan Shah Muhallah, Mangi Muhallah, Nizamani Muhallah and Kamangar Muhallah UC Shah Latif upto Bhutta village on west of east Feeder near Khaki Shah Bridge i/c Masonery Structure Taluka Khairpur (Revised on 03.06.23)	LG (Water Supply)	197.446
2089	Construction of Town Committee at Village Punhal Khan Chandio Taluka Sakrand District Shaheed Benazirabad (SDG # 9)	LG (Water Supply)	27.483
2090	Construction of New 100 MGD Pump House (Equipped with M&E Pumping Machineries) at Dhabeji (Revised on 07.04.22) (SDG # 6)	LG (Water Supply)	1620.860
2091	Rehabilitation of Drainage Works & Construction of New CC Flooring in Village Ber Sharif, Taluka Kamber (Revised) (SDG#6)	LG (Water Supply)	99.682
2118	Providing & Laying Water Supply and Drianage Line at Taluka Qasimabad, District Hyderabad	LG (Water Supply)	100.000
2119	Construction / Improvement of CC Paving Block & CC Block at Taluka Rural Hyderabad & Taluka Qasimabad District Hyderabad	LG (Water Supply)	149.999
2211	Construction of CC Paving Block / CC Block of Internal Sreets Shah Latif Colony, Chandio Colony, Narejo Village, Mehar Colony, Panhwar Village Bhatti Village, Jinnah Colony, Kohisar & Habib Form Allah Bux Brohi Goth Taluka Latifabad District Hyderabad	LG (Water Supply)	79.997
2216	CC/Paver & Open Drain in various Ucs of Ward 1, Ward 2, Ward 3 & Ward 4 of Taluka City Hyderabad	LG (Water Supply)	268.961
2256	Replacement of Drainage System (12", 24" & 36"), & Construction of Nalla at Mowach Goth, Gulshan-e-Benazir 500 Quarter, Budhani Goth, Tikkri Village, Dilfulabad, Sher Muhammad Village, Machhar Colony, District Keamari	LG (Water Supply)	90.953
2261	Construction of Road 03km link Road from Jarha Stop to Village Fateh Khan Sohu UC- Kamaro Taluka Bathoro. Construction of CC Paver Block in different Villages of UC- Kamaro Taluka Mirpur Bathoro District Sujawal	LG (Water Supply)	69.850
2262	Providing /Lying and Fixing of C.C paving & open surface drain in various villages of PS- 63 Taluka Rural Hyderabad	LG (Water Supply)	69.999
2276	Urban Water supply scheme Sehwan improvement & Extension (Phase-II) Balance work of Filtration Plant, Taluka Sehwan, District Jamshoro	LG (Water Supply)	193.182
2277	Construction of RCC Nallah including paver Block and replacement of P.E Pipe lines in the route of RCC Nallah for Sehwan Town, District Jamshoro	LG (Water Supply)	189.562
2278	Construction of CC Paving Block, CC Block & Drain Nali in UC Dhamachani & UC Narejani & UC Mori, Taluka Rural District Hyderabad	LG (Water Supply)	150.000
2279	Construction of CC Paving Block, CC Block & Drain Nali in UC Musa Khatiyani, UC Sawan Khan Gopang & UC Tando Qaiser, Taluka Rural District Hyderabad	LG (Water Supply)	181.000
2280	Construction of CC Paving Block, CC Block & Drain Nali in UC Chukhi, UC Moolan & UC Almani, Taluka Rural District Hyderabad	LG (Water Supply)	178.900
2281	Construction of CC Paving, CC Block & Drain Nali in UC Seri, UC Tando Fazal, UC Halepota & Town Committee Tando Jam, Taluka Rural District Hyderabad	LG (Water Supply)	179.000
2282	Construction of CC Paving Block, CC Block & Drain Nali in Tando Alam Mari, UC Sanhwar & UC Behram, Taluka Rural District Hyderabad	LG (Water Supply)	150.000
2283	Construction of CC Paving Block, CC Block & Drain Nali in UC Bohiki & UC Tando Hyder, Taluka Rural District Hyderabad	LG (Water Supply)	149.000
2454	Construction of floating jetties and Passenger sheds at Baba, Bhit & Mubarak village, Karachi. (SDG # 15) (Revised on 15.03.22)	LG (Bldgs)	304.984
2458	Construction of Mayor Office, Sukkur (ADP#1620/2021-22) (SDG # 9)	LG (Bldgs)	59.990
2459	Construction of Sukkur Municipal Corporation, Sukkur (ADP# 1621/2021-22) (SDG # 9)	LG (Bldgs)	72.047
2462	Construction of Zulfiqar Oil Tanker Parking Terminal Ph-II Zulfiqarabad Karachi (KmC)[GoS share 50% (Rs. 429.955 M), KmC share 15% (Rs. 128.987 M), MP&NR share 5% (Rs. 42.996 M), OMCS share 20% (Rs. 171.982 M), Non POL share 10% (Rs. 85.991 M)] (SDG # 9)	LG (Roads)	859.911
2464	Widening /Reconditioning of link road from Tail Mori to Tando Allahyar Sugar Mill via Sobhraj mile 2/0-5/6 (6.03 Km) (SDG # 9)	LG (Roads)	77.409
2468	Various Development Schemes of Kamber, Shahdaktot (31 Nos.) (SDG # 9)	LG (Roads)	743.371

ADP	Name of Scheme	Sector	Estimated Cost
2471	Rehabilitation of 4000 Road (SDG # 9)	LG (Roads)	246.000
2472	Rehabilitation / Improvement of Shahrah-e-Humayun (From Karimabad Flyover to Ziauddin Roundabout between Moosa Colony and Block 4&5) by road work, Water & Sewerage works, RCC perforated SW Drain, lighting work including beautification of Ziauddin Roundabout, F.B.Area District Central, Karachi (SDG # 9)	LG (Roads)	172.560
2473	Construction of Road from Village Toung Shareef to Thana Ahmed Khan mile 0/0 -12/4 (20 Km), Taluka Thana Bula Khan, District Jamshoro (SDG # 9)	LG (Roads)	247.581
2474	Construction / Reconditioning of Roads (7 units) in UC Arzi Bhutto, Taluka Sijawal Junejo (18.4 Km) (SDG # 9)	LG (Roads)	164.681
2475	Construction / Reconditioning of Roads (16 units) in UC Mastoi, Taluka Sijawal Junejo (30 Km) (SDG # 9)	LG (Roads)	206.528
2476	Construction / Reconditioning of Road (14 Units) in UC Seelra, Taluka Shahdadkot (14.7 Km) (SDG # 9)	LG (Roads)	112.562
2477	Construction / Reconditioning of Roads (02 Units) in Shahdadkot City, Taluka Shahdadkot (6 Km) (SDG # 9)	LG (Roads)	70.000
2478	Construction of Road from Indus Highway to Adam Camp Jamshoro I/c M/Structure @ Mile 0/0-5/0. Taluka Kotri, District Jamshoro (Re-revised on 03.01.23)	LG (Roads)	194.661
2484	Construction of Dumlottee Road from Dumlottee Well to M-9 & M-5 Link Road (12.3 Km)	LG (Roads)	798.323
2486	Reconditioning of road from Majeed Kerio-Mehrabpur road to Vill Dado Gohram Faqeer Zardari, UC Marvi, Taluka Sakrand Mile 0/0-3/5 (5.80 Km) (Revised on 03.01.23)	LG (Roads)	167.790
2497	Construction/Installation of 10 (TEN) No. Pedestrian Bridges at Different Locatios of Karachi (Revised on 31.05.23)	LG (Roads)	564.109
2499	Construction of roads in various U.Cs: (a) Construction / Remodeling of road from 68 Mori road to connect Jam Wah Mori 2.5 k.m (b) Construction of road from Chak road to village Jangi Khan Mari Deh 5-Chak (2.00 Km) (c) Construction of road from Preshan stop to village Shabir Shahani via Raheem Bux Brohi 1.5 Km Deh 44- Narat. (d) Construction of road from Dost Ali rind road to village Sono Khan Mari, Approaches (04 Furlong). (e) Road from 60th Mile main Phatak to Rehmatullah Jamali House via Hafiz Amjad Ali Abro House, Daur City 1000 ft. (f) Road from Mehran Highway to village Mubarak Chandio 3000 ft. (g) Construction of road from Nabi Dad Brohi road to village Amjad Shah Ji Kubi Deh 40 Dad road mile 0/0-0/3+110 (0.63 Km). (h) Paver Block in various streets of Town Committee, Bandhi. (i) Paver Block in various streets of Town Committee, Jam Sahib. (j) Paver Block in various streets of Star Colony, Town Committee, Daur.	LG (Roads)	161.896
2500	Construction of road Village Hassan Dohar, Construction of road village Master Hidayatullah Mallah via Dad Jat, Construction of road village Nooro Thahmoor, Construction of road village Ibrahim Madhro, Construction of road village Nazir Mallah, Construction of road village Wadero Sindhu Mundro, Construction of road village Mir Muhammad Rind Wahiya Khaskheli Bridge: Sim Nali village Sindhu Mundro	LG (Roads)	90.780
2501	Construction / Improvement of 19 nos. roads of District Sujawal (35.41 Km)	LG (Roads)	197.445
2505	Construction of roads alongwith drainage, Sewerage, Pipes and paving blocks in UC-2 Muslimabad, Malir Karachi	LG (Roads)	118.300
2509	Construction of road Milad Mustafa Chowk via Long Bhatti to National Highway and Ghulam Ali Shaikh Chowk via Piyaro Chohan construction C.C Topping Umer Khas wah village Jatoi to Eidan Shaikh, paver block and drains UC Hingoro and UC Nindapur Kot Bullo, Kolachi Sirohi	LG (Roads)	125.172
2510	Const: of Road Tando Jan Muhammad to Soomro Khan Kalohi (Balo jo kumb) to village Mir Hayat Talpur Deh 265 to Mir yar Muhamamd (Rabou) connect to Tando Jan Muhammad Digri Road (Revised on 11.05.23)	LG (Roads)	171.746
2513	Construction of Road from Dargah Shah Bukhari to Ayoub Hotel N-5 (3.50 Km) Taluka Qasimabad Hyderabad (Revised on 25.05.23)	LG (Roads)	192.771
2514	Improvement / Construction of Road from Sanjhar Mir Bahar to Hyderabad Bypass via Sajjan Detho (3.60 Km) Taluka Qasimabad Hyderabad (Revised on 11.05.23)	LG (Roads)	162.791
2518	Construction of road from Chaudhry Nek Muhammad road (near Ali Muhammad Katiar) to village Ramzan Jokhio (via village Khaman Jokhio, Kabil Bathro and Ramzan Jokhio water supply point), Taluka Mirpur Sakro, District Thatta	LG (Roads)	60.000
2524	Improvement & Reconstruction of Roads in UC-37 Ward 1	LG (Roads)	81.007
2526	Dualization of Old Indus Highway City Portion Larkano from Larkano Gate to connect Indus Highway (N-55) = 3.60 Km	LG (Roads)	190.678
2528	Reconditioning of Link Road from Nawabshah Sanghar Road to Village Haji Daim Khan Dhamrah District Sanghar and Construction of Pure Block Streets village Haji Daim Khan Dhamrah District Sanghar	LG (Roads)	37.404
2529	Construction of road and footpath from Jinnah Avenue to Saadi Garden in Scheme-33, Karachi (Revised on 29.05.23)	LG (Roads)	305.946
2531	Reconditioning / Improvement of various (6 Nos) roads of District Sukkur (5.3 Kms) (Revised on 08.03.23)	LG (Roads)	252.000
2585	Construction / Reconditioning of road from Larkana near professor colony to village shahabad parallel to ghaar wah (2.1 Km) District Larkano	LG (Roads)	138.994
2621	Construction of internal road of Shah Inayat village Kiran Hospital Road PS-100	LG (Roads)	29.895
2626	Widening and reconditioning of roads of city Khairpur (ADP 2021-22 Gen. Sr. No. 1655)	LG (Roads)	270.000

ADP	Name of Scheme	Sector	Estimated Cost
2627	Construction and Rehabilitation of Hyderabad Rural Road Taluka Tando Jam (SDG # 9) (ADP 2021-22 Gen. Sr. No: 1637)	LG (Roads)	1560.157
2784	Rehabilitation and Construction/ Re-construction of Veterinary Hospital/ Dispensaries and Centres in District Khairpur (39Units) (C:137.511+R:1.461)(SDG#2)	LG (Livestock)	138.972
2787	Establishment of Cattle Colony at Rohri (C:339.939)	LG (Livestock)	399.939
2789	Renovation & Rehabilitation of Temples in Various UC's of Sukkur, Shikarpur & Jacobabad (SDG # 11)	LG (Community Services)	55.000
2791	Constt: of 05 Nos. Union Council Offices in PS-73 (C:40.000+R:5.000) (SDG # 11)	LG (Community Services)	45.000
2792	Establishment of Theme Park at Khairpur City (Revised on 12.08.21)	LG (Community Services)	198.195
2793	Establishment of Covered Market at Old Bus Stand Khairpur (Revised on 01.04.21)	LG (Community Services)	222.090
2795	Construction of Compound Wall Around Graveyard Village Rajab Dayo, Graveyard M.C Rohri, Bakaar Graveyard, Khai Dargha Hyder Ali Shah, Fazalabab Graveyard, Massan Road Graveyard, Makhdoom Family Graveyard, Kot Mir Yaqoob Ali Shah Graveyard, Near Railway Station Graveyard, Kot Jan Ali Shah Graveyard, Gul Shah Graveyard, Memon Muhallah Graveyard, Kachi Abadi Graveyard, Sakhi Deen Panah Graveyard Taluka Rohri (Revised on 25.05.23)	LG (Community Services)	115.000
2796	Beautification of M.C Rohri District Sukkur (Revised on 25.05.23)	LG (Community Services)	100.000
2797	Development of Ghazi Abdul Rasheed Park Sukkur	LG (Community Services)	199.998
2798	Establishment of Dispensaries & Parks and Grounds in Different UCs of NA-249	LG (Community Services)	195.364
2799	Rehabilitation of Grounds & Parks, Eid Gah Ground Ward-2, Railway Ground Ward-3, Qalandari Ground Ward-7, Park in Railway Colony Bulbul Barrick Ward-3 Park in Chandio village Adjoued to Dada Bhai village, Park in Kaleem Qazi Ground Ward-7	LG (Community Services)	132.477
2824	Establishment of Zoological Park at Khairpur (Ph-II) (SDG#8) (ADP # 1419 of 2020-21)	LG (Community Services)	54.827
2825	Constt: of Roundabouts and Landscaping of Khairpur City (ADP # 1421 of 2020-21)	LG (Community Services)	50.000
2855	Rehabiliton/Renovation of Government Low Cost Houses & Shops at Jam Nawaz Ali City, District Sanghar	LG (HTP)	230.720
3242	Repair Maintenance & Rehabilitation of Various Road and Allied Works at SITE Karachi (Revised on 05.04.22)	Mega Schemes for Karachi	2392.949
3243	Rehabilitation / Reconstruction of Shahrah-e-Noor Jehan from Abdullah College to Qalandaria Chowk (Revised on 10.05.23)	Mega Schemes for Karachi	3367.735
3244	Reconstruction of Road from Sher Shah Chowk to Mirza Adam Khan Road intersection (District West) including SWD System	Mega Schemes for Karachi	901.580
3245	Rehabilitation / Reconstruction of Road from Café Piyala (near Gulberg Chowrangi) to Rashid Minhas road (near UBL Sports Complex) (Revised on 17.05.23)	Mega Schemes for Karachi	902.131
3246	Reconstruction of Rafiqi Shaheed Road and Kalapul Road from Shahrah-e-Faisal to Main Korangi Road (Revised on 17.05.23)	Mega Schemes for Karachi	526.268
3249	Re-Construction / rehabilitation of Chakiwara Road, Mehrab Khan Essa Road and Tannery Road, Lyari Town (District South) Including SWD System (Revised on 17.05.23)	Mega Schemes for Karachi	1500.000
3250	Construction of Flyover and Underpass at Johar Chowrangi Intersection	Mega Schemes for Karachi	4225.601
3251	Rehabilitation/Replacment/Improvement of Water Supply and Sewerage System including E&M Inslation of Pumping Station of Each District Karachi (KW&SB)	Mega Schemes for Karachi	789.127
3254	Re-construction of Syed Raees Ahmad Jafri road from Peoples Chowrangi up to Rashid Minhas road (Revised on 05.04.23)	Mega Schemes for Karachi	712.930
3269	Construction of Prayer Hall at St. Paul's Church Azam Basti Karachi	Minorities Affairs	20.000
3272	Construction of Satsang Hall at Pir Sumbak Taluka Thana Bulla Khan District Jamshoro	Minorities Affairs	20.000
3276	Construction of Compound Wall and Hall at Christian Graveyard at Deh Ghab Survey No.635 Taluka & District Tando Allahyar	Minorities Affairs	19.926
3277	Rehabilitation & Construction of Compound Wall and Hall at Children Massan at Sujawal City	Minorities Affairs	20.000
3278	Rehabilitation / Renovation of Dharmshala at Hindu Lohana Shamshan Ghat Umerkot	Minorities Affairs	20.000
3279	Construction of Compound Wall & Hall at Hindu Massan Dhoronaro Taluka Pithoro District Umerkot	Minorities Affairs	20.000
3282	Construction of Satsang Hall, Compound Wall & Paver Blocks at Aba Ji Than at Village Rana Jagir Taluka & District Umerkot	Minorities Affairs	20.000
3286	Construction of Dharmshala & Satsang Hall / (Lali Bai) Maheshwari MoHalla Digri District Mirpurkhas	Minorities Affairs	20.000
3290	Construction of Prayer Hall & BoundaryWall of Church at Masih Graveyard Padari jo Goth UC Miyan Taluka & District Sanghar	Minorities Affairs	19.836
3291	Renovation of Khorī Darbar UC Khorī Taluka Khipro District Sanghar	Minorities Affairs	19.836
3292	Construction of waiting Hall, Thala (Cremation Place) and Paver Blocks at Hindu Massan Peru Mal Town Deh Sattar Pir District Sanghar	Minorities Affairs	20.000
3293	Construction of Prayer Hall & Compound Wall at Masih Graveyard Nawabshah & Rehabilitation of Hindu Community Hall at Shiv Mandir Ghareebabad Nawabshah	Minorities Affairs	30.000

ADP	Name of Scheme	Sector	Estimated Cost
3294	Construction of Ladies Satsang Hall with Compound Wall & Paver Blocks at Kanji Colony Near Ambedhkar Bhawan, Mithi	Minorities Affairs	20.000
3297	Construction of Satsang Hall, Compound Wall, Washroom & Water Tank at Nanjo Mal Menghwar north Colony Diplo Town District Tharparkar	Minorities Affairs	20.000
3298	Rehabilitation of Satsang Hall at Dado Ladhu Ram Temple Chhachro Taluka Chhachro, Tharparkar	Minorities Affairs	20.000
3303	Rehabilitation / Renovation of Temple & Satsang Hall at Village Doonhon Ibrahim Shah Taluka Babarloi District Khairpur	Minorities Affairs	19.835
3304	Rehabilitation / Renovation of Domes & Finishing Work i/c Floor Tile of Shri Krishana Mandir at Gambat District Khairpur	Minorities Affairs	19.812
3309	Construction of Compound Wall Christian Graveyard at Jacobabad City Taluka & District Jacobabad	Minorities Affairs	19.996
3310	Rehabilitation of Hindu Massan at Hayat Pitafi Mirpur Mathelo District Ghotki	Minorities Affairs	19.800
3312	Construction of Hall 2 Bathrooms 2 Cremation Places Platform sheds & Paver at Shamshanghat Jhampir District Thatta	Minorities Affairs	10.000
3313	Construction of Boundary Wall and Installation of 50 KVA Solar System with 24 Hours Backup at Mole Darbar Taluka Thana Bula khan District Jamshoro.	Minorities Affairs	44.800
3333	Renovation & Rehabilitation Shri Geeta Sangat Hall, Sant Chatro Ram (Shiwalo) Sukpul Shikarpur.	Minorities Affairs	9.999
3334	Rehabilitation of Guru Nanik Mandir Chak District Shikarpur	Minorities Affairs	14.998
3342	Construction of prayer Hall with Rooms at Bomanshaw Minocher Homji Parsi, Plot no. 96 Depot Line near Empress Market Saddar Karachi	Minorities Affairs	9.987
3416	Construction/Reconstruction of District office-Cum-Residences of Sindh Bureau of Statistics at Kamber	Planning & Development	21.870
3417	Construction/Reconstruction & Rehabilitation of Field Offices-Cum-Residences of Sindh Bureau of Statistics at Meher	Planning & Development	19.993
3420	Reconstruction of Field offices-cum- Residences of Sindh Bureau of Statistics at Mirpurmathelo	Planning & Development	34.529
3421	Reconstruction of District & Sub Divisional Field offices-cum Residences of Sindh Bureau of Statistics at Khairpur, Tharimirwah, Kotdiji	Planning & Development	82.030
3426	Strengthening & Capacity Building of Regional Offices of M&E Cell at Hyderabad & Sukkur (SDG # 17) (Revised on 19.04.2023)	Planning & Development	327.824
3441	Remaining works of RHS-A Centre at Garhi Khairo(C:5.817) (SDG # 3, 5)	Population Welfare	5.817
3442	Remaining works of RHS-A Centre at Dokri(C:2.847) (SDG # 3, 5)	Population Welfare	2.847
3444	Rehabilitation of RHS-A Centres Mirpurkhas Division (SDG # 3, 5)	Population Welfare	14.874
3445	Remaining works of RHS-A Centre at Mirpur Mathelo (C:5.778) (SDG # 3, 5) (ADP #2027 of 2021-22)	Population Welfare	5.778
3446	Remaining works of RHS-A Centre at Lakhi (C:5.503) (SDG # 3, 5) (ADP #2028 of 2021-22)	Population Welfare	5.503
3463	Replacement of Damaged Rising Main East Jamrao Water works to Khipro Bus Stand Booster Pumping Station for Water Supply Scheme Mirpurkhas City.	Public Health Engineering	100.000
3464	Improvement / Extension water supply scheme Khararo syed and Khararo Charan	Public Health Engineering	34.830
3472	Rural Water Supply Scheme Pir Patho & Sourranding Villages (SDG # 6).	Public Health Engineering	63.099
3473	Improvement & Extention of Water Supply Scheme Baghan (SDG # 6).	Public Health Engineering	25.322
3479	Improvement & Extension of Water Supply Scheme for Kotri City (SDG#6)	Public Health Engineering	160.900
3486	Water Supply Scheme of Village and Union Council Akbarpur (Revised on 16.05.23)	Public Health Engineering	89.000
3487	Water Supply Scheme of Village and Union Council Khabri Bhatt (Revised on 16.05.23)	Public Health Engineering	77.799
3488	Water Supply Scheme of Village and Union Council Lal Jurio (Revised on 16.05.23)	Public Health Engineering	87.014
3489	Water Supply Scheme various Areas of Abad Lakha and Arain Sukkur (Revised on 18.04.23)	Public Health Engineering	131.070
3490	Construction of 3.0 MGD Filtration Plant i/c distribution network for Water Supply Scheme Rohri Taluka Sukkur (Revised on 19.04.2023)	Public Health Engineering	641.518
3491	Rural Water Supply Scheme Village Jaggan Bhayo (Shifting of Source)	Public Health Engineering	96.520
3492	Water Supply Scheme Mir Sher Muhammad Khan UC Saiful Taluka Tangwani (SDG # 6)	Public Health Engineering	14.800
3497	Rural Water Supply Scheme Chak # 23, 24 Dewan Wali Ram	Public Health Engineering	51.448
3514	Construction of Tube Well for Village Chairman Muhammad Idrees Soomro, Union Council Khokhrapar, Taluka & District Umerkot	Public Health Engineering	7.991
3527	Solarization of Water Supply Scheme Sita Road and K.N Shah (intake works source sites) i/c installation of Express Feeder Power Connection facilities of Old Water Works	Public Health Engineering	80.000

ADP	Name of Scheme	Sector	Estimated Cost
3529	Construction of Water Supply Scheme at Village Chakar Khan Seehol, Bhawal Gorar, Kolachi, Safar Lakhair, Amber and Dahot Village Taluka Mehar (SDG#6)	Public Health Engineering	50.000
3533	Construction of Filter Plants in various villages of Taluka Ratodero	Public Health Engineering	60.000
3537	Water Supply Scheme (Filtration) Sakrand Town (SDG # 6) ADP No.2068 (2021-22).	Public Health Engineering	400.473
3583	Construction of RCC Nala from Mehmood Goth to Sea Side at Lath Basti UC Rehri, Taluka Ibrahim Hyderi. (SDG # 6).	Public Health Engineering	99.789
3586	Rehabilitation of Urban Drainage Scheme Mirpur Sakro (SDG#6)	Public Health Engineering	150.152
3587	Construction of Drainage Scheme Garho City (SDG # 6).	Public Health Engineering	89.647
3588	Construction of Drainage Scheme Kati Bandar (SDG # 6).	Public Health Engineering	72.498
3589	Improvement and extension of Urban Drainage Scheme Ghora Bari Taluka Ghora Bari (SDG # 6).	Public Health Engineering	90.273
3590	Improvement and extension of Urban Drainage Scheme Ver Taluka Ghora Bari (SDG # 6).	Public Health Engineering	118.252
3591	Drainage Scheme along with CC Block for villages Nana Gandaro, Manik Behrani, Daragh Shah Mubeen, Abdul Majeed Sabughar, Daragh Shah Ladho via Kashighar Muhalla, Ghulam Thenga, Haji Khamiso Khaskheli, Christian Colony (SDG # 6).	Public Health Engineering	70.000
3592	Construction of Open Surface Drain, CC Flooring and Paving Block for Different Wards of Thatta City (SDG#6)	Public Health Engineering	174.283
3601	Improvement and Extension of Urban Drainage Scheme Manjhad, District Jamshoro (Revised on 16.05.23)	Public Health Engineering	118.324
3606	Construction of CC Block & Drains at Various Streets of District Jamshoro (Revised on 15.03.2022) (SDG # 6).	Public Health Engineering	120.682
3613	Drainage Scheme Village Hussain Kalwhar Taluka Pano Aqil (SDG # 6).	Public Health Engineering	15.000
3614	Drainage Scheme Village Rajib Ali Dayo, Pir Hasil Shah Colony, Murad Shah Colony Lokoshed and Village Khari Mumbrani and; Rehabilitation of Drainage Scheme Mola Mohib Shah Muhallah, Bedal Becus Tunnel disposal, Al-Abbad disposal Rohri City (Revised on 16.05.23)	Public Health Engineering	183.853
3615	Construction of Drainage Scheme at Various Village of Khabri Bhatt (SDG#6) (Revised on 18.04.23)	Public Health Engineering	151.956
3616	Construction of Drainage Scheme at various Village of Lal Jurio (SDG # 6) (Revised on 18.04.23)	Public Health Engineering	89.306
3617	Construction of Drainage Scheme at Various Areas of Abad Lakha and Arain Sukkur (Revised on 16.05.23)	Public Health Engineering	158.392
3618	Construction of Drainage Scheme Lal Mashaikh Sukkur (Revised on 16.05.23)	Public Health Engineering	109.864
3619	Construction of Drainage Scheme at Various areas of Newpind and Micro Tower Sukkur and Qureshi Goth (Revised on 16.05.23)	Public Health Engineering	176.775
3621	Drainage Scheme Village Piaro Labano, Village Lal Bux Mahtam, Village Ali Shaikh & Village Jatoi & Malik Taluka Rohri (SDG # 6) (Revised on 18.04.23)	Public Health Engineering	124.571
3623	Drainage Scheme Village Nabi Shah Waggan Taluka Garhi Yaseen (SDG # 6).	Public Health Engineering	24.265
3630	Improvement / Extension of Drainage Scheme Kamber (SDG # 6)	Public Health Engineering	648.500
3631	Rural Drainage Scheme Mubarakpur Taluka Miro Khan (SDG # 6) (Revised on 18.04.23)	Public Health Engineering	46.215
3632	Construction of C.C Drains and Paver Blocks for Muhallas of Shahdaddkot City (SDG # 6).	Public Health Engineering	100.000
3633	Paver Block and C.C Drains in Various Muhallas of Mirokhan City (SDG # 6).	Public Health Engineering	52.180
3634	Paver Block and C.C Drain in Various villages of Taluka Mirokhan and Sujawal and Kamber (SDG # 6).	Public Health Engineering	137.120
3635	Paver Block and C.C Drain in Various Muhallas of City Kamber. (SDG # 6).	Public Health Engineering	90.990
3636	Construction and Renovation Road & Paver Block & CC Drain in Various location in City Kamber & Taluka Kamber (SDG # 6).	Public Health Engineering	200.000
3637	Paver Block and C.C Drain in Various villages of Taluka Kamber & Warah (SDG # 6).	Public Health Engineering	146.910
3638	Construction of Renovation Road & Paver Block & CC Drain in Various Location in Town Ghaji Khuhawar (SDG#6)	Public Health Engineering	47.769
3641	Improvement & Extension of Drainage Scheme Aadilpur including Shaikh Muhalla Taluka Ghotki (SDG # 6) (Revised)	Public Health Engineering	97.455
3646	Construction of Surface Drains, CC Topping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Municipal Committee Moro Taluka Moro (SDG#6).	Public Health Engineering	142.255
3647	Construction of Surface Drains, CC Topping, CC Paver Blocks, Culverts, Birck Pavement and Pipe Line at Town Committee Padidan, Taluka Naushero Feroze (SDG # 6).	Public Health Engineering	44.258

ADP	Name of Scheme	Sector	Estimated Cost
3649	Rural Drainage Scheme for Village Mirwah Jagir Dadu Dero, Sardar Dad Muhammad Jakhriani, Taluka & District Jacobabad (SDG#6)	Public Health Engineering	21.776
3650	Drainage Scheme for Khandhkot Ward No. 1 to 16 (SDG#6).	Public Health Engineering	104.747
3654	Drainage Scheme Village Jahan Khan Bhangwar (SDG#6)	Public Health Engineering	33.484
3660	Providing or Surface Drain & CC Pavor for Drainage scheme Thari Mirwah (Revised on 16.05.23)	Public Health Engineering	199.326
3696	Construction of Surface Drains, CC Block and Paver Block at different Mohallas of Town Committee Hingorja, UC Sami, Village Niwaro UC Meerak, Village Razal Memon, UC Madd, Village Haji Abdul Rahim Bhutto UC Rasolabad, Abbasi Mohalla and Mir Mohalla Committee Sobo Dero (SDG # 6)	Public Health Engineering	62.789
3712	Providing Paving Blocks and various street of K.N Shah and Sita Raod (SDG#6)	Public Health Engineering	20.000
3716	Construction of Paver Block and Surface drain in Sinjhoru City (SDG# 6)	Public Health Engineering	80.000
3717	Elimination of three (03) Domestic Waste Water Disposal Pumping Stations & Diverting Sewage flow towards a new proposed disposal pumping station including construction of Drains, RCC Nala & Paving Block for Larkano city Drainage system (SDG#6).	Public Health Engineering	1240.045
3718	Construction of Drains i/c Pavement of left over streets with Paver Block at Different Muhallas of Larkano city (SDG#6).	Public Health Engineering	580.000
3721	Construction of Paver Block and CC drains in village Garhi Khuda Bux Bhutto and village Banguldero	Public Health Engineering	20.000
3729	Construction of Compound Wall and C.C paver SSD Dham Sukkur	Public Health Engineering	19.952
3731	Construction of CC Drains & Paver Blocks in various Mohallas of Kamber City. (SGD #6)	Public Health Engineering	50.000
3739	Rehabilitation of Drainage Scheme Perumal (SDG # 6) ADP No.2151 (2021-22).	Public Health Engineering	30.233
3740	Rural Drainage Scheme Dalel Dero Uc - Punhal Khan Chandio (SDG # 6) ADP No.2174 (2021-22).	Public Health Engineering	37.311
3741	Rural Drainage Scheme Mashak (old) Mashak (New) & Abdul Hameed para, UC -Gohram Mari, Taluka Sakrand (SDG#6) ADP No.2175 (2021-22).	Public Health Engineering	62.209
3742	Rural Drainage Scheme village Gohram Mari, UC Gohram Mari Taluka Sakrand (SDG # 6) ADP No.2176 (2021-22).	Public Health Engineering	24.115
3743	Rural Drainage Scheme Landhi, UC-Kamal Keroi, Taluka Sakrand (SDG#6) ADP No.2177 (2021-22).	Public Health Engineering	24.115
3744	Construction of RCC Covered Main Nala at various villages (06 Nos.) (Revised) Shahdadkot (SDG # 6) ADP No.2326 (2021-22)	Public Health Engineering	442.780
3745	Drainage Scheme of for Miro Khan Town (SDG # 6) ADP No.2328 (2021-22)	Public Health Engineering	119.278
3842	Construction of CC drain and paver block village Murtaza Chandio (Mirpur Buriro and village shoukat jarwar Taluka shahdadkot & Qubo Saeed Khan	Public Health Engineering	20.000
3868	Rehabilitation of 16 Filtration Plants for Urban & Rural Water Supply Schemes (SDG # 6)	Public Health Engineering	452.093
3877	Rehabilitation of Non-functional Water Supply & Drainage Schemes in District Sukkur (Phase-II) (SDG # 6).	Public Health Engineering	78.338
3903	Construction of Link Road from Village Shabbirabad to Muhammad Khan Sarki Road via Village Sain Dino & Faiz Muhammad Noonari and Construction of Link Road from Tangwani -36 Mile Road to Village Saif-ur-Rehman Rind, Taluka Tangwani.	Rural Development	18.000
3910	Construction of Link Road Pano Regulator to Shah Alam Shah Ji Wasi on Hyd Branch and Construction of Link Road Bio Dero to Village Abdullah Panhwar.	Rural Development	14.000
3911	Construction of Road from Sari Bypass to Village Wadero Mal Khan Palari, UC Sari, Taluka Thana Bulla Khan.	Rural Development	14.000
3916	Construction of Metalled Road from Sheedo Khan Road via Lodra Road via Piyaro Goth to Naik Muhammad Brohi and Construction of Road from Village New Laliyoon to Magsi Village.	Rural Development	24.700
4055	Renovation of Sindh Public Service Commission Rest House, Hyderabad	Sindh Public Service Commission	120.000
4058	Peoples Promise Sindh Social Protection Strategy - Feasibility and Institution Building (Revised on 26.04.23) (Jamshoro, Thatta, Tharparkar, T.M.Khan, Jacobabad, Maitiari, T.A.Yar, SBA, N.Feroze & Larkano)	Social Protection	339.920
4061	Establishment of Rehabilitation Center for Senior Citizens at Karachi (C:53.731 + R:21.469) (SDG # 5 & 10)	Social Welfare	75.200
4089	Construction of Sports Ground at Dahrki District Ghtoki (C:36.575)	Sports & Youth Affairs	36.575
4091	Rehabilitation & Renovation of Sports Complex Khalidabad Taluka Mirpur Mathelo	Sports & Youth Affairs	60.500
4099	Construction of Synthic Futsul Ground at Shaheed Benazirabad University	Sports & Youth Affairs	40.700

ADP	Name of Scheme	Sector	Estimated Cost
4103	Laying of New Blue Synthetic Hockey Turf & Digital Score Board at Existing Hockey Stadium NIPA	Sports & Youth Affairs	88.000
4105	Construction & Rehabilitation of Cricket Ground at Jinnah Government College and Installation of Net around the Boundary Wall of Annu Bhai Cricket Ground Nazimabad.	Sports & Youth Affairs	65.995
4106	Construction of Grassy Cricket Ground at Qadirpur	Sports & Youth Affairs	49.499
4109	Construction of Ladies Gym & Indoor Hall at Ghotki	Sports & Youth Affairs	55.000
4111	Construction of Futsal Ground for Ladies at Government Girls College	Sports & Youth Affairs	44.000
4113	Laying of Football Turf and Allied Works at Lyari International Ground, Phase -I (Revised on 14.04.23)	Sports & Youth Affairs	192.374
4115	Construction of Lakhmir Sports Ground at Taluka Jacobabad	Sports & Youth Affairs	49.500
4116	Construction of Grassy Cricket Ground at Sahib Khan Lund	Sports & Youth Affairs	49.499
4118	Rehabilitation and Up-gradation of Sports Ground at Karsaz	Sports & Youth Affairs	44.000
4119	Provision of Sports Facilities at SSB Sports Club, Qasiamabad	Sports & Youth Affairs	44.000
4121	Construction of Football Stadium in Manghopir	Sports & Youth Affairs	44.000
4122	Construction of Fitness Gym at Taj Mahal Jahangir Memorial Football Ground North Nazimabad	Sports & Youth Affairs	22.000
4165	Construction of Sports Indoor Hall, Synthetic Foot Ball Ground & Basketball Court at A.G Sindh Karachi (Phase-I), (ADP No. 2523 of 2021-22)	Sports & Youth Affairs	54.796
4236	Boring & Installation of 150 Nos Tubewells on Solar Energy for Assured Supply of 100 cusecs for Thar Coal from LBOD Spinal Drain RD-362 (Revised on 08.11.16)	Thar Coal Infrastructure	1936.266
4255	Construction of Bus Shelters on various routs at Jacobabad.	Transport & Mass Transit	107.978
4258	Safe custody of Ex-SRTC/ KTC Government Properties	Transport & Mass Transit	199.247
4286	Rehabilitation of Bus Terminal at Garhi Khairo.	Transport & Mass Transit	70.000
4289	Establishment of Women Complaint Cells at Sanghar, Kamber, Kashmore, Jamshoro, Khairpur, Shikarpur, Badin, Ghotki, Naushero Feroze, Thatta, T.A. Yar, Umerkot, Tharparkar, Dadu & Matiari. (R: 76.90) (SDG # 4, 5 & 16)	Women Development	76.900
4293	Renovation of Existing Building of Women Development Complex at Sanghar (Revised on 25.01.23)(C: 21.772+R:4.246) (SDG # 1,4, 5,8 & 9)	Women Development	26.018
4300	W/R of Kot Gulam Muhammad Jhudo via Sikriery and Tando Jam Mohammad mile 0/0-31/2 (50.0 Kms)	Works & Services	494.250
4306	Improvement / Construction of road from National Highway Bogo Wah on Both site (10.00 Kms)	Works & Services	260.815
4307	W/R of road National Highway to Tando Adam via Bhit Shah mile 0/0-17/0 (27.20 Kms)	Works & Services	747.346
4310	W/R of road from Arrore Bachal Shah to Choundko (32.18 Kms)	Works & Services	540.878
4320	Widening / Reconditioning of road from Bheda to Suhebja via Dargah Shah Abdul Rehman Mirani to connect National Highway @ Panj Moro i/c approaches to villages (12.00 Kms) (Re- Revised on 14.04.23)	Works & Services	434.410
4321	Reconditioning of road Mirpurkhas Bypass to Jhillori with asphalt Taluka Shujaabad mile 0/0-10/5 (17.0 Kms) (Revised on 14.04.23)	Works & Services	243.148
4335	Reconditioning of road from Airport road to village Mad Bahu via village Sijawal Tunio, village Haroon Tunio to Habib Petrol Pump Larkano Khairpur road i/c approaches to various villages and Reconditioning of road from village Hyder Brohi to village Gul Muhammad Jatoti (i/c M. Structure). (8.80 Kms) (Revised on 08.05.23)	Works & Services	122.538
4336	Reconditioning of road from Rahoja Bridge to village Shahani via village Khakhrani & village Bhoonbhatpur (4.00 Kms) (Revised on 08.05.23)	Works & Services	136.496
4337	Improvement of road from Shahdadkot Motorway Bypass (M-8) road @ Point Police Chowki to village Meenhoon Khan Leghari (Old Railway Track) via Juneja and Brohi (11.00 Kms) (Revised on 08.05.23)	Works & Services	185.974
4338	Reconditioning of road from Thouf Chosul - Bhand Chowk road Mahmoodabad Police Chowki to Miro Khan (7.00 Kms) (Revised on 08.05.23)	Works & Services	98.813
4340	Improvement and Construction of various roads of Taluka Sijawal (Revised on 08.05.23)	Works & Services	171.553
4341	Improvement and Construction of various roads of Taluka Qubo Saeed Khan (Revised on 08.05.23)	Works & Services	112.341
4342	Reconditioning of road from Behram to Kamber Miro Khan road via Buthi Mubarak Kalhoro, Tharo Wadhoo, Lal Bux Leghari (8.00 Kms) (Revised on 08.05.23)	Works & Services	122.865
4343	Rehabilitation / Widening and Reconditioning of road Rohri Interchange M-5 to Salehpat City Dual Carriageway (Due to Heavy Traffic existing 24' proposed 50') (0.80 Kms) (Revised on 25.01.23)	Works & Services	456.195
4344	Rehabilitation / Reconditioning of road from Ghulam Bund to Dhandi via Faqirabad (11.00 Kms) (Revised on 08.05.23)	Works & Services	159.371

ADP	Name of Scheme	Sector	Estimated Cost
4345	Reconditioning / Construction of road from Khanpur Thikratho road to Ibrahim Mahtam via Khameso Bhatti, Ali Madad Mahtam, Ucheer enclosed various links and Kabil Mahtam (18.60 Kms) (Revised on 17.03.23)	Works & Services	311.773
4346	Rehabilitation of road from NHA to Piryalo via Phul Wahan Razi Goth, Khedo Goth, upto village Khorkhani (8.00 Kms) (Revised on 08.05.23)	Works & Services	153.541
4347	Rehabilitation of various roads at village Serai Piyaro Khan, Nazar Mohammad Gaho, Imam Bux Palh, sahib Khan Chakrani, Shadi Shaheed road, Rattal Bhambhro and Babar Wada Jhango road to Ahdi Rajper (15.00 Kms) (Revised on 08.05.23)	Works & Services	196.880
4348	Reconditioning of road from Mehran N/Highway to Dejarja Nawab Ali Shah Bhambhan via Khariri road (14.00 Kms) (Revised on 08.05.23)	Works & Services	182.564
4349	Reconditioning of road from Jalal Jee Stop Mehran N/Highway to village Pholirhi via Bhangho Behan, UC Bhangho (11.60 Kms) (Revised on 08.05.23)	Works & Services	148.922
4350	Reconditioning of road from Sutyaro to Kharirah and Pir Bux Jalalani, UC Kharirah (7.00 Kms) (Revised on 08.05.23)	Works & Services	101.385
4351	Rehabilitation / Construction of road from Odha More to Ali Murad Jamali via Amanullah Odho. Paraocha Ulro, G. Nibo Ulro, Muhammad Hayat Ulro, Shaman Ulra, Mehmood Odho mile 0/0-7/4, (12.06 Kms) (Revised on 22.05.23)	Works & Services	202.457
4352	Rehabilitation / Construction of road from Assain road to Almedpur Bus Stop via Pir Badal, Tapali Sarak, Khawaja Pull mile 0/0-8/0, UC Pir (12.86) Badal, Taluka Kingri (Revised on 22.05.23)	Works & Services	291.444
4355	Improvement of road from Fakirabad to Jan Muhammad Gopang to Old N.H Way road mile 0/0-2/4 (4.00 Kms) Rehabilitation of road from Jhanda Shakh to Fakirabad upto GIMS road mile 0/0-5/0 (8.00 Kms) (Revised on 22.05.23)	Works & Services	211.403
4356	Reconditioning of road from Kumb to Jagir Ali Akbar road (6.80 Kms) (Revised on 08.05.23)	Works & Services	118.194
4357	Widening / Reconditioning of road from Khahira to Zafarabad (12.00 Kms) (Revised on 22.05.23)	Works & Services	261.022
4358	Widening / Reconditioning of road from Thari to Tarko (8.00 Kms) (Revised on 08.05.23)	Works & Services	179.089
4359	Widening / Reconditioning of road from Mehar Vessar to Bozdar Wada mile 0/0-2/4 (12.87 Kms) (Revised on 24.05.23)	Works & Services	240.204
4360	Widening / Reconditioning of road from Karoondi Town Committee Karoondi to Baseero Union Council Karam Khan Rajper road Taluka Faiz Ganj mile (13.00 Kms) (Revised on 24.05.23)	Works & Services	359.835
4361	Reconditioning of road from Pacca Chang to Karoondi via Hussain Shah & via Sijawal Khaskheli (5.20 Kms) (Revised on 08.05.23)	Works & Services	66.564
4362	Reconditioning of the road from Bab- e -Ahmed Shah Gate, National Highway Ranipur to Sobhodero City (11.26 Kms) (Revised on 24.05.23)	Works & Services	228.159
4364	Reconditioning of road from N/Highway to village Wali Muhammad Kalhoro via village Wada Bhellar, village Mehar Hussain Mangniyo, village Khaki, village Sando Machi, village Ameer Bux, village Buet Panhyar, village Khalifo Juman, village Setharja Lower and village Wali Muhammad Gadehi (8.00 Kms) (Revised on 08.05.23)	Works & Services	93.567
4365	Reconditioning of road from Tando Masti Khan road to Rafique Mahesar (Asphalt Work) 0/0-7/4 (12.06 Kms) (Revised on 24.05.23)	Works & Services	232.695
4366	Widening / Reconditioning of road from Khuhra City to Larkana road via Kamaldero, Pir Essa road (Asphalt Work) link with Syed Sabit Ali Shah to Shar (12.87 Kms) (Revised on 24.05.23)	Works & Services	213.119
4367	Reconditioning of road from Rafique Mahesar to Noraja via Khaat Nareja (Asphalt Work) 0/0-7/0 (11.26 Kms) (Revised on 08.05.23)	Works & Services	128.651
4369	W&R /Construction of road from Old National Highways Bhurghari Regulator to Hussain abad upto Makol Pahore Parallel to Mirwah Canal (Right Side Bank) (Phase-1) (2.50 Kms) (Revised on 08.05.23)	Works & Services	159.092
4370	W/R of road from Mori to Ahmedpur Pir Goth road via Raja Ulro Kot Mir Muhammad road (12.12 Kms) (Revised on 24.05.23)	Works & Services	278.297
4371	Reconditioning of road from Machar Minor to Sami to Merak via NiWaro, Taluka Sobhodero (6.00 Kms) (Revised on 08.05.23)	Works & Services	93.366
4372	Widening / Reconditioning of road from Haji Ali Nawaz Deepar to Achhi Masjid approach link village Budak (10.00 Kms) (Revised on 14.04.23)	Works & Services	241.998
4373	Reconditioning of road from Kandiaro Bus Stop to Saeed Khan Lakho via Siddique Lakho (10.00 Kms) (Revised on 11.04.23)	Works & Services	114.911
4378	Improvement / Rehabilitation / Construction of various roads / streets of Daur, Bandhi, Jam Sahib and Buchery City (35.03 Kms) (Revised on 31.05.23)	Works & Services	1006.980
4380	W/R / Construction of road from N.H.A Sarkari Khooh to connect Aumb Junejo road via Bachalpur, Muhammad Ismail Bhand road (16.00 Kms) (with 5cm thick Asphalt surface) (Revised on 14.04.23)	Works & Services	388.982
4381	W/R / Construction of road from N.H.A Nawab Wali Muhammad to connect Muhammad Ismail Bhand road via Jujhan Khan Muhammad Rind, Karam Bughio road (7.00 Kms) Actual Length 11.00 Kms (with 3.80 cm thick Asphalt surface) (Revised on 11.04.23)	Works & Services	149.368
4382	W/R / Construction of road from 60th Mile - 3 Chak Suhallo road @ 18 Shak Stop to connect Ghazi Khan Bhurgari road @ Nim Stop via Sui Gas H.Q & link to village Masood Nabi Noor along Akdohi Minor mile 0/0-5/2+330 (8.50 Kms) (Revised on 14.04.23)	Works & Services	243.155
4383	Reconditioning of road from Nawabshah - Sanghar road to village Ali Jan Brohi road mile 0/0-2/1 (3.40 Kms) (Revised on 11.04.23)	Works & Services	61.452

ADP	Name of Scheme	Sector	Estimated Cost
4385	Reconditioning / Construction of road from N.H Way Mir Khan Leghari road to connect Sakrand - Khadhar road via Hamal Faqeer, Mehmood Leghari, Jan Muahhmad Keerio, Abdul Wahid Soomro and Esso Keerio road (0.00 - 11.00 Kms) (with 3.80 cm Thick Carpet with Paver Machine) (Revised on 11.04.23)	Works & Services	149.947
4386	Reconditioning / Construction of road from Kazi Ahmed Pubjo road to connect Sher Purrian via Sun, Jeyad Leghari, Wali Muhammad Merasi, Khushhal Dahri (12.00 Kms) (Revised on 11.04.23)	Works & Services	181.662
4387	Reconditioning / Construction of road from Old National Highway to connect Al-Noor Sugar Mill road via Raj Muhammad Dahri, Khar Ashique Abad, Bahar Ji Koor and Bado Dahri road (11.80 Kms) (Revised on 11.04.23)	Works & Services	168.640
4389	Reconditioning of road from Mehran Highway @ Bhooral Shah Stop to village Abdullah Bughio via Gabol Stop and village Jeeand Khan Gabol mile 0/0-3/6 = 6.03 Kms (With 2' Thick Asphalt) (Revised on 11.04.23)	Works & Services	97.369
4390	(A) Reconditioning of link road from Khipro Ghulam Nabi Shah road to village Molvi Abdul Rehman Dars to Ding Khahi road via Dargah Abdullah Shah road mile 0/0 - 4/0 = (6.40 Kms) (TST 12' width) (PS -42, NA-216) (B) Reconditioning / Construction of link road from Aqil Hingoro road to village Haji Usman Chaniho to Hassan Ali Chaniho via village Drabhi to village Khamiso Khan Dars road mile 0/0 - 4/0 = (6.40 Kms) (TST 12' width) (PS -42, NA-216) (Revised on 06.04.23)	Works & Services	128.883
4391	W/R of Shahdadpur Gird Station road to Budho Chandio road mile 0/0-4/3 (7.00 Kms) (1-1/2' Thick Asphalt Surface 12' to 18' ft Width)(Revised on 22.05.23)	Works & Services	284.105
4392	Improvement of road from Mirpurkhas - Khan Patoyoon road to connect various villages (10.00 Kms) (Revised on 08.05.23)	Works & Services	163.489
4393	W/R of road from Dangan Bhurgari to Jhuluri (9.00 Kms) (Revised on 14.04.23)	Works & Services	234.815
4394	Reconditioning of road from Dharnio More to Talhi Station (12.60 Kms) (Revised on 11.04.23)	Works & Services	198.139
4396	Reconditioning of link road from Allah Bux Mirjat Stop to village Haji Pir Muhammad Baloch via village Haji Ismail Baloch & link to village Haji Sher Muhammad Baloch & village Amitan Baloch mile 0/0-5/0=8.00 (Revised on 13.04.23)	Works & Services	98.535
4397	Reconditioning of link road from N.H.Way Saeedabad road to village Zair Pir road via Burira Chowk road mile 0/0-5/0 = 6.40 Kms (with Asphalt) (Revised on 13.04.23)	Works & Services	104.407
4399	Reconditioning of different link roads of Taluka Matiari (4 Units) (Revised on 18.04.23)	Works & Services	174.319
4400	Reconstruction / Construction of different link roads of Taluka Matiari (2 Units) (Revised on 13.04.23)	Works & Services	197.546
4401	Reconditioning / Construction of road from National Highway to village Ghulam Muhammad Balal via Miranpur link to village Adil Balal and village Syed Azam Shah 0/0-7/4 (12.00 Kms) (Revised on 08.05.23)	Works & Services	173.664
4402	W/R road Missan Wadi to T.D.R Mirwah road via Qazi Noor Muhammad Leghari, Ghulam Ali Leghari, Saleh Faqeer Mir Jat i/c approach Bypass road Missan Nandhi mile 0/0-3/7 (6.34 Kms) (Revised on 13.04.23)	Works & Services	144.457
4403	Reconditioning of road Mashak Hoti Timore road i/c Lashari village mile 0/0-7-4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	148.391
4404	Reconditioning of road from Mall Khan Thebo to old Mirabad via Muhabbat Shah i/c link Soomar Khaskheli Mile 0/0 - 7/4 = 12.00 Kms (Revised on 13.04.23)	Works & Services	150.663
4405	Reconditioning of link road from Tando Adam - Mirpurkhas road to Yousuf Narejo via Murad Balouch Siddique Baloch, Piyaro Khaskheli, Saleh Khaskheli, Chacho Mall mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	148.954
4408	Reconditioning of link road from Haji Wali Muhammad Dars near Haji Karim Dars to Piyaro Lund road via Ali Khan Jarwar, Mevo Khaskheli, Khuda Bux Mari, Daim Khaskheli, Bashir Babar mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	148.969
4409	Reconditioning of link road from Tando Allahyar Mirwah road to Wangi Mori Saindad Deeshak road via Jarar Thebo, Hanif Leghari, i/c Juman Otho mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	150.302
4410	Reconditioning of link road from Mian Chamber road to Mira Khori Minor via Saeed Khan Laghari, Haji Muhammad Khan Lund to Dad Jarwar to Zahoor Minor Mureed Mori mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	151.603
4411	Reconditioning of link road from Chamber road Azizullah Memon Otaque to Sahib Khan Jarwar road via Kouro Daidano, Saleh Solangi, Obhriyo Dars, Mitho Khaskheli mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	147.526
4413	Reconditioning of Asphalt Concrete road from Hyderabad - Mirpurkhas road at point Rahuki Bus Stop to Hyderabad - Shaikh Bhirkio road via Bhindo Sharif & Reconditioning of Asphalt Concrete road from Mirpurkhas - Hyderabad road to village Wali Muhammad Khaskheli (6.30 Kms) (Revised on 13.04.23)	Works & Services	96.501
4414	Reconditioning of Asphalt Concrete road from Tando Fazal Chowk to village Bukho Leghari mile 0/0-3/6 (6.00 Kms), Taluka Rural Hyderabad (Revised on 13.04.23)	Works & Services	88.821
4416	W/R of road from Tando Muhammad Khan - Shaikh Bhirkio road @ point 1/0 mile via Baqar Nizamani (9.25 Kms) (Revised on 24.05.23)	Works & Services	226.520
4418	Reconditioning of road from Gharo Mori to Panjtana (6.20 Kms) (Revised on 13.04.23)	Works & Services	79.318
4420	Reconditioning of road from Sujawal road @ mile 23/3 to Bulla Khan Jat mile 0/0-3/6 (6.00 Kms) (Revised on 13.04.23)	Works & Services	88.378
4421	Improvement of road from Dumbalo to Kapri Mori mile 0/0-7/0 (11.263 Kms) (Revised on 14.04.23)	Works & Services	240.870

ADP	Name of Scheme	Sector	Estimated Cost
4423	Improvement of road from Matli Tando Ghulam Ali at mile 6/4 Shesh mile to Akram Wah mile 0/0-7/0 (11.26 Kms) (Revised on 06.04.23)	Works & Services	158.229
4424	Widening / Reconditioning of link road from Chach Jahan Khan - Mian Usman Quba road @ 5.00 Kms to village Haji Ali Muhammad Jat Warri - 0.00-7.30 Kms (Revised on 13.04.23)	Works & Services	201.908
4425	Reconditioning of link road from Chuhar Jamali Chahch Jahan Khan road village Ladyoon to Kothi 0.00 - 8.60 (8.60 Kms) (Revised on 13.04.23)	Works & Services	143.769
4426	Reconditioning of link road from Chachjahan Khan - Mian Usman Quba road @ 1.42 Km to village Jaffar Boohar via Moosa Pathan Mile 0/0 - 4/3 = (7.00 Kms) (Revised on 13.04.23)	Works & Services	96.736
4427	Rehabilitation of road from Amra Stop Sujawal Bathoro to village Shahnawaz Khan Leghari Km 0.00 - 7.00 (7.00 Kms) (Revised on 13.04.23)	Works & Services	99.047
4428	Improvement / Construction of road from Makli - Thatta Bypass road mile 3/1 (R/S) along Sim Drain to village Charan Memon road mile 0/0-7/4 (12.00 Kms) (Taken Up Length 0.00 - 8.60 Kms) (Revised on 13.04.23)	Works & Services	187.854
4429	Rehabilitation / Construction of road from Gharo-Sakro road mile 7/2 (Lait Stop) to Coastal Highway via village Mathino Rind and Moosa Khaskheli road mile 0/0-8/0 (12.00 Kms) (Taken Up Length 0.00 - 10.00 Kms) (Revised on 13.04.23)	Works & Services	164.338
4430	Improvement of road from DC Office Gopang Centre to Muslim Town road via Garibabad, Sikanderabad, Brohi Chowk, Khosa Chowk upto Indus Highway i/c various streets mile 0/0-7/0 (7.5 Kms), Taluka Kotri (Revised on 18.04.23)	Works & Services	153.841
4433	Rehabilitation of road Indus Highway (Old alignment - Sendoz road) Dual Carriageway mile 5/6-7/0, Taluka Kotri (Revised on 18.04.23)	Works & Services	126.654
4434	Improvement of road from Unerpur village to Zardari Mori via Chara via Budhapur Back to Zardari Mori i/c M/S mile 0/0-4/4 (7.24 Kms), Taluka Manjhand (Revised on 18.04.23)	Works & Services	75.795
4439	W/R of road from Indus Highway to Choukhandi via Ali Bux Junejo village Towards Boriri village, i/c Paver Block & Drain mile 0/0-3/0 (4.83 Kms) (Revised on 18.04.23)	Works & Services	137.490
4443	Widening & Reconditioning of road from Walwani Chodagi to Tharri Jado Shaheed via Phulji village (8.50 Kms) (Revised on 18.04.23)	Works & Services	172.443
4447	Reconditioning of road from Seri Pinyari Path road to Suleman Soomro road (7.64 Kms) (Revised on 08.05.23)	Works & Services	85.587
4448	W/R of road from Khipro to Umerkot via Ghulam Nabi Shah road mile 0/0-46/5=(75.00 km) with Asphalt Surface 18' - 24' width (P.S- 42 N.A=216) (Revised on 14.04.23)	Works & Services	4036.614
4451	Reconditioning of road from Tando Allahyar Tando Adam road to Piyaro Lund stop via Yar Muhammad Thebo, Wanhyal Thebo and Bachal Nagar mile 0/0-9/6 (15.70 Kms) (1 1/2 Thick Asphalt) (Revised on 22.05.23)	Works & Services	262.794
4457	W/R of road from Tando Allahyar to Mirwah road at Belaro Shakh Stop mile 0/0-20/4 (33.00 Kms) (18' to 24' with 2' Aspht Concrete) (Revised on 14.04.23)	Works & Services	1342.916
4462	W/R of road from Ali Bunder to Diplo road mile 0/0-36/2 (58.00 Kms) (Revised on 14.04.23)	Works & Services	3907.577
4564	W/R of link road from Shahdadpur - Gupchani road to village Din Muhammad Khoso Mile 0/0-2/4 (4.00 Kms) (12' to 18' width) (With 1-1/2' thick Asphalt Surface)	Works & Services	148.592
4592	Rehabilitation / Construction of roads in UC Doomani, UC Faqir Jo Goth, UC Bijara, UC Buhara (6.00 Kms)	Works & Services	128.217
4612	W/R of road from Bachal Shah CNG to Yousif Hajano via Dargah Hazrat Ahmed Shah Lakyari connecting National Highway @ Kameja Shakh (12.00 Kms) i/c approaches of villages (2' thick asphalt) (width 24ft)	Works & Services	398.781
4614	W/R of road from Thatta to Ghorabari via Pir Patho (41.00 Kms)	Works & Services	1660.510
4623	Improvement / Construction of road from Saddar Pull to Dhandari taken up length 13.5 Kms	Works & Services	272.020
4727	Reconditioning of road from Khando road Tando Adam to Village Ismail Raho Via Sacho Sand, Muhammad Bachal Raho & Sarang Keerio road 2.50 km (B) Reconditioning of road from Khando road Tando Adam to Village Bagho Lashari road 1.20 km.	Works & Services	70.000
4742	Reconditiioning / Construction of Link Road from Tando Allahyar Chamber road to Village Manik Lanjwani approach road to Muhammad Ali Rind, Natho Pitafi Mile 0/0-4/3 (7.0 KM)	Works & Services	100.000
4773	Rehabilitation of road from Indus Highway via Arazi Godam to Sijawal Burdi i/c Masonary structure mile 0/0-1/6 (2.80) Taluka Sehwan	Works & Services	56.000
4786	Improvement/Construction of Roads in Various Villages of UC- Mahar, including village of Meer Lashari, Gul Tandio to Anwar Rind, Badal Rind, Sattar Tandio to Ibrahim rind, Haji malik rind to village haji Jalal, Aurangzaib rind, Otho mori to ahmed Chanro, Lal khan lashari to mir lashari, Dil Murad rind to katho Manchari, Molvi Jaffar Barran, Umer Arain to Ali Muhammad Rind, Hafiz Hakim Rind to Pariyo Jatt, Muradani to Chuto Lal Dargah I/C other connecting village Links Taluka Ghorabari	Works & Services	300.000
4793	Imoroven of road from Gharo Keti Bunder @ 11.00 KMs lait Stop to Connect Ahmed Zangiani road Vi aAbdullah Shoro road 17.00 KMs.	Works & Services	300.000
4796	Improvement /Construction of road from Var Mehar Mitho Shaikh (Jam Jageer Mori) @ 10.0 Kms to Village Pathan Shoro via Village Nazeer choudry i/c Village Links KM 0.00 - 12.0=12.0 Kms	Works & Services	247.000
4817	Reconditioning of road from Dasori to Shah Dino Thebo i/c link Abdul Rehman Thebo, Allah Rakhio Pathan, Sobharo Thebo road mile 0/0-7/3 (9.00 Kms)	Works & Services	180.000
4823	Construction of Thano Ahmed Khan Karchat Center (Kherthar National Park) Thano Bulla Khan mile 0/0-45/0 = 45-0 (M) = 72.45 Kms.	Works & Services	408.830

ADP	Name of Scheme	Sector	Estimated Cost
4825	Construction / Reconditioning of road from Dhandhi to Khan pur via Thikratho i/c Bye-Pass (25.00 Kms) (Revised on 22.05.23)	Works & Services	680.230
4826	Construction of road Schemes of Kazi Ahmed at Daulatpur (17.00 Kms) (SDG # 9)	Works & Services	221.447
4828	Construction of road from Bandhari road to village Mogio via Moosa Khan Gabol, Hyder Gabol, (19.00 Kms)	Works & Services	198.234
4829	Construction of various roads in UCs of Taluka Naseerabad Kamber Warah & Miro Khan (5.00 Kms) (Phase-I)	Works & Services	808.704
4833	Construction of road from Usman Behan to Chotiaryoon mile 0/0-57/4 (92.57 Km) (Revised)	Works & Services	1327.799
4839	Construction of road from F.P Bund to Hairo Khan (15.29 Kms)	Works & Services	183.295
4840	Construction of road from Yaro Lund Soomar Mori road Chato Lund Bridge to village Shahbazabad via Fateh Ali Lund Qaim Lund Sobdar Lund Mohd Bux Lund Allah Ditto Lund Bachal Lund Ghulam Lund and Sheer Muhammad Lund (15.00 Kms)	Works & Services	181.163
4846	Construction / Improvement of various roads in District Sukkur (42.00 Kms)	Works & Services	1408.326
4863	Construction of road from @ village Muhammad Essa Hullio to village Karani mile 0/0-11/0 (17.70 Kms)(Revised on 24.05.23)	Works & Services	238.664
4867	Construction / Reconditioning of various roads in Taluka Nasirabad (8.50 Kms) (Revised on 08.05.23)	Works & Services	159.886
4869	Construction of road from Dost Ali Umaid Ali Gopang road to village Sarang Shah Qabristan, along Bank of Sim Nallah (5.0 Kms) (Revised on 08.05.23)	Works & Services	116.004
4871	Construction of road Widening 40ft and Reconditioning alongwith Drainage from both sides from Baiji Chowk NHA to Dua Chowk via Eid Gah Chowk and Shahi Bazar Pano Akil (0.60 Km) (Revised on 06.03.23)	Works & Services	282.926
4873	Construction of new road from Hindyari to village Aliabad via enroot villages Abbasabad, Usman Dasti, Mithal Dasti @ Hindyari Bachrah road (6.00 Kms) (Revised on 08.05.23)	Works & Services	103.651
4874	Construction of road from Jhanda Shakh / Jhango road to village Arbab Ali Wassan, UC Ali Muhammad Machi road mile 0/0-3/1 (5.00 Kms) (Revised on 08.05.23)	Works & Services	69.026
4876	Construction / Reconditioning of road from Mehran Highway @ Mungla Naako to connect Malhar mangrio, road via village Shaman Lashari & village Muhammad Bux Mojai (9.00 KM) (Revised on 08.05.23)	Works & Services	183.185
4877	Construction of road from Roshan Ali Mari along Faiz Ganj Wah upto Juman Khaskheli road (3.60 KM) (Revised on 08.05.23)	Works & Services	67.351
4880	(A) Construction of road from Haleem Bhangwar village Simnala road to connect Jheemal Minor via Tarighat More to connect Mir Qurban Ali Bhangwar road (B) Reconditioning of road from Nawabshah-Daur road @ 7/5 mile to Katchi Chowdagi to Sain Dad Zardari via Trimore road mile 0/0-3/6 (6.0 Kms) wide 18ft (C) Reconditioning of road from Mehran Highway road at mile 2/5 + 330 to village Mureed Khan Zardari via Zakir Hussain Zardari, Salim Zardari, Nazar Muhammad Zardari road mile 0/0-3/5+330 (5.90 Kms) (Revised on 14.04.23)	Works & Services	231.548
4881	Construction / Reconstruction of road from 60th Mile -3 Chak Suhallo road @ 18 Shak Stop to Bachi Kalhori via Khudadad brohi road along Sim Nala / Drain (0.0-7.0 kms)(Revised on 29.05.23)	Works & Services	123.944
4882	Construction / Reconstruction of road from 60th Mile, -3 chak suhallo road@ Tariq abad mour to connect sultan dahri mori road @ village Mahram Shah road mile 0/0-3/5 (5.80 kms). (Revised on 11.04.23)	Works & Services	107.259
4883	Construction of road from Darya Khan Kaloi road at mile 1/3 to village Hashim Kaloi via Abdullah Kaloi, village Ashiq Hussain Zardari, Alan Menjotho, village Naseer Manjthio, Pyaro Magsi to connect Nabi Dad Brohi road 0/0-2/5 (4.20 Kms) (Revised on 11.04.23)	Works & Services	74.877
4884	Construction / Reconditioning of road from Malwah Minor to Abdul Hameed Dahri, Muhammad Otho, Yar Muhammad Dahri, Qutibi & Sobho Dahri road (6.20 Kms) (with 3.80 cm Thick Carpet with Paver Machine) (Revised on 11.04.23)	Works & Services	106.412
4886	Reconditioning of road from Bandhi Moro road to village Abdul Rauf Dahri, Manahro, Chariro and Sawri, Kazi Ahmed road (0.00 - 9.80 Kms) (Actual Length 9.80 Kms).(Revised on 11.04.23)	Works & Services	154.299
4887	Construction / Reconditioning of Asphalt road Mirpurkhas District Mirpurkhas length 6000 Rft (Revised on 22.05.23)	Works & Services	298.300
4888	Construction of road from Mirpurkhas-Sindhri to Patoyoon road to link various villages Union Council Old Mirpur & Ahmed Bux Narejo (Length - 8.30 Kms) (Revised on 08.05.23)	Works & Services	137.100
4889	Construction of road from Mirpurkhas - Khan Patoyoon road to connect various villages (Length -8.30 Kms) (Revised on 08.05.23)	Works & Services	139.964
4890	Construction of road from Mirpurkhas - Tando Adam road to connect various villages (Length - 8.70 Kms) (Revised on 08.05.23)	Works & Services	167.219
4891	Construction of road from Araro Bhurgari to Punhoon Khaskhally via Asif Brohi (5.63 Kms) (Revised on 11.04.23)	Works & Services	174.014
4892	Construction of road from Mureed Khaskhally to Sonharo Dal via Hassan Shah Baghban (4.00 km) (Revised on 11.04.23)	Works & Services	81.254
4893	Construction of road from Hadakar Kunbhar Bhada to Jarkhari via Okraro (4.00 km) (Revised on 11.04.23)	Works & Services	128.350
4894	Construction & Reconditioning of different link roads of U.C K.K Nizamani Taluka Hala (3 Units) (Revised on 13.04.23)	Works & Services	123.842

ADP	Name of Scheme	Sector	Estimated Cost
4895	Construction & Reconditioning of different link roads of Taluka Matiari (3 Units) (Revised on 13.04.23)	Works & Services	125.507
4896	Construction & Reconditioning of Different link roads of Taluka Saeedabad (5 Units) (Revised on 18.04.23)	Works & Services	103.086
4897	Construction & Reconditioning of different link roads of Taluka Saeedabad (7 Units) (Revised on 18.04.23)	Works & Services	169.393
4898	Construction & Reconditioning of different link roads of Taluka Hala (4 Units) (Revised on 13.04.23)	Works & Services	170.938
4900	Construction / Reconditioning of link road from Tando Allahyar Tando Adam road to village Ibrahim Aqlani via village Bahar Mirajat, village Doulat Mirjat Deputy Abdul Haque village Kolhi Kot Aslam Nizamani village Sando Mirjat village Ahmed Mirjat road Mile 0/0 - 7/4 = 12.00 Kms (Revised on 13.04.23)	Works & Services	157.245
4901	Construction / Reconditioning from Bukera road to Bheel Colony Sufaida Colony, Sameja Street Akram Colony, Nagori Plot to Bye pass Bukera road via Soomra Colony, and Chamber road and Hyderabad road, Islamabad Colony and Madina Colony, Malak Street mile 0/0 - 5/4 (8.84 Kms) (with 1-1/2' Thick Carpet i/c Drain Nala, Paver Block) (Revised on 13.04.23)	Works & Services	127.203
4904	Reconditioning / Widening of road from Jarri Mori to Dando to village Nazar Khoso via Haji Khan Stop (7.10 Kms) (Revised on 13.04.23)	Works & Services	159.078
4905	Reconditioning / Widening of road from Digh Mori Soomerki Shakh to village Jan Muhammad Wassan to Peeru Wassan to village Bashir Brohi via Nawab Pakko (6.00 Kms) (Revised on 13.04.23)	Works & Services	127.186
4907	Construction / Reconditioning of road from Jahan Khan Mori to Haji Yaqoob Khaskheli via Dargah Lal Mehmoodani road mile 0/0-5/0 (8.00 Kms) (Revised on 13.04.23)	Works & Services	119.671
4909	Construction / Reconditioning of road from Kario Ghanwar road to village Haji Bachal Leghari alongwith Jarki Shakh mile 0/0-7/4 (12.00 Kms) (Revised on 13.04.23)	Works & Services	181.722
4914	Reconditioning / Construction of Various road of Taluka Shah Bander (5.90 Kms) (Revised on 13.04.23)	Works & Services	100.924
4915	Construction / Reconditioning of various village roads of District Sujawal (5.10 Kms) (Revised on 13.04.23)	Works & Services	100.195
4916	Construction of road from Allah Dino Mandhro road @ 11.60 Kms to Baharo Zangejo village 0.00-5.00 Kms (Revised on 13.04.23)	Works & Services	96.090
4917	Construction of Link road from Chachjahan Khan Mian Usman Quaba road @ 1.87 KM to Qadria Minor via village Gul Muhammad Jat and Malook Kalmati 0.00 - 6.00 Kms (Revised on 13.04.23)	Works & Services	97.524
4918	Reconditioning / Construction of Various village road village Abdul Khaliq Leghari, village Allah Dino Soomro and village Muhammad Khan Dibh of Taluka Sujawal 0.00-6.00 Kms (Revised on 13.04.23)	Works & Services	96.200
4919	Construction / Rehabilitation of various roads of UC-19, UC-20 & UC 22, Taluka Mirpur Sakro, District Thatta (12.80 Kms) (Revised on 13.04.23)	Works & Services	178.473
4921	Construction / Rehabilitation of various roads of UC-11, UC-12, Taluka Thatta, District Thatta (Revised on 13.04.23)	Works & Services	126.759
4922	Construction of road from Guru Balpuri Toung road Mile 3/2 village Allah Bux Lalani to village Chibhar Nout Deh Bhal (6.00 Kms) (Revised on 18.04.23)	Works & Services	118.864
4931	Reconditioning / Re-Build Mehran Highway from 89 Landhi Karachi to Port Qasim road Karachi (0.00-12.00 Kms) District Malir (Revised on 22.05.23)	Works & Services	1761.905
4936	Construction / Reconditioning of road from Ghora Bari road to village Natho Kelai, village Jumo Kamwani, village Nasir Shaikh, village Abdul Rehman Panhwar, village Hashim Panhwar, village Mureed Parehri, village Alyas Panhwar, village Molvi Natho Panhwar KM-0.00-9.50 = 9.50 Kms	Works & Services	229.459
4942	Construction of road from Jhagal Malik to village Baloch Khan Chang (3.00 Kms)	Works & Services	44.513
4943	Construction of road from Shaheed Hassan Chowranghi Kashmore road to village Din Muhammad Mazari UC-Pacca Chandia (1.50 Kms)	Works & Services	20.242
4944	Construction of road from Agra City Bypass road	Works & Services	64.295
5077	Construction of schemes proposed by MPAs of District Dadu & Jamshoro (MPA Program) (General On-Going) (2019-20)	Works & Services	130.065
5179	Construction of Road from 8 mile Mori, Sinjhor road to Goth ch. Muhammad Naseem	Works & Services	108.900
5247	Construction of Chief Engineer Building Office / Residence Sukkur (Revised on 13.03.23)	Works & Services	84.209



ASSET
DISTRIBUTION
CEREMONY
January 2024



Annexure (E)

MEC Offices & Team Members

SECRETARIAT HEAD OFFICE	
Nisar Ahmed Memon	Director General (MEC)
Gulan Khan Khaskheli	Director (Admin & Accounts)
Ghulam Hussain Bughio	Director (Monitoring)
Mr. Naveed Saleh Memon	Sr. System Analyst
Hafeez-ur-Rehman Janwari	Deputy Director (Admin & HR)
M. Javed Khan	Assistant Director
Sallah Saleh Thebo	Admin & Accounts Officer
Illahi Bux Chand	Private Secretary
Noor Muhammad	Superintendent
Abdul Rauf Shaikh	Assistant
Nabi Bux	Assistant
Ali Muhammad Jogi	Assistant
Syed Muhammad Fazal	Sr. Clerk
Habib-ur-Rehman	Key Punch Officer

MIS DIRECTORATE	
Sarfaraz Ahmed Khan	Director (MIS)
Mohsin Ali Awan	Assistant Director (Coord)
Tufail Ahmed Shaikh	Assistant Director (Content Management)
Ashraf Baloch	Sr. Programmer
Bilal Bin Ismail	Programmer (OS)
Teerath Kumar	Network Admin
Avinash Sharma	System Support Engineer
Muhammad Faaz	Hardware Technician
Junaid Ahmed Shaikh	Data Processing Officer
Muhammad Panjal	Data Processing Officer
Suhail Ahmed Memon	Data Processing Officer

SECTOR MONITORING & PROCUREMENT OFFICE KARACHI

Mr. Fateh uddin Junejo	Sector Monitoring & Evaluation Officer (SMEO)- Infrastructure
Dr. Javed Khawaja	Sector Monitoring & Evaluation Officer (SMEO)- Social Sector
Mr. Saeed Ahmed Nizamani	Procurement Specialist
Mr. Shuja Ahmed Lanjar	Programmer
Mr. Muhammad Faisal Tunio	Data Processing Supervisor
Mr. Arif Raza	Key Punch Operator
Muhammad Saleh Lund	Steno-Typist

REGIONAL MONITORING OFFICE KARACHI

Mr. Aurangzeb Vistro	Regional Monitoring Evaluation Officer (RMEO)- Karachi
Mr. Muhammad Salman Shaikh	Monitoring & Evaluation Officer (MEO)
Mr. Ghulamullah Mahar	Monitoring & Evaluation Officer (MEO)
Mr. Imran Khan Memon	Monitoring & Evaluation Officer (MEO)
Mr. Ahmed Hussain Mahar	Monitoring & Evaluation Officer (MEO)
Ms. Rabia Muhammad Ali	Monitoring & Evaluation Officer (MEO)
Mr. Shafique Ahmed Samtio	Sub Engineer
Mr. Hizbullah Dars	Data Processing Officer
Mr. Muhammad Moosa	Steno Typist

REGIONAL MONITORING OFFICE LARKANA

Aziz-ur-Rehman	Regional Monitoring & Evaluation Officer (RMEO)
Kashif Anwar	MEO (Water Supply & Drainage)
Rasheed Ahmed Jumani	MEO (Agriculture)
Shah Faisal	MEO (Live Stock & Fisheries)
Shams Uddin Mahesar	MEO (Live Stock & Fisheries)
Umair Aslam	MEO (Roads)
Ghulam Murtaza Khan	System Support Engineer
Waseem Ahmed Soomro	Data Processing Officer
Mohsin Ali Khokhar	Office Assistant
Khalid Hussain	I.T Assistant

REGIONAL MONITORING OFFICE HYDERABAD

Mr. Tufail Ahmed Abro	Sector Monitoring & Evaluation Officer (SMEO)
Mr. Muhammad Azeem Jarwar	Regional Monitoring Officer
Mr. Syed Shafqat Shah	MEO (Health)
Mr. Jahanzeb Mallah	MEO (Education)
Mr. Abdul Qayoom Palijo	MEO (Water & Drainage)
Mr. Bilal Ahmed	MEO (Education)

REGIONAL MONITORING OFFICE SUKKUR

Shahzeb Ahmed Shaikh	Regional Monitoring Evaluation Officer (RMEO)
Muhammad Naeem Korejo	MEO (Agriculture)
Muhammad Aamir Arain	MEO (Health)
Dr. Shazia Mahar	MEO (Livestock & Fisheries)
Mr. Rameez Bajkani	MEO (Road)
Mohsan Ali Memon	MEO (Social Sector)
Muhammad Hanif Abro	MEO (Buildings)
Muhammad Hanif Hingoro	MEO (Education)
Jahangir Khan Chandio	MEO (Livestock & Fisheries)
Nisar Ahmed Khatii	MEO (Irrigation)
Ameet Kumar	Data Processing Officer

Annexure (F)

MEC Team Members Pictures



Director (Admin and Accounts) Office Karachi



Director (Monitoring) Office Karachi



SMEO Infra Office



SMEO Social Office



Procurement & System Analyst Office Karachi



MIS Directorate Office Karachi



Regional Office Karachi



Regional Office Larkana



Regional Office Sukkur



Regional Office Hyderabad

DIRECTOR GENERAL (MEC)

**3rd Floor, Tughlaq House, Sindh Secretariate
Saddar, Karachi**



www.mecsindh.gov.pk

MIS DIRECTORATE

9th Floor, Vital Foak Tower, Shahrah-e-Faisal, Karachi

KARACHI REGIONAL OFFICE

**Barrack# 92, Sindh Secretariate,
Opposite Sindh Assembly
+92 21 99204634**

HYDERABAD REGIONAL OFFICE

**Block-F, Adj. DG Agriculture Ext. Office,
Shahbaz Building, Thandi Sarak, Hyd.
+92 22 9201337**

SUKKUR REGIONAL OFFICE

**Bungalow#: A-128, Sindhi,
Society, Sukkur
+92 71 9310737**

LARKANA REGIONAL OFFICE

**Bunglow #: 20, Street #3,
Shahbaz Colony, Larkana
+92 74 4752101**
